

Contractor's Proposed Schedule -
As of February 2023:
6/1/23 - 7/31/23

CTH JJ tentatively scheduled to remain
open until June 2023

| | | | | | |
|------------------------|-------------|-------------------|---|-------|---|
| PROJECT NO: 1146-75-72 | HWY: STH 15 | COUNTY: OUTAGAMIE | TRAFFIC CONTROL - STAGE 2A DETAIL - OLD STH 15 EAST | SHEET | E |
|------------------------|-------------|-------------------|---|-------|---|

6/1/23 - 7/31/23

CTH JJ tentatively scheduled to remain open until June 2023

FOR ADVANCED SIGNS SEE SDD
- "TRAFFIC CONTROL, ADVANCE
WARNING SIGNS 45 M.P.H. OR
GREATER, TWO WAY UNDIVIDED
ROAD OPEN TO TRAFFIC"

FOR SHOULDER CLOSER SEE
SDD "TRAFFIC CONTROL, —
LANE SHIFT, MULTI-LANE
DIVIDED OR ONE-WAY ROAD"

FOR SHOULDER CLOSER SEE
— SDD "TRAFFIC CONTROL,
LANE SHIFT, MULTI-LANE
DIVIDED OR ONE-WAY ROAD"

FOR ADVANCED SIGNS SEE SDD
— "TRAFFIC CONTROL, ADVANCE
WARNING SIGNS 45 M.P.H. OR
GREATER, TWO WAY UNDIVIDED
ROAD OPEN TO TRAFFIC"

FOR SHOULDER CLOSER SEE SDD
"TRAFFIC CONTROL, LANE SHIFT,
MULTI-LANE DIVIDED OR ONE-WAY ROAD"

FOR ADVANCED SIGNING SEE SDD
"TRAFFIC CONTROL, LANE SHIFT, MULTI-LANE
DIVIDED OR ONE-WAY ROAD.

T

WISDOT/CADDS SHEET 42

Contractor's Proposed Schedule -
As of February 2023:


4/10/23 - 7/31/23

SPEED
LIMIT
45
R2-1
24" x 30"




700'

MATCH LINE STA 500'EB+00

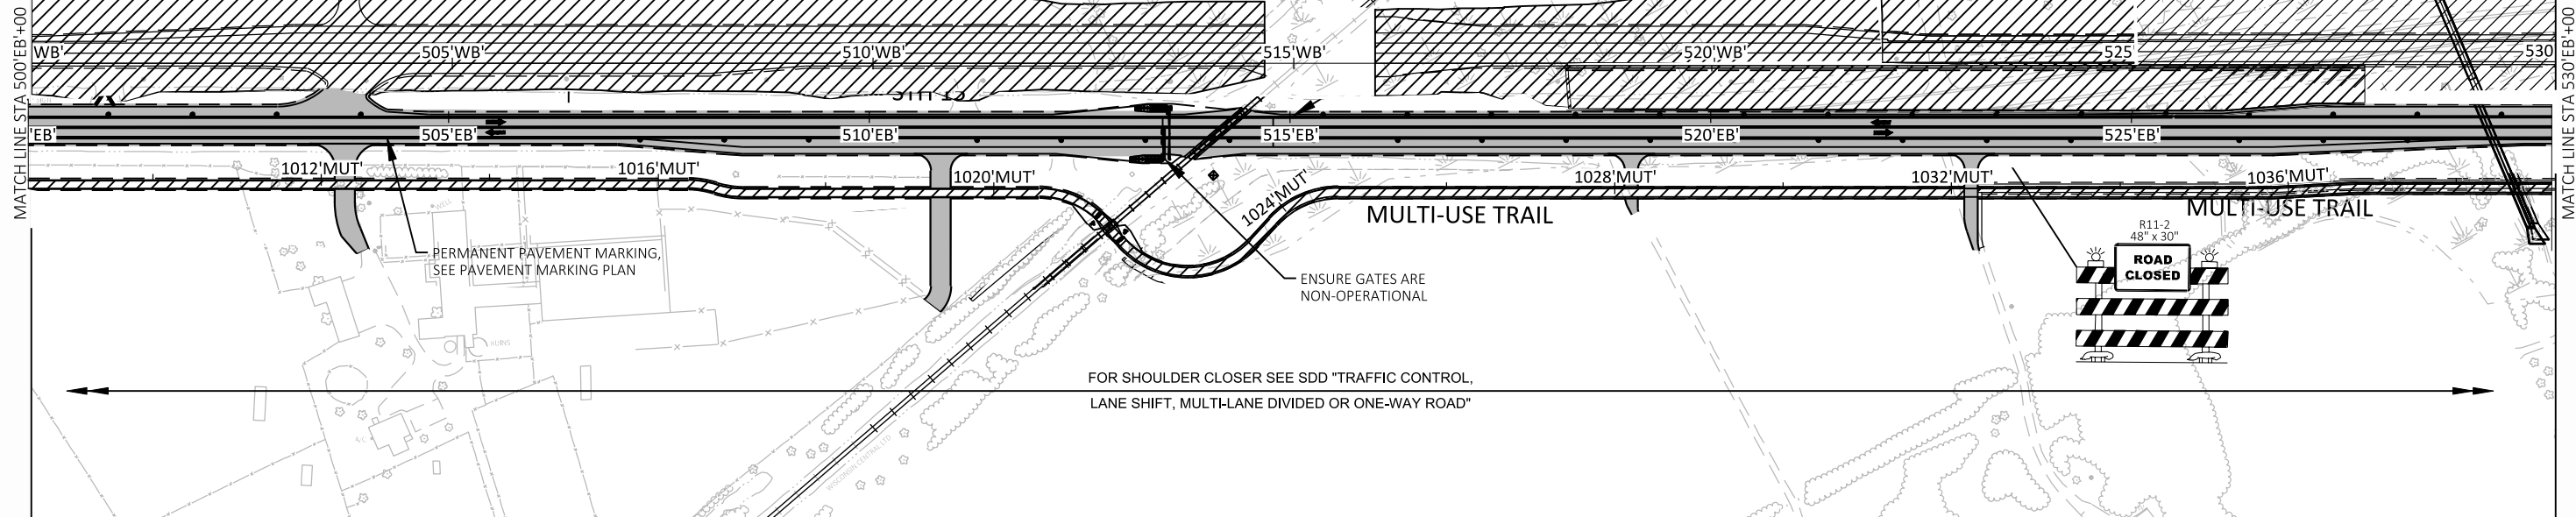

MATCH LINE STA 530'EB+00

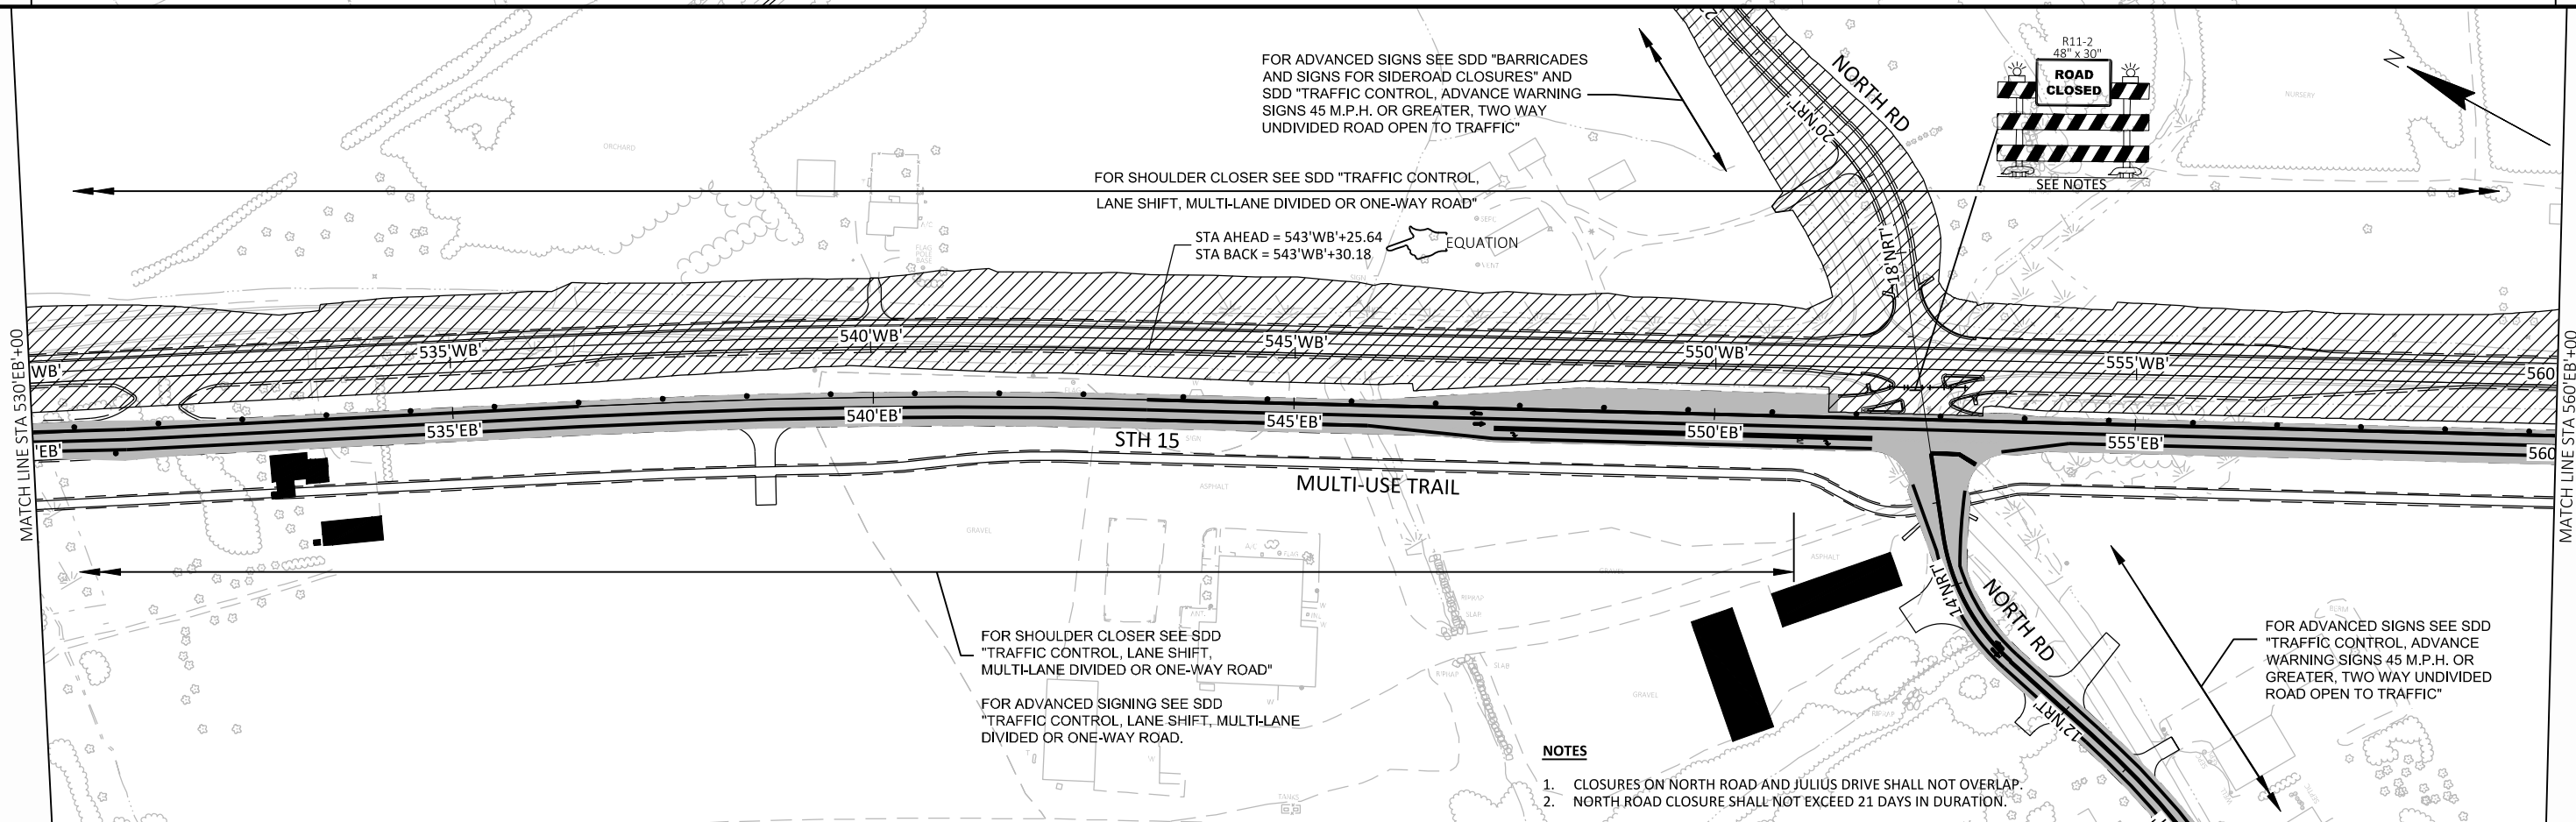

MATCH LINE STA 560'EB+00

PROJECT NO: 1146-75-72


HWY: STH 15


COUNTY: OUTAGAMIE

TRAFFIC CONTROL - STAGE 2A DETAIL - STH 15

SHEET

E

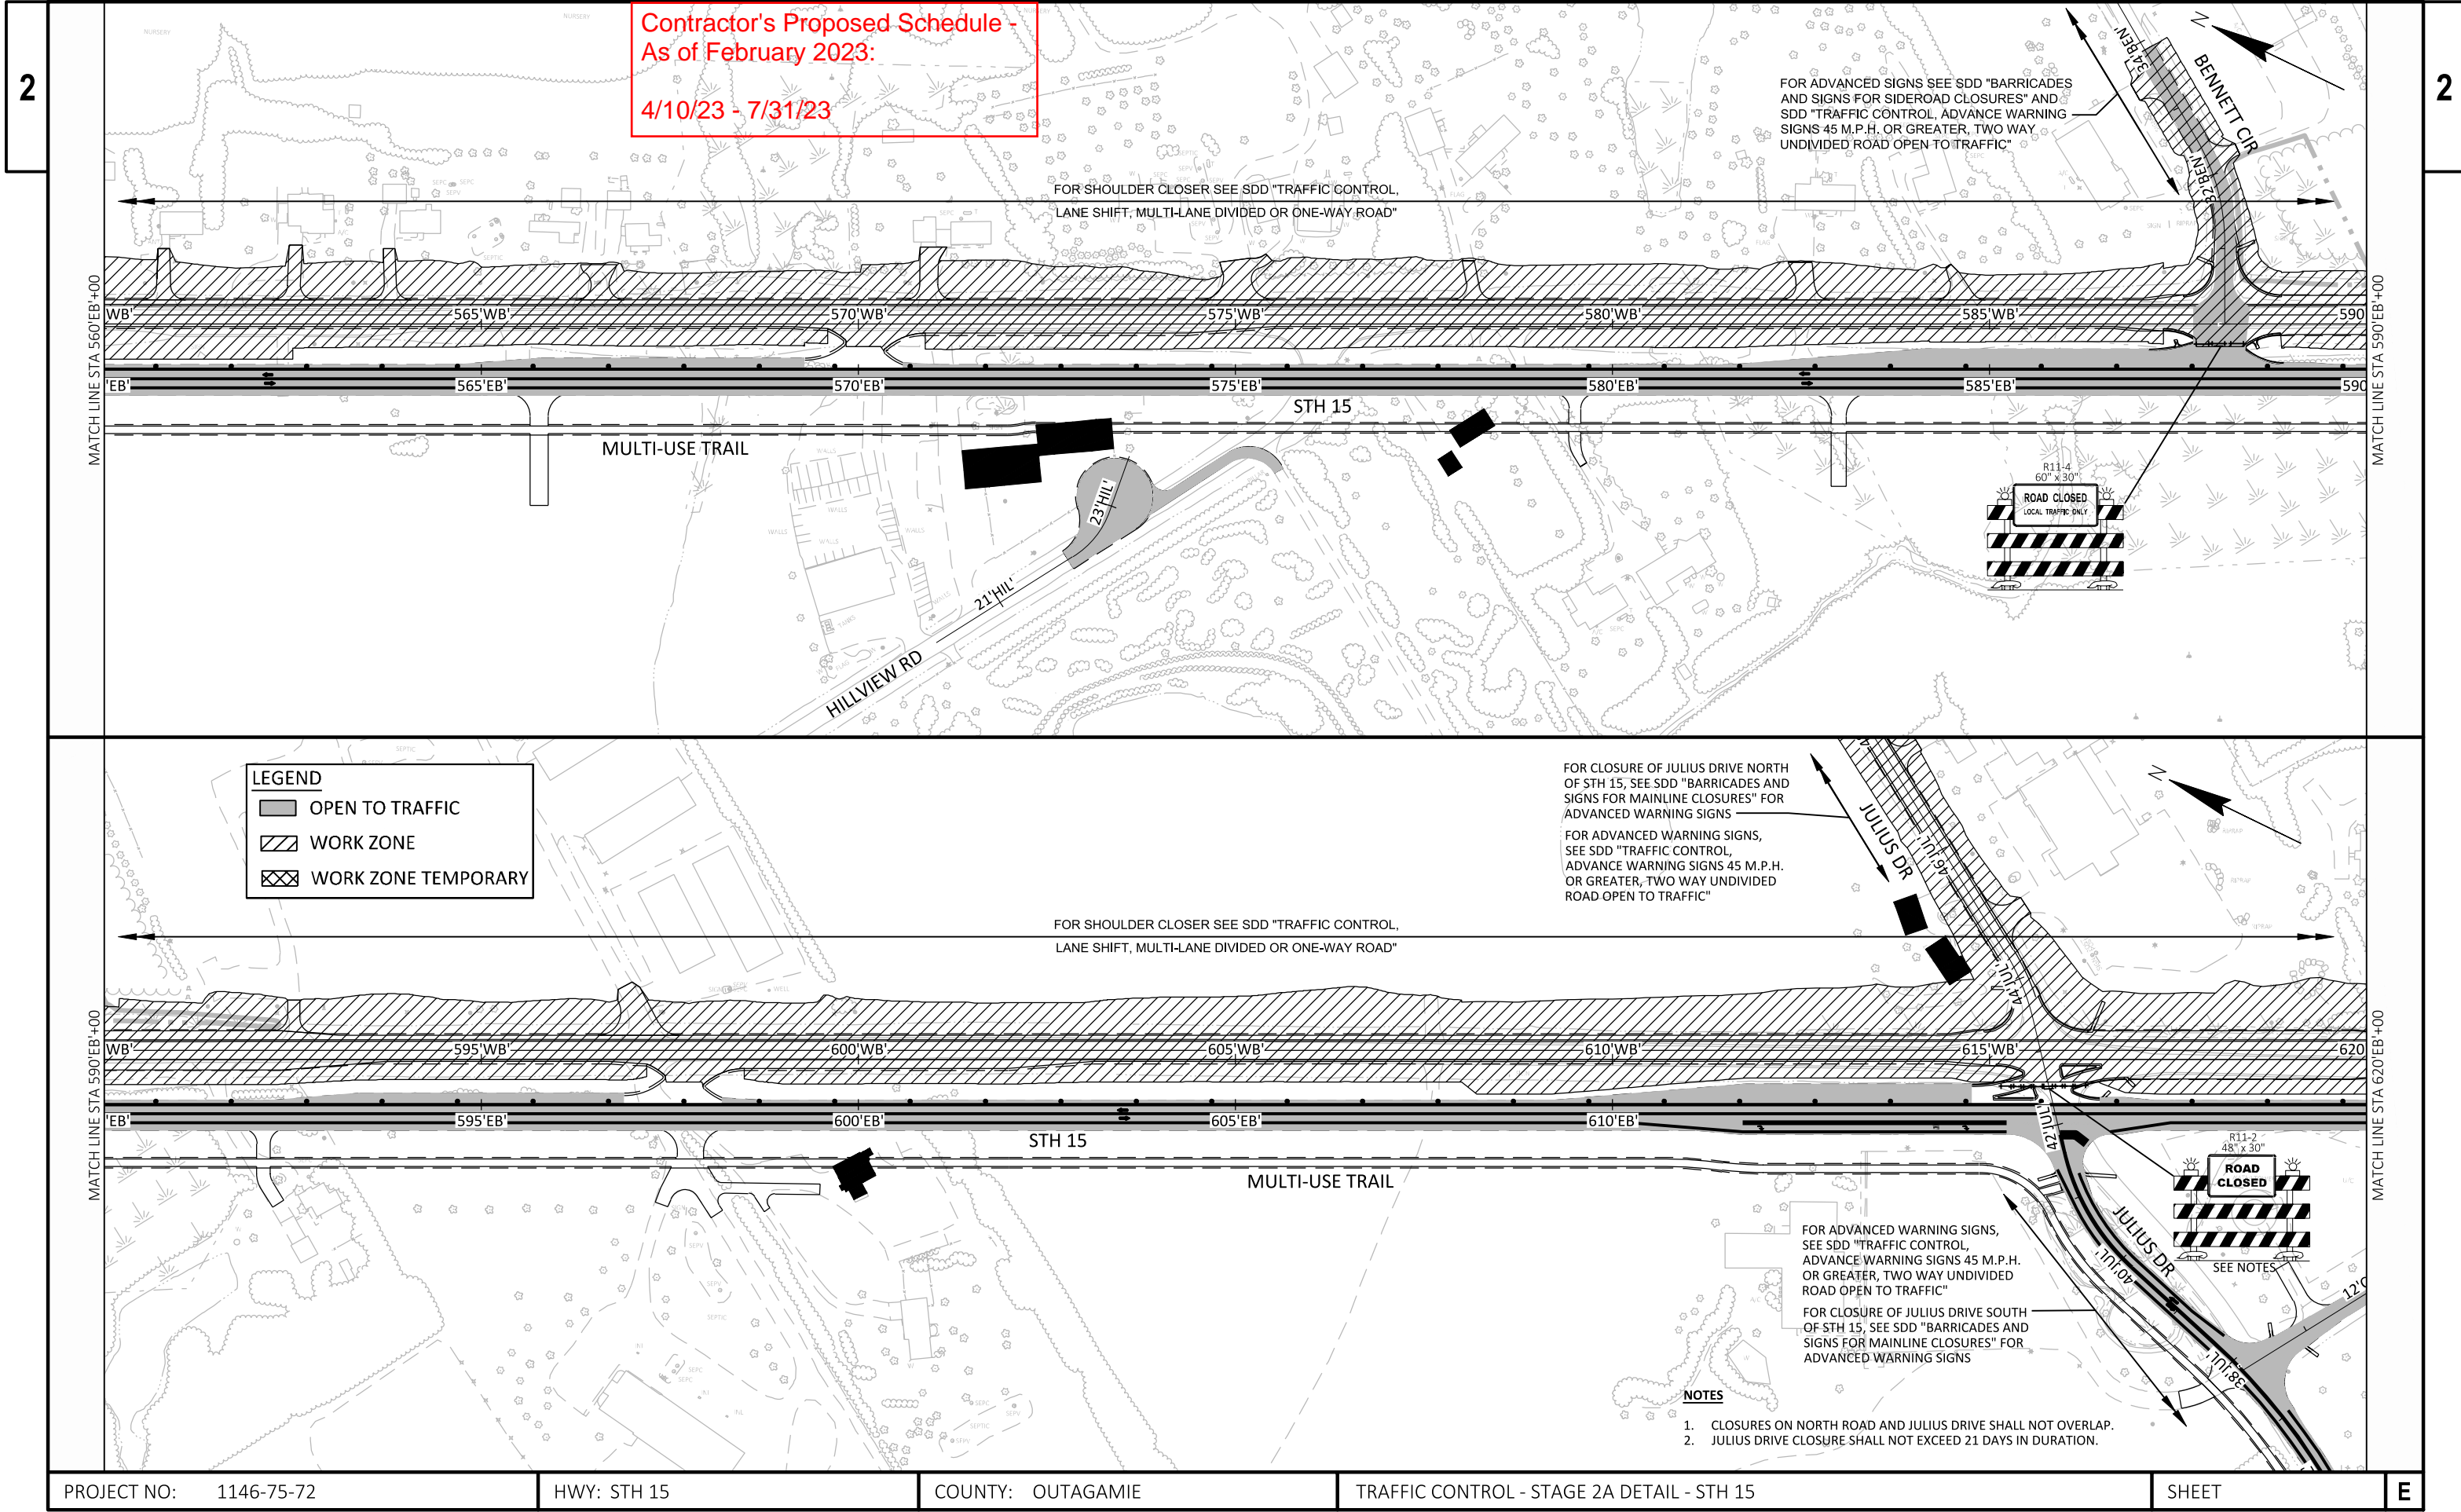

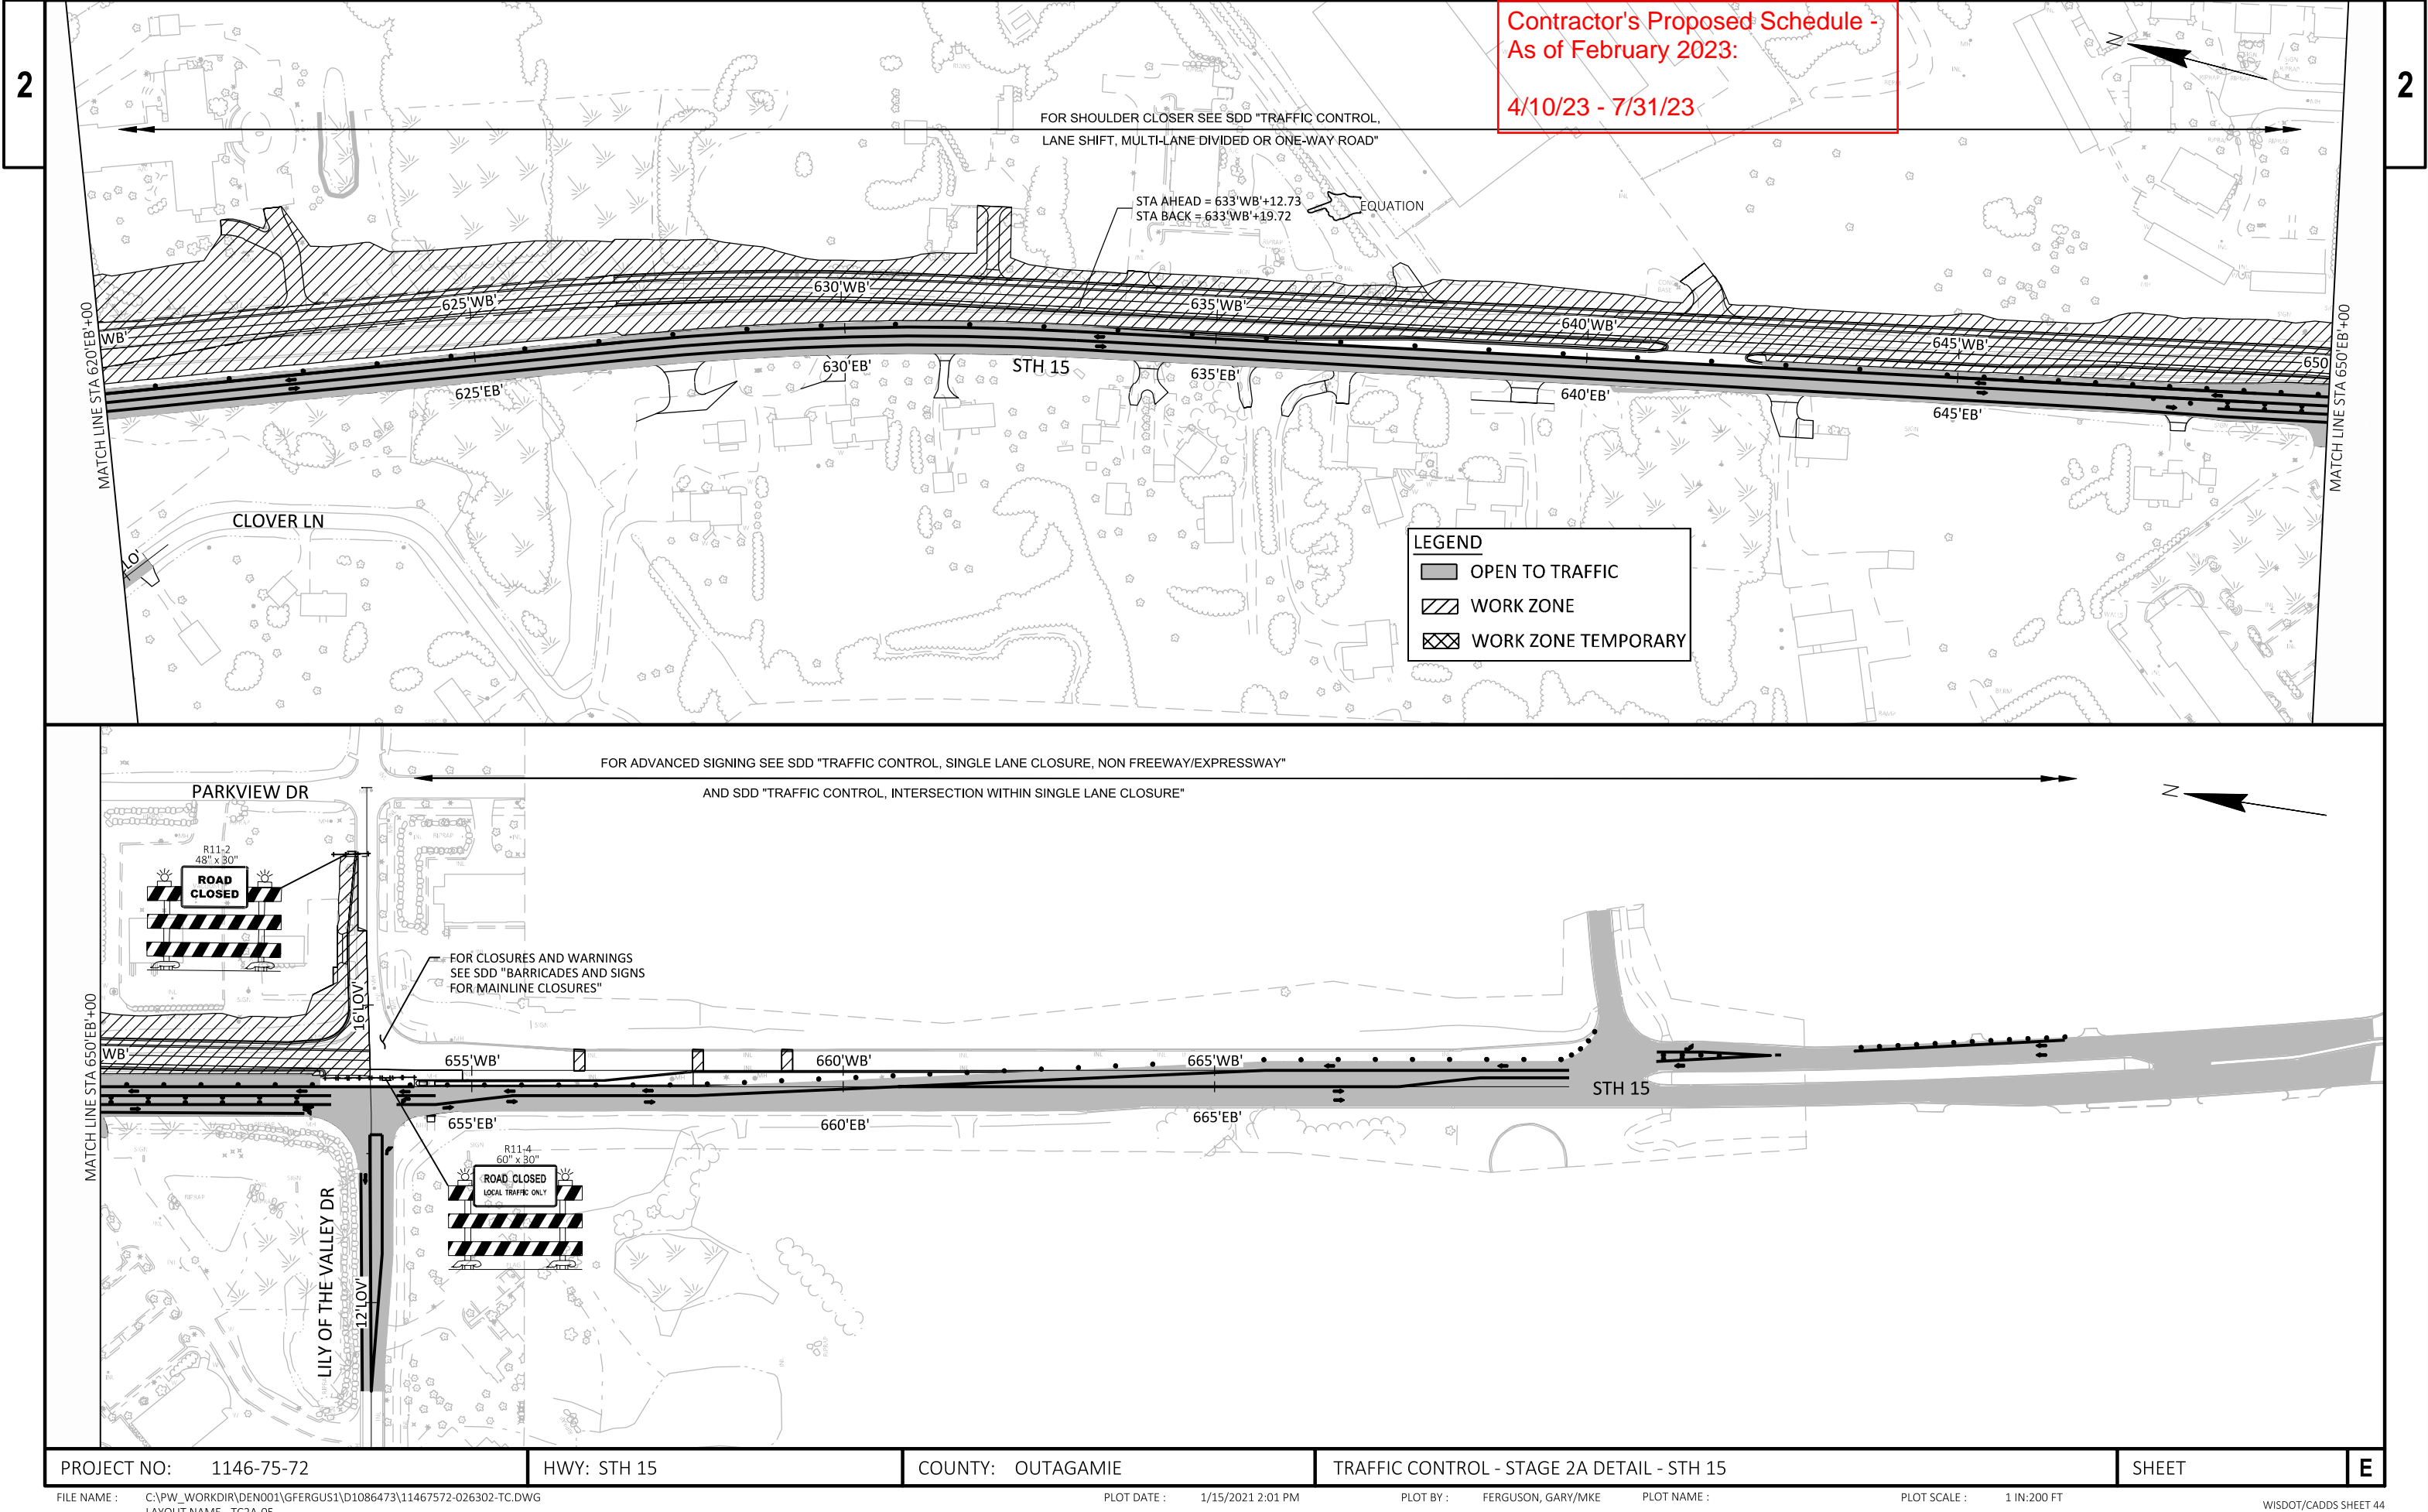

2

STAGE 2C

MAINTENANCE OF TRAFFIC:
STH 15 AND LOCAL ROADS OPEN TO TRAFFIC.

CONSTRUCTION ACTIVITIES TO BE COMPLETED:
CONSTRUCT OVERLAY ON CTH JJ.
CONSTRUCT CUL-DE-SAC ON MANLEY ROAD (NORTH).
CONSTRUCT MULTI-USE PATH FROM GREENDALE ROAD TO MANLEY ROAD.
RECONSTRUCT THE MEDIAN ISLAND EAST OF LILY OF THE VALLEY DRIVE.

MAINTENANCE OF TRAFFIC:
STH 15 AND LOCAL ROADS OPEN TO TRAFFIC.



CONSTRUCTION ACTIVITIES TO BE COMPLETED:
 CONSTRUCT OVERLAY ON CTH JJ.
 CONSTRUCT CUL-DE-SAC ON MANLEY ROAD (NORTH).
 CONSTRUCT MULTI-USE PATH FROM GREENDALE ROAD TO MANLEY ROAD.
 RECONSTRUCT THE MEDIAN ISLAND EAST OF LILY OF THE VALLEY DRIVE.

Contractor's Proposed Schedule -
As of February 2023:

8/15/23 - 10/26/23

8/15/23 - 10/26/23

2

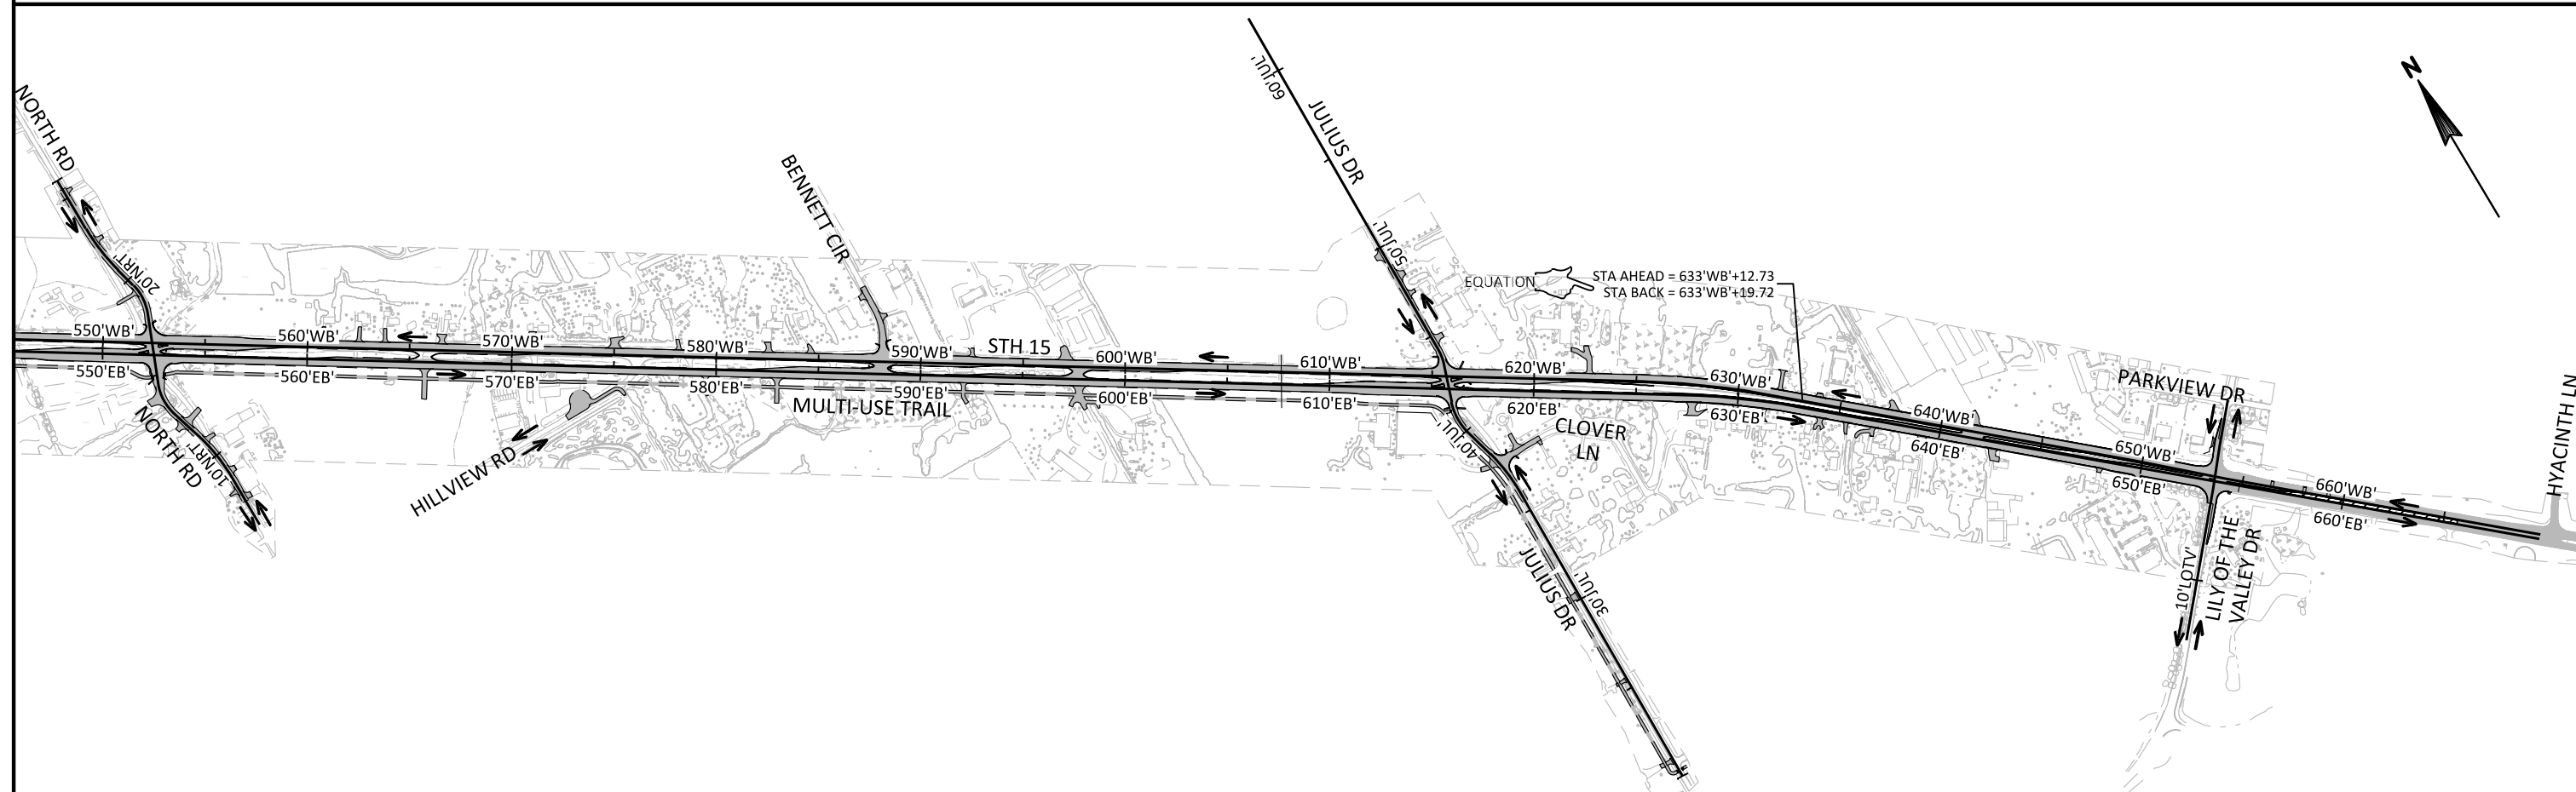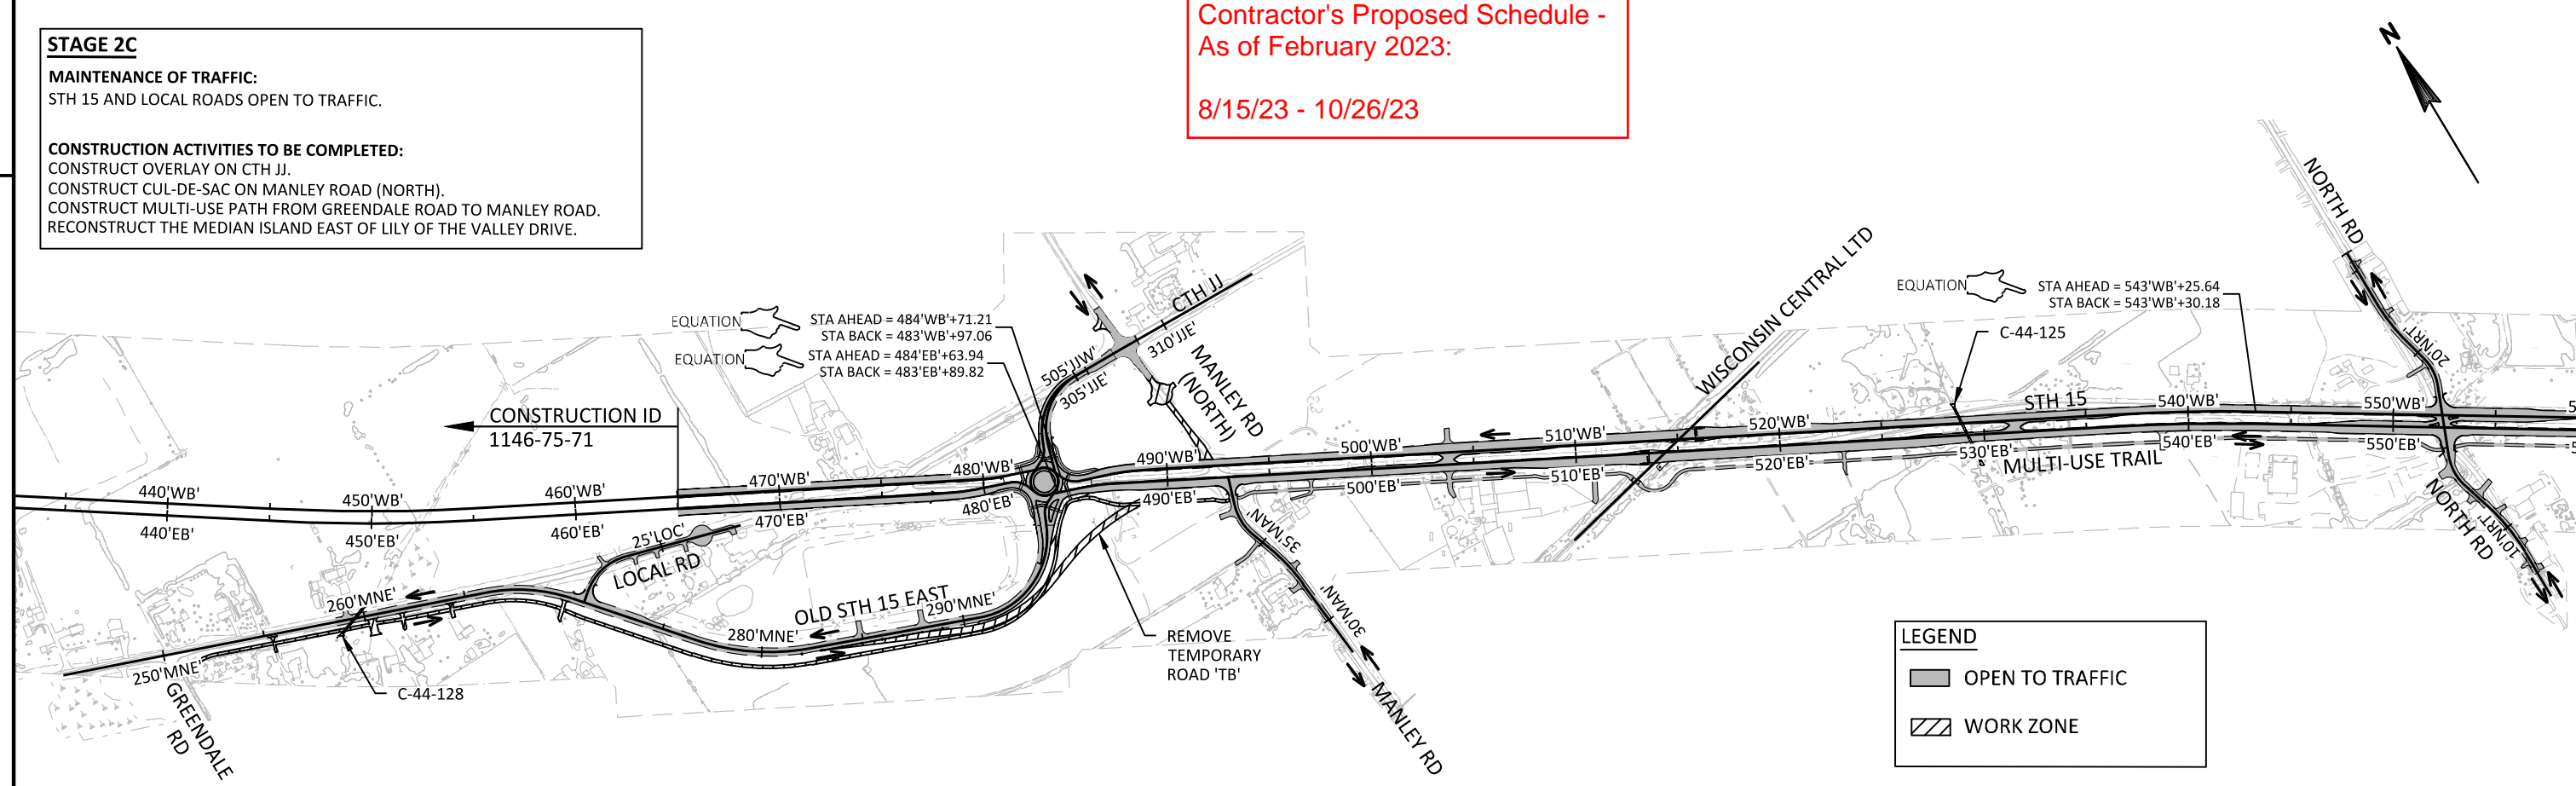

PROJECT NO: 1146-75-72

HWY: STH 15

COUNTY: OUTAGAMIE

TRAFFIC CONTROL - STAGE 2B OVERVIEW

SHEET

E

FILE NAME : C:\PW_WORKDIR\DEN001\JEG_BUGARIJA\D1086473\11467572-026501A-TC.DWG
LAYOUT NAME - TC 2C OVERVIEW


PLOT DATE : 2/5/2020 1:20 PM PLOT BY : BUGARIN, JOSE

PLOT BY : BUGARIN, JOSE PLOT NAME :

PLOT NAME : PLOT SCALE :

PLOT SCALE: #####

WISDOT/CADDS SHEET 44

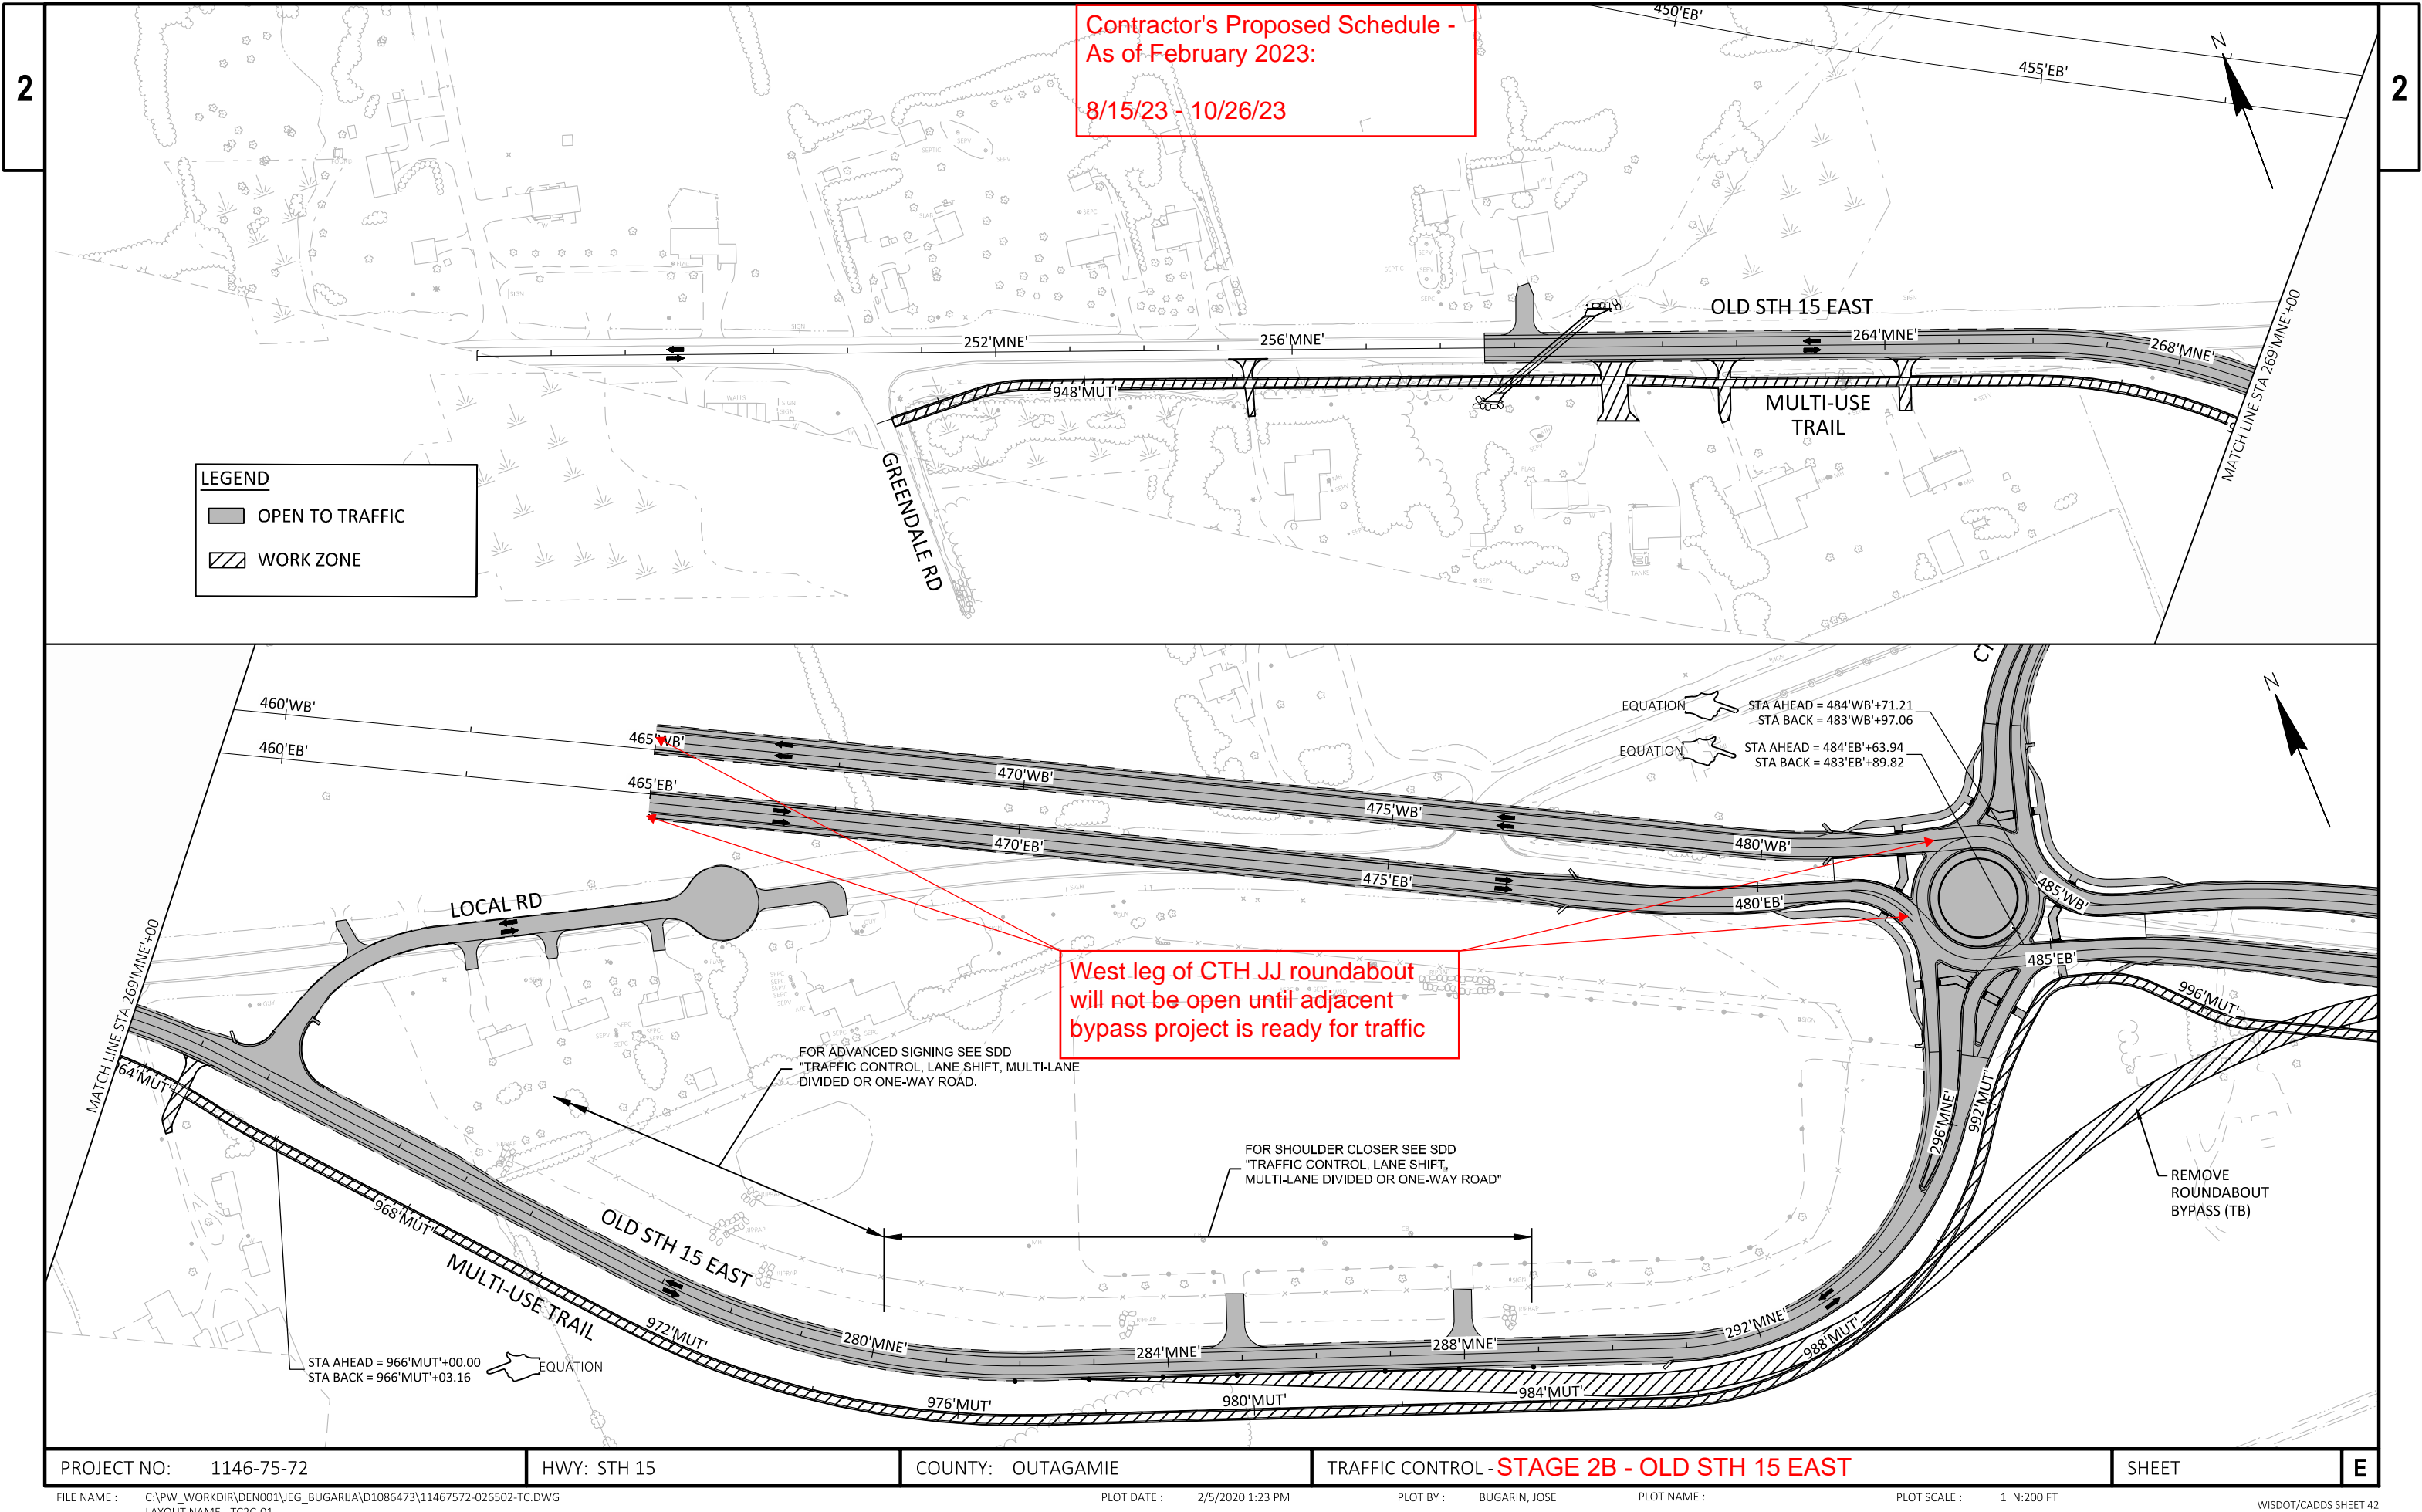

Stage 2B will include various median and outside lane closures to complete remaining median work at North Rd, Bennett Ct, and Julius and work along the MUT.

Contractor's Proposed Schedule -
As of February 2023:


8/15/23 - 10/26/23

FOR ADVANCED SIGNS SEE SDD
"TRAFFIC CONTROL, ADVANCE
WARNING SIGNS 45 M.P.H. OR
GREATER, TWO WAY UNDIVIDED
ROAD OPEN TO TRAFFIC"

EQUATION
STA AHEAD = 484'WB'+71.21
STA BACK = 483'WB'+97.06
EQUATION
STA AHEAD = 484'EB'+63.94
STA BACK = 483'EB'+89.82

West leg of CTH JJ roundabout
will not be open until adjacent
bypass project is ready for traffic

REMOVE
ROUNDABOUT
BYPASS (TB)

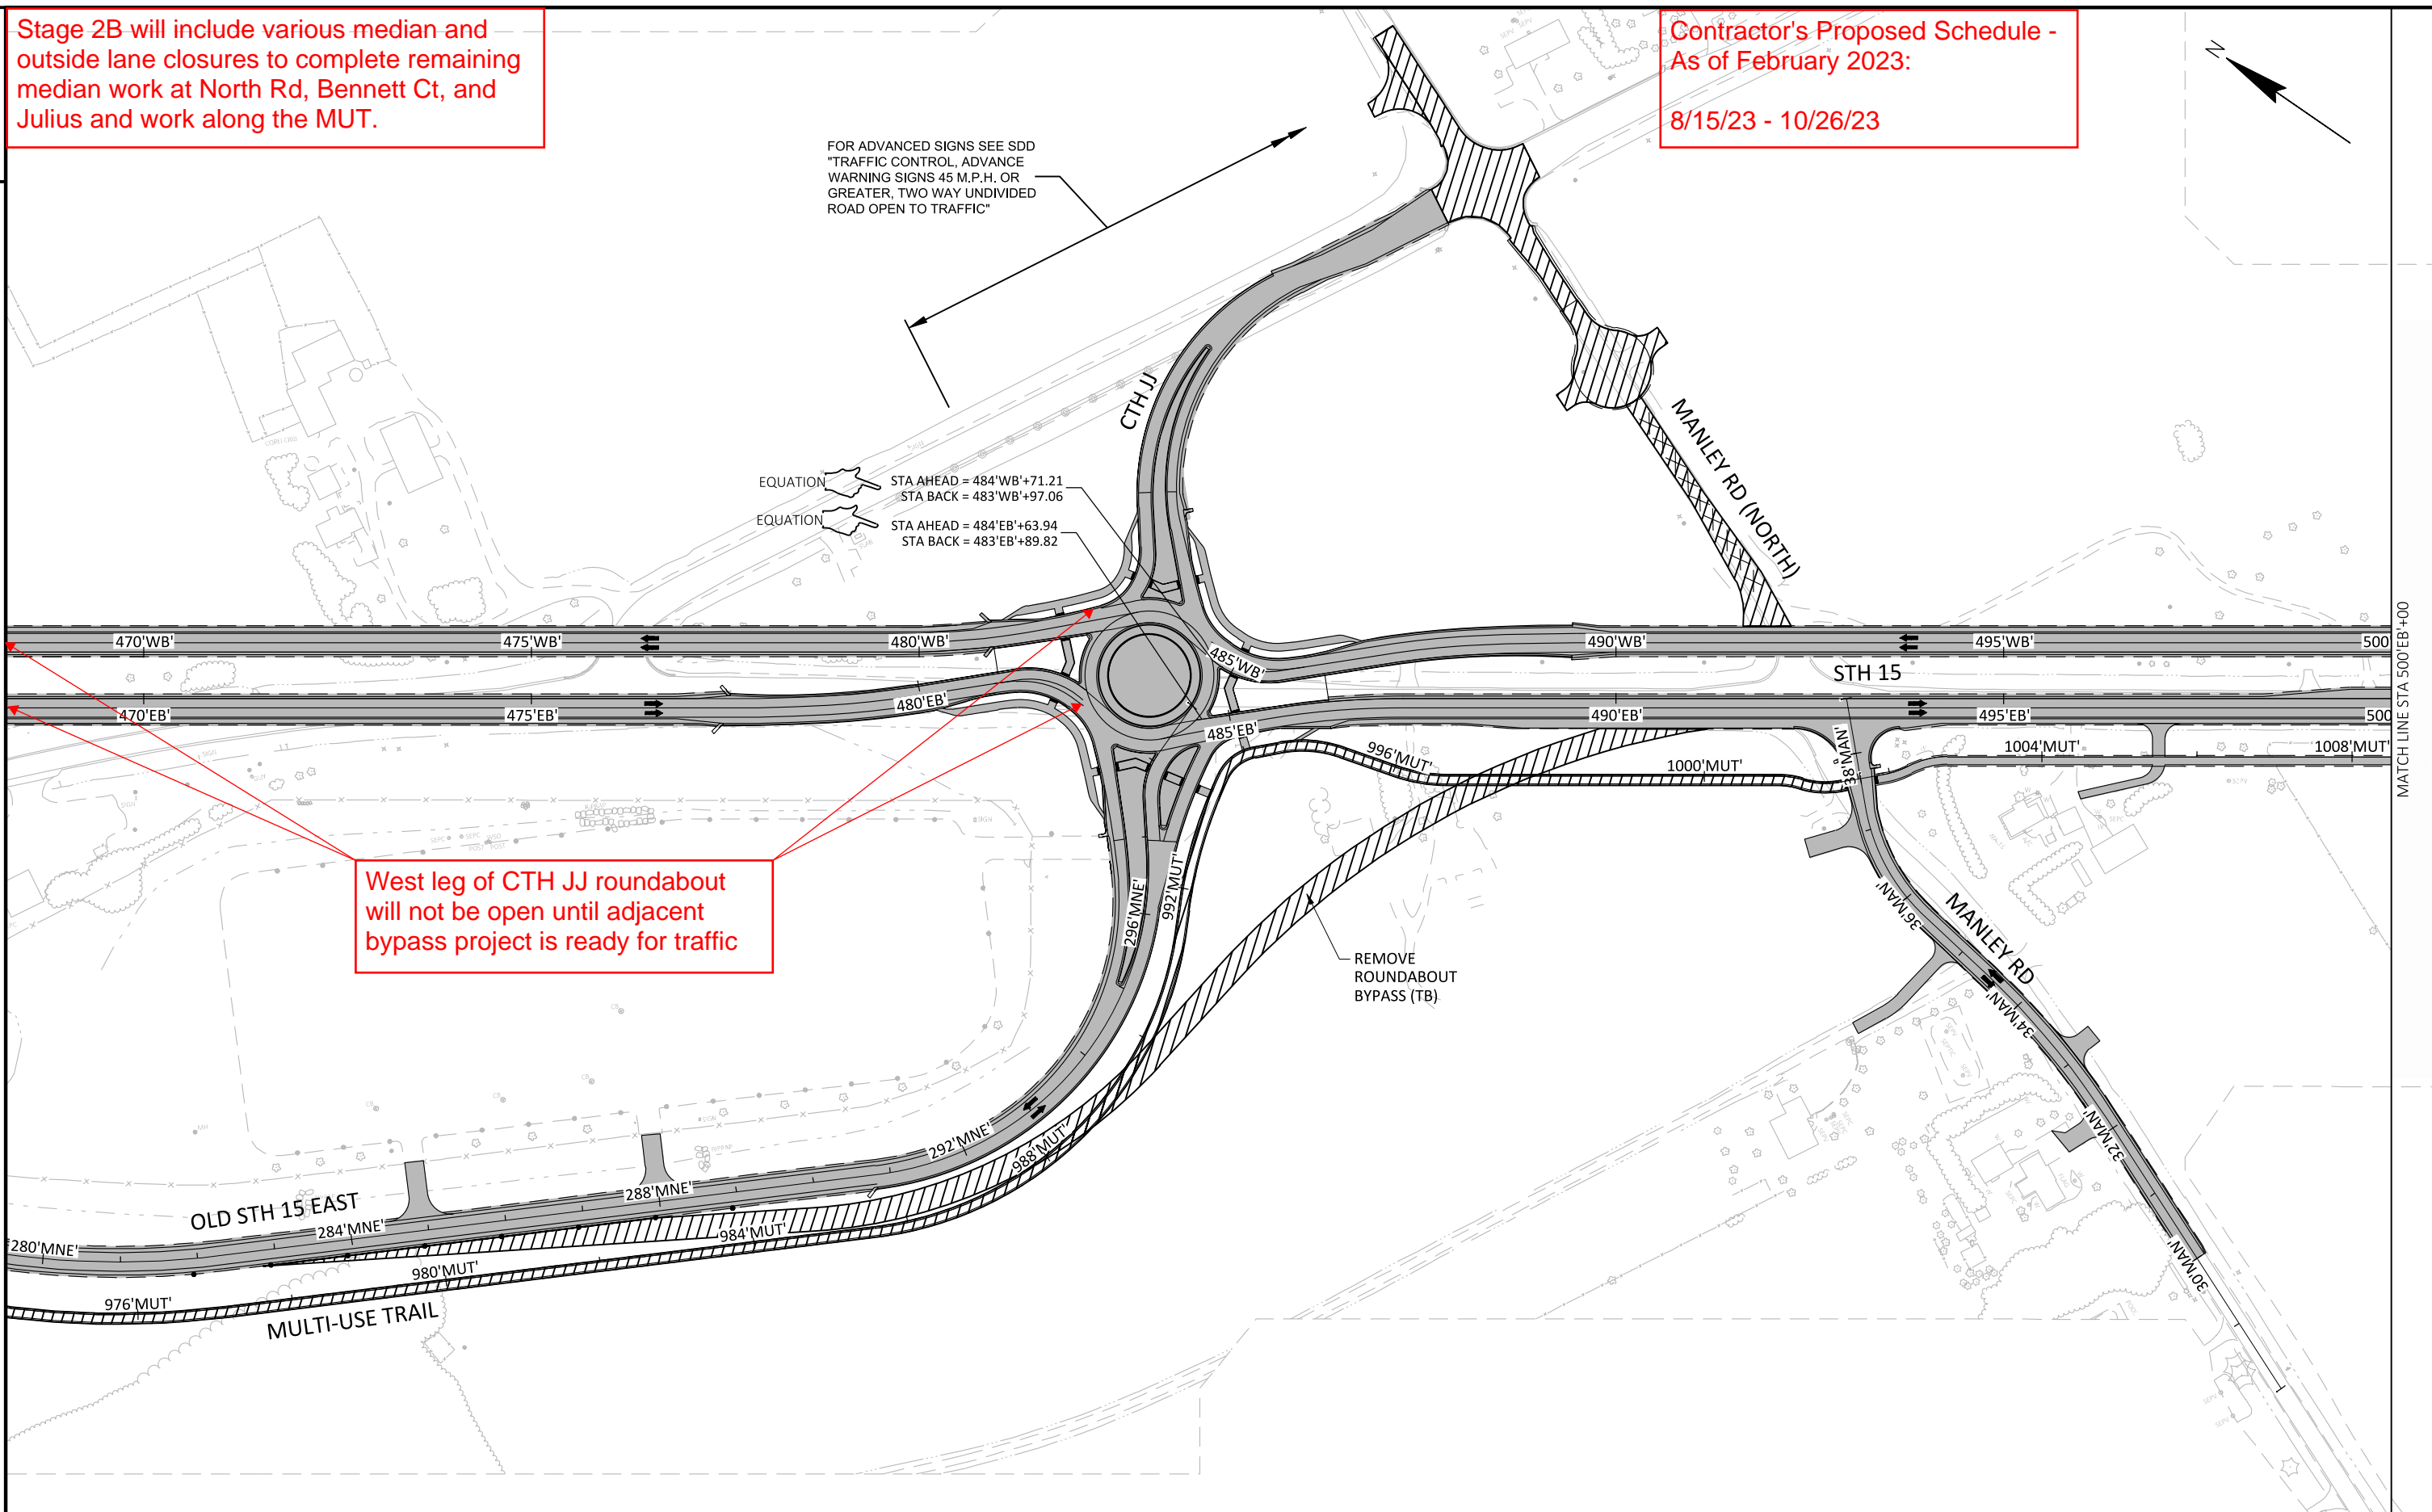

PROJECT NO: 1146-75-72

HWY: STH 15

COUNTY: OUTAGAMIE

TRAFFIC CONTROL - **STAGE 2B STH 15**

SHEET

E

FILE NAME : C:\PW_WORKDIR\DEN001\JEG_BUGARIJA\11467572-026502-TC.DWG
LAYOUT NAME - TC2C-02



PLOT DATE : 2/5/2020 1:23 PM

PLOT BY : BUGARIN, JOSE

PLOT NAME :

PLOT SCALE : #####

WISDOT/CADD5 SHEET 42

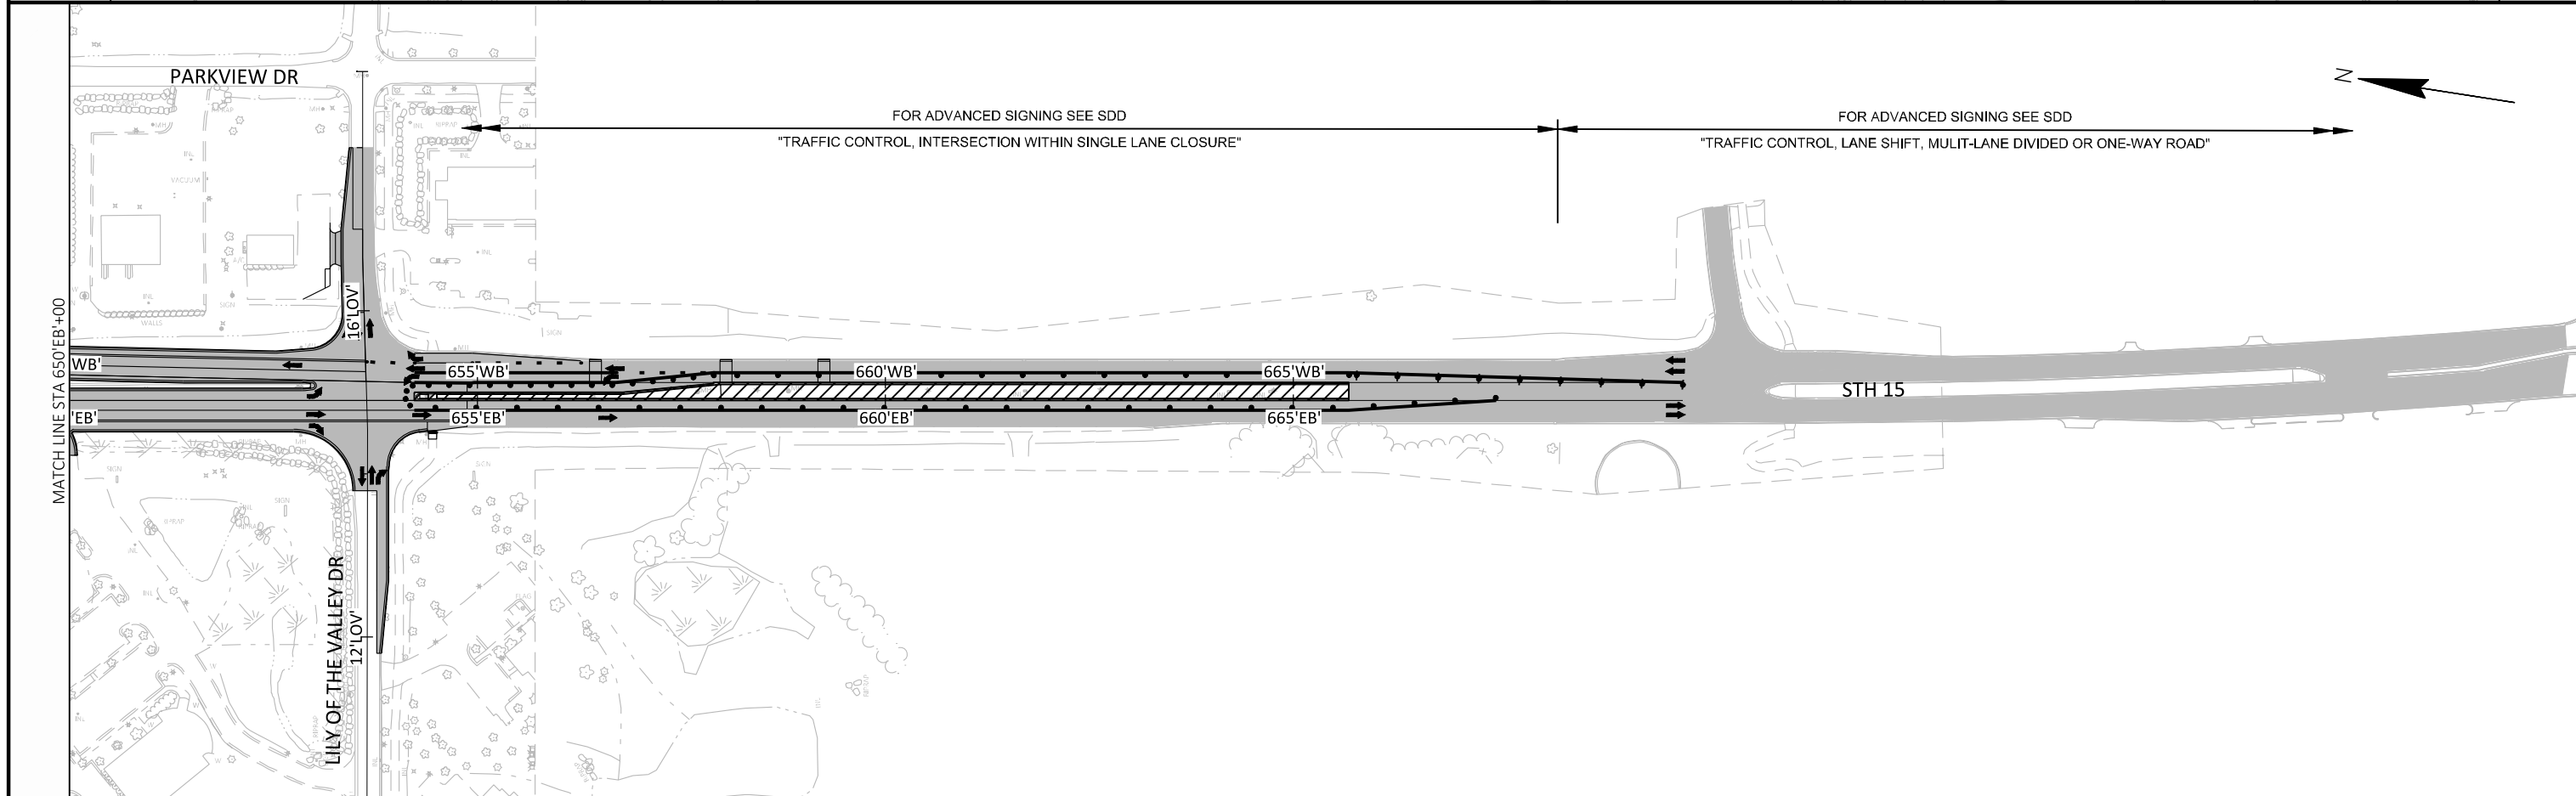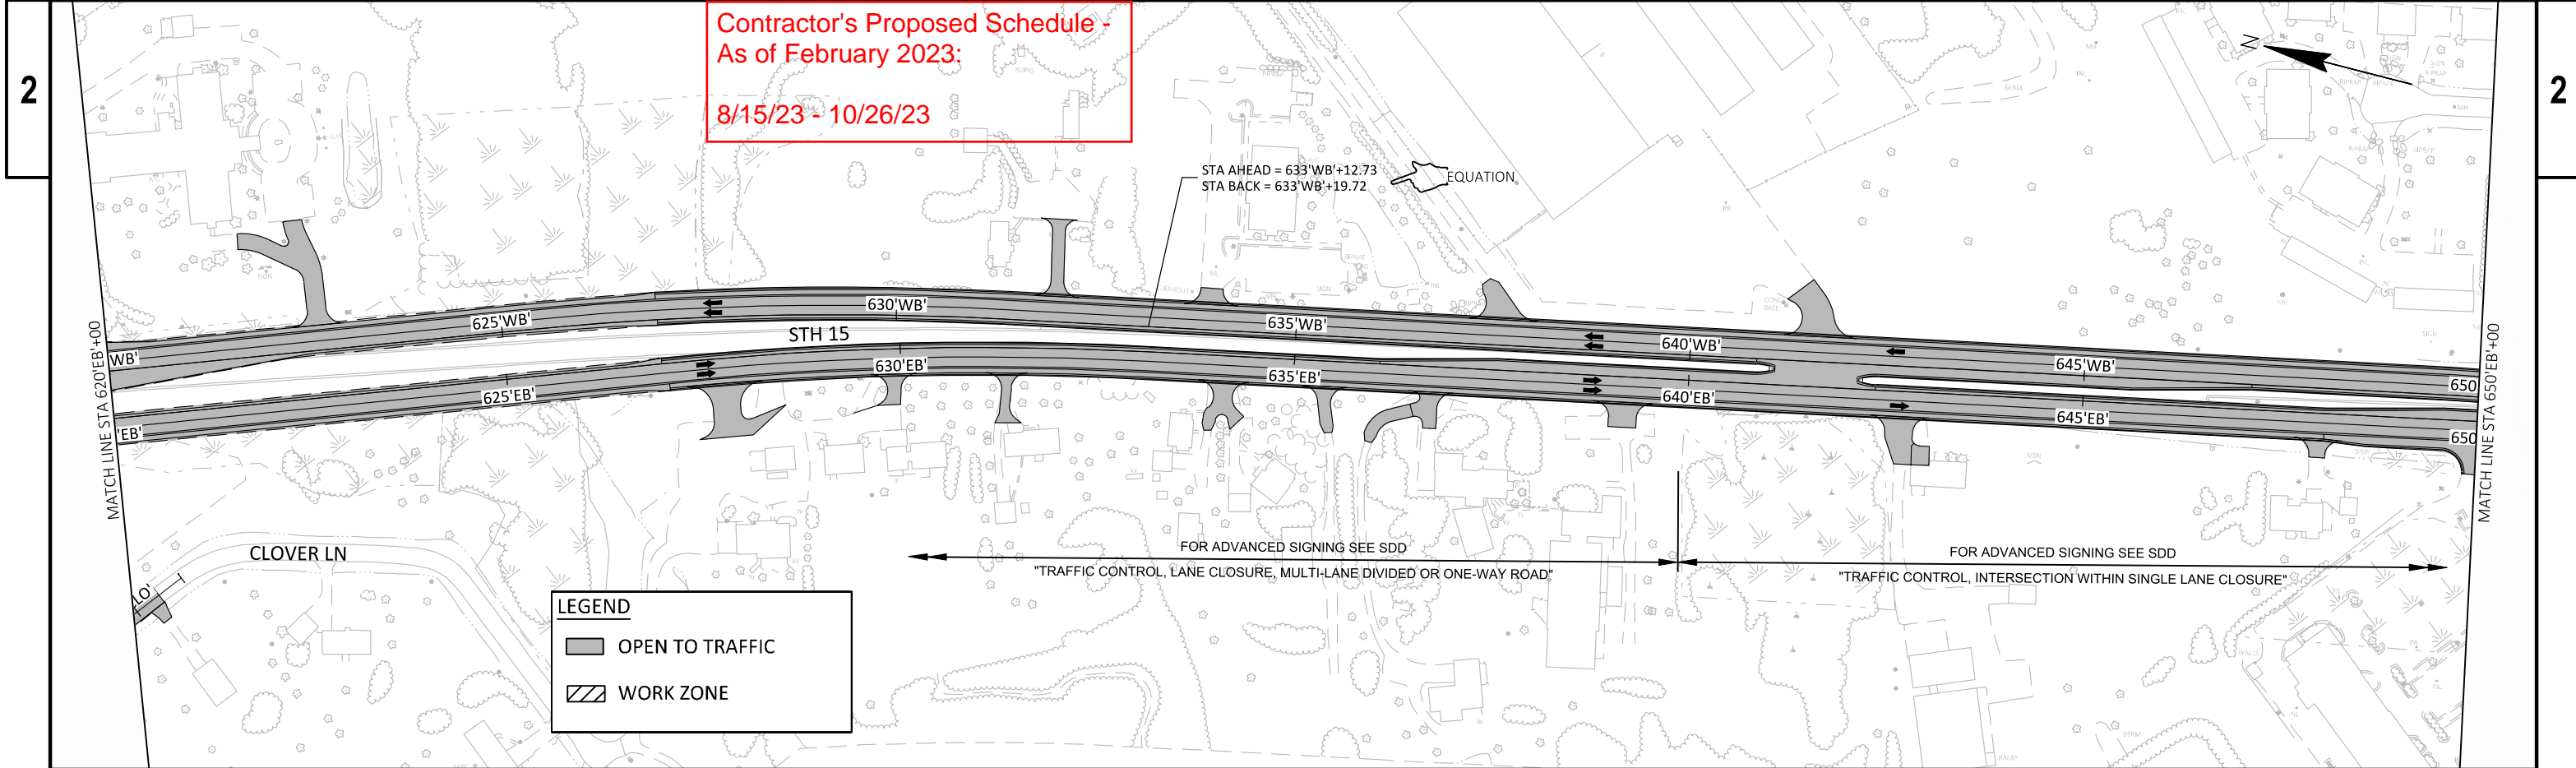

| | | | | | |
|------------------------|-------------|-------------------|--|-------|---|
| PROJECT NO: 1146-75-72 | HWY: STH 15 | COUNTY: OUTAGAMIE | TRAFFIC CONTROL - STAGE 2B STH 15 | SHEET | E |
|------------------------|-------------|-------------------|--|-------|---|
