


HAULING ACTIVITY: I-94 & WISCONN VALLEY PROJECTS

WEEK OF 6/16/19 - 6/22/19

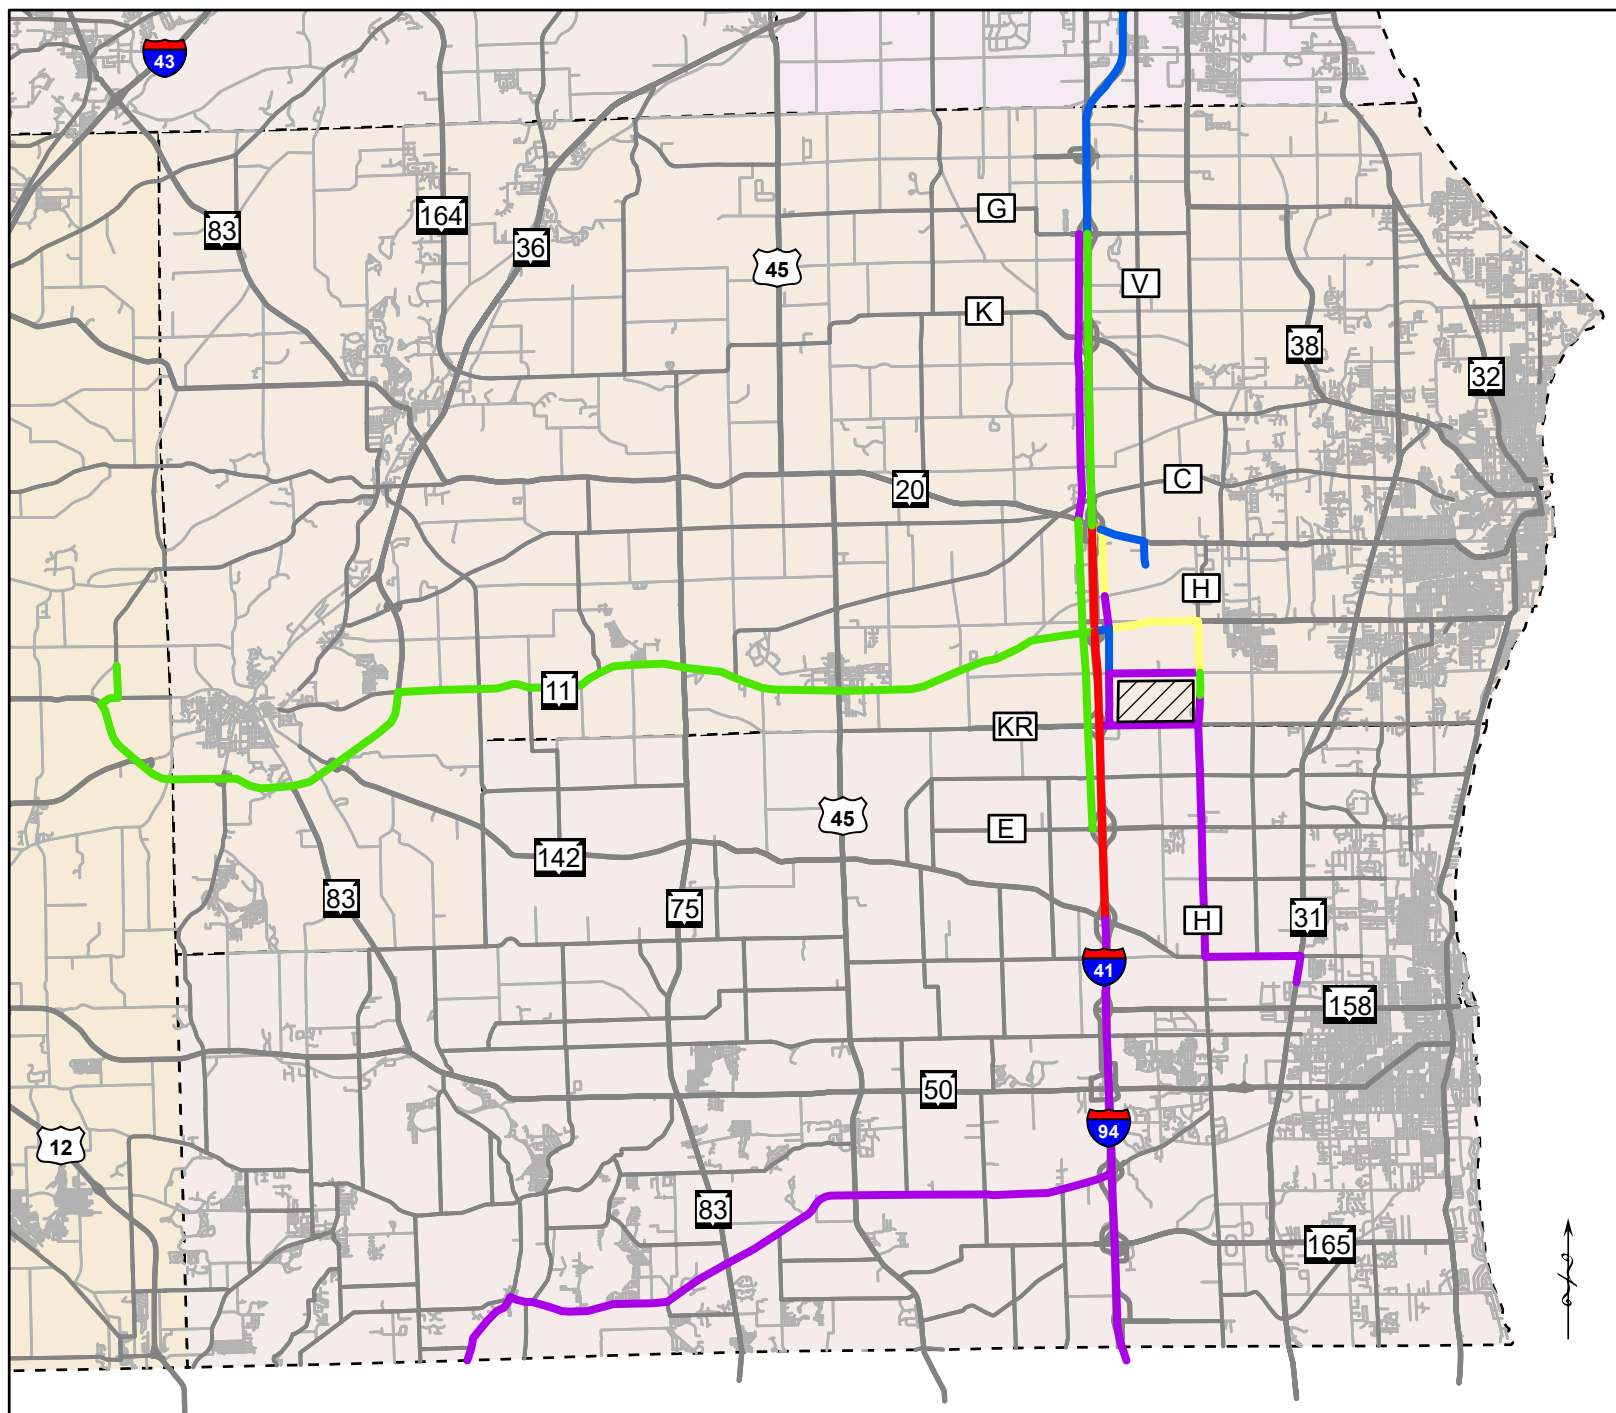

Average Loads/Day

- 750+
- 600-749
- 450-599
- 300-449
- 150-299
- 1-149

Map represents average truck trips per day on each route for combined public and private projects.

Hauling generally occurs Monday-Saturday.

Truck volume will fluctuate daily.

I-94 North Segment hauling is not included.

Questions?
Stephanie Leraneth, 414-750-1397

I-94 NS & Wisconn Valley Projects

Weekly Hauling Activity Memo

week of 6/16/19 - 6/22/19

Public Projects

Private Projects

Utility Projects

Project	Origin	Route	Destination	Avg Loads per day	Purpose	Community Impacts	Hauling Hours
I-94 S. Seg	On Site Hauling	NB/SB 94 between STH 142 and STH 20 (Hoffman)	I-94 Access	530	onsite material balancing/Wilks Site	Mt.Pleasant to Somers	7a - 6p
I-94 S. Seg	Thelen Sand and Gravel	CTH C (Kenosha) to IH 94 to IH 94 Access	I-94 Access	105	Storm Sewer Backfill Material	Wilmont to Mt. Pleasant	7a - 5p
I-94 S. Seg	On site Hauling (Michels)	WFR (project limits) to IH 94 Access	I-94 Access	395	onsite material balancing (removal materials)	Mt.Pleasant	7a - 6p
I-94 C. Seg	On site Hauling (Michels)	WFR (project limits) to IH 94 Access	I-94 Access	65	onsite material balancing (removal materials)	Mt.Pleasant	7a - 6p
I-94 C. Seg	On Site Hauling	NB/SB 94 between CTH G and STH 20	I-94 Access	190	onsite material balancing/Lange	Mt.Pleasant to Caledonia	7p - 5a
Braun Rd	Cornerstone Batch Plant	East Frontage Rd north to WIS-11 east to CTH H south to Braun Rd.	Braun Road	100	incoming concrete	Mt. Pleasant, Racine Co,	7a - 6p
International Dr.	Franklin Aggregate	CTH BB west to S 68th St south to W Drexel Ave east to I-94 South to WIS-20 east to International Dr. south	International Dr.	100	incoming aggregate	Franklin, Oak Creek, Mt. Pleasant, Racine Co, Milwaukee Co	7a - 5p
International Dr.	Burlington Spring Valley	WIS-11 east to I-94 north to WIS-20 east to International Dr. south	International Dr.	100	incoming aggregate	Mt. Pleasant, Racine Co	7a - 5p
CTH H Phase 1	Hribar	EFR south to WIS-11 east to CTH H south	CTH H	40	incoming concrete	Mt. Pleasant, Racine Co	6a - 8p
CTH KR	Thelen Materials LLC	IL-173 east to US-41 north to I-94 north to CTH KR to access driveways	CTH KR	12	storm sewer backfill	Mt. Pleasant, Racine Co, Kenosha Co	6a - 6p
CTH KR	Hribar	EFR south to CTH KR east	CTH KR	20	incoming aggregate	Mt. Pleasant, Racine Co	6a - 6p
Wisconn Valley	Thelen Materials	IL-173 east to US-41 north to I-94 north to CTH KR to EFR north to Braun Rd	Braun Road	20	incoming pipe backfill	Mt Pleasant, Racine Co, Kenosha co	7a-6p
Wisconn Valley	Franklin Aggregate	CTH BB west to S 68th St south to W Drexel Ave east to I-94 South to WIS-20 east to East Frontage Rd south to Braun	Braun Road	80	incoming aggregate	Franklin, Oak Creek, Mt. Pleasant, Racine Co, Milwaukee Co	7a - 6p
Gilbane	Burlington	EB STH 11- SB CTH H - Gate 5 Monday - Friday	Dev. Area 1	200	incoming aggregate	Burlington, Union Grove, Mt Pleasant, Racine Co	6a - 6:30p
Gilbane	Point Ready Mix (Burlington)	EB STH 11 - SB CTH H - Gate 5 Wednesday - Friday	Dev Area 1	70	Concrete	Mt. Pleasant, Racine Co	6a - 630p
Gilbane	Ozinga Concrete (Kenosha)	NB STH 31 - WB Washington Rd - NB CTH H - Gate 5 Wednesday - Friday	Dev Area 1	30	Concrete	Mt. Pleasant, Racine Co	6a - 630p
Gilbane	Illinois	NB I-94 - EB STH 11-SB CTH H - Gate 5 Monday - Friday	Dev Area 1	3	Rebar	Mt. Pleasant, Racine Co	6a - 630p
Gilbane	Dev. Area 1	Gate 5 - NB CTH H - WB STH 11 - SB East Frontage Road - Wisconn Valley Way Monday - Friday	Wisconn Valley Way	80	Spoils/Hauling	Mt. Pleasant, Racine Co	6a - 630p

Questions:

Stephanie Leranthy, 414-750-1397

