


PROJECT UPDATE

CHESTER STREET CONSTRUCTION TIMELINE

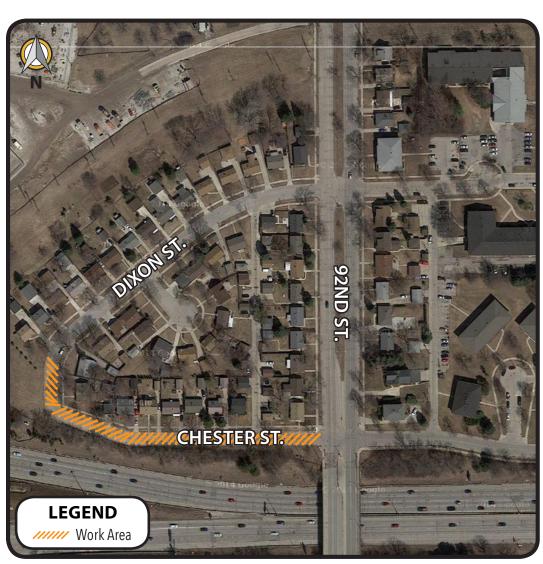

As part of the Zoo Interchange project, work continues on and around Chester Street. Work on Chester Street will require the implementation of one-way traffic on Chester Street. This switch is scheduled to take place on Monday, December 22. In addition to the traffic switch, upcoming work is outlined below.

12/22: Implementation of one-way traffic on Chester Street. Although there are short portions of two-way roadway, a majority of the area will be one-way, eastbound traffic, permanently.

12/22 and 12/23: Installation of 6' chain-link fence with screening and barrier wall down the center line of Chester Street.

12/26 - 1/5/15: Prepare area for installation of retaining wall. This will include pavement breaking and removal, excavation and creating a bench for the drill rig to sit on. The drill rig will work inside the fence only. During this time, there will be very limited trucking on Chester Street due to limited access.

1/5/15: A drill rig will begin installing a soldier pile wall. The wall work in this area will last about 5 months. This work will not include pile driving, but drill rigs, dump truck removal of dirt, and concrete pours will take place during long daytime hours.

End of January/Beginning of February 2015: Close 92nd Street, over I-94, to demolish bridge. The bridge is to remain closed through Fall 2015. Pile driving will take place during the end of February and into March.

End of Summer 2015: Installation of noise wall along Chester Street.

August 2015: Begin reconstruction of pavement on Chester Street. This work is slated to take approximately two months and be completed in Fall 2015. This work will require intermittent disruption to residential access, but the project team will always work closely with the residents to coordinate these impacts. High early strength concrete will be utilized to decrease the length of impacts. As part of this work, driveway widening and reconfiguration will be completed to match the new street.

The project team understands how great of an impact this work is and will continue to work with each of you to coordinate as much as possible. Please keep in mind that all construction activities are weather dependent and subject to change. Additional communications will be sent out any time there is a significant change to schedule or if there will be nighttime work occurring near your home. The project team appreciates your patience during this period of intense construction in your area.













