

State Project ID: 1206-06-79
US 12, Dane County
Whitney Way to I-39/90
Madison

Update Date: **June 25, 2021**

Project Weekly Update **(Madison Beltline Construction)**

General Project Information –

WisDOT is making the following improvements on the Madison Beltline (US 12) between the Whitney Way exit and I-39/90 interchange.

- Resurface to address deteriorating pavement;
- Improve existing drainage deficiencies;
- Replace the existing median barrier wall; and
- Upgrade the Beltline median shoulders to be used part-time as travel lanes.

Project Schedule:

- Overall Completion Date: December 2021

Traffic Impacts:

- Nighttime single and double lane closures will be occurring from approximately Agriculture Drive to Fish Hatchery Road for the EB and WB Beltline from 6:30 PM to 6:00 AM. Daytime shoulder closures will also be taking place for the EB and WB Beltline between Agricultural Drive to Fish Hatchery Road.
- Various ramp closures from Seminole Highway to Stoughton Road will also be taking place throughout any given night.
- **Holiday work restriction for Independence Day will be in effect from 6am Friday, July 2 until 6:30am Tuesday, July 6.**


Please refer to the following website link for anticipated specific closure locations (<https://projects.511wi.gov/flexlane/closures/>). Please note that work is weather dependent and may be subject to change.

Work this week (week of 6/28/2021)

- Crews will continue survey and layout operations throughout the project.
- Crews will continue median sign structure shafts from Park Street to the west project limits.
- Crews will continue existing median barrier wall / pavement breaking and removal operations from Park Street working west.
- Crews will continue storm sewer installations from Park Street to Seminole Highway.
- Crews will continue finish grading operations for concrete base from the Yahara River to Park Street.
- Crews will continue placing concrete base in the median from Agriculture Drive to the Yahara River bridge and from the Yahara River bridge to Park Street.
- Crews will continue barrier wall footing and barrier wall placement from the Yahara River bridge to Park Street.
- Crews will continue electrical installations throughout the project.
- Crews will continue concrete base patching operations.



Concrete barrier wall transition placement.

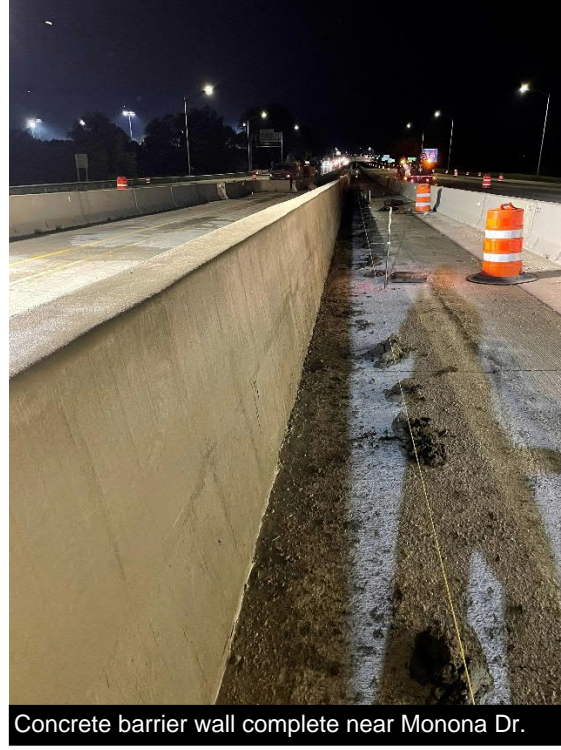

Concrete barrier wall complete near Monona Dr.

Work scheduled for the next week (week of 7/05/2021)

- Crews will continue survey and layout operations.
- Crews will continue placing sign structure shafts from Park Street to the west project limits.
- Crews will continue electrical installations throughout the project.
- Crews will continue existing pavement removals from Park Street to the west project limits.
- Crews will continue storm sewer installation operations from Park Street to the west project limits.
- Crews will continue finish grading operations for concrete base from South Towne Drive to Park Street.
- Crews will continue placing concrete base from the Yahara River bridge to Park Street.
- Crews will continue barrier wall footing and barrier wall placement from the Yahara River bridge to Park Street.
- Crews will continue overnight base patching operations.
- Crews will continue electrical installations throughout the project.
- Crews are anticipated to resume HMA paving operations the week of July 12 from I-39 to the Yahara River bridge.

Contact information

Trenton Diehl, Strand Associates, Inc.- Project Leader

Email: trenton.diehl@strand.com

If you would like to be added to the weekly update distribution list, please email your name and email address to trenton.diehl@strand.com. Thank you for your patience and understanding throughout this construction season.

Project Website

<https://projects.511wi.gov/flexlane/>



Beltline aerial photo between Fish Hatchery Rd and Todd Drive. (Photo provided by WisDOT Bureau of Aeronautics.)
