

**State Project ID: 1206-06-79**  
**US 12, Dane County**  
**Whitney Way to I-39/90**  
**Madison**

Update Date: **July 01, 2021**

## **Project Weekly Update** **(Madison Beltline Construction)**

### **General Project Information –**

WisDOT is making the following improvements on the Madison Beltline (US 12) between the Whitney Way exit and I-39/90 interchange.

- Resurface to address deteriorating pavement;
- Improve existing drainage deficiencies;
- Replace the existing median barrier wall; and
- Upgrade the Beltline median shoulders to be used part-time as travel lanes.

### **Project Schedule:**

- Overall Completion Date: December 2021

### **Traffic Impacts:**

- Nighttime single and double lane closures will be occurring from approximately Agriculture Drive to Fish Hatchery Road for the EB and WB Beltline from 6:30 PM to 6:00 AM. Daytime shoulder closures will also be taking place for the EB and WB Beltline between Agricultural Drive to Fish Hatchery Road.
- Various ramp closures from Seminole Highway to Stoughton Road will also be taking place throughout any given night.
- EB and WB Beltline long term HMA paving operations will continue for the remainder of the construction season.
- **Holiday work restriction for Independence Day will be in effect from 6am Friday, July 2 until 6:30am Tuesday, July 6.**

Please refer to the following website link for anticipated specific closure locations (<https://projects.511wi.gov/flexlane/closures/>). Please note that work is weather dependent and may be subject to change.

### **Work this week (week of 7/05/21)**

- Crews will continue survey and layout operations throughout the project.
- Crews will continue storm sewer installations from Park Street to Seminole Highway.
- Crews will continue finish grading operations for concrete base from the Park Street to Seminole Highway.
- Crews will continue placing concrete base in the median from the Yahara River bridge to Park Street.
- Crews will continue barrier wall footing and barrier wall placement from the Yahara River bridge to Park Street.
- Crews will complete placement of barrier wall transitions at sign structures from Agriculture Drive to the Yahara River bridge.
- Crews are anticipated to resume HMA paving at on the WB Beltline at the east project limits to the Yahara River bridge on the night of July 8<sup>th</sup>.
- Crews will continue electrical installations throughout the project.
- Crews will continue concrete base patching operations.



Concrete barrier wall complete near Stoughton Road (looking east).

**Work scheduled for the next week (week of 7/12/2021)**

- Crews will continue survey and layout operations.
- Crews will continue electrical installations throughout the project.
- Crews will continue storm sewer installation operations from Park Street to the west project limits.
- Crews will continue finish grading operations for concrete base from Park Street to Seminole Highway.
- Crews will continue placing concrete base from the Yahara River bridge to Park Street.
- Crews will continue barrier wall footing and barrier wall placement from the Yahara River bridge to Park Street.
- Crews will continue placement of barrier wall transitions at sign structures from the Yahara River bridge to Park Street.
- Crews will continue electrical installations throughout the project.
- Crews will continue HMA paving operations from the east project limits to the Yahara River bridge.



### **Contact information**


Trenton Diehl, Strand Associates, Inc.- Project Leader

Email: [trenton.diehl@strand.com](mailto:trenton.diehl@strand.com)

If you would like to be added to the weekly update distribution list, please email your name and email address to [trenton.diehl@strand.com](mailto:trenton.diehl@strand.com). Thank you for your patience and understanding throughout this construction season.

### **Project Website**

<https://projects.511wi.gov/flexlane/>

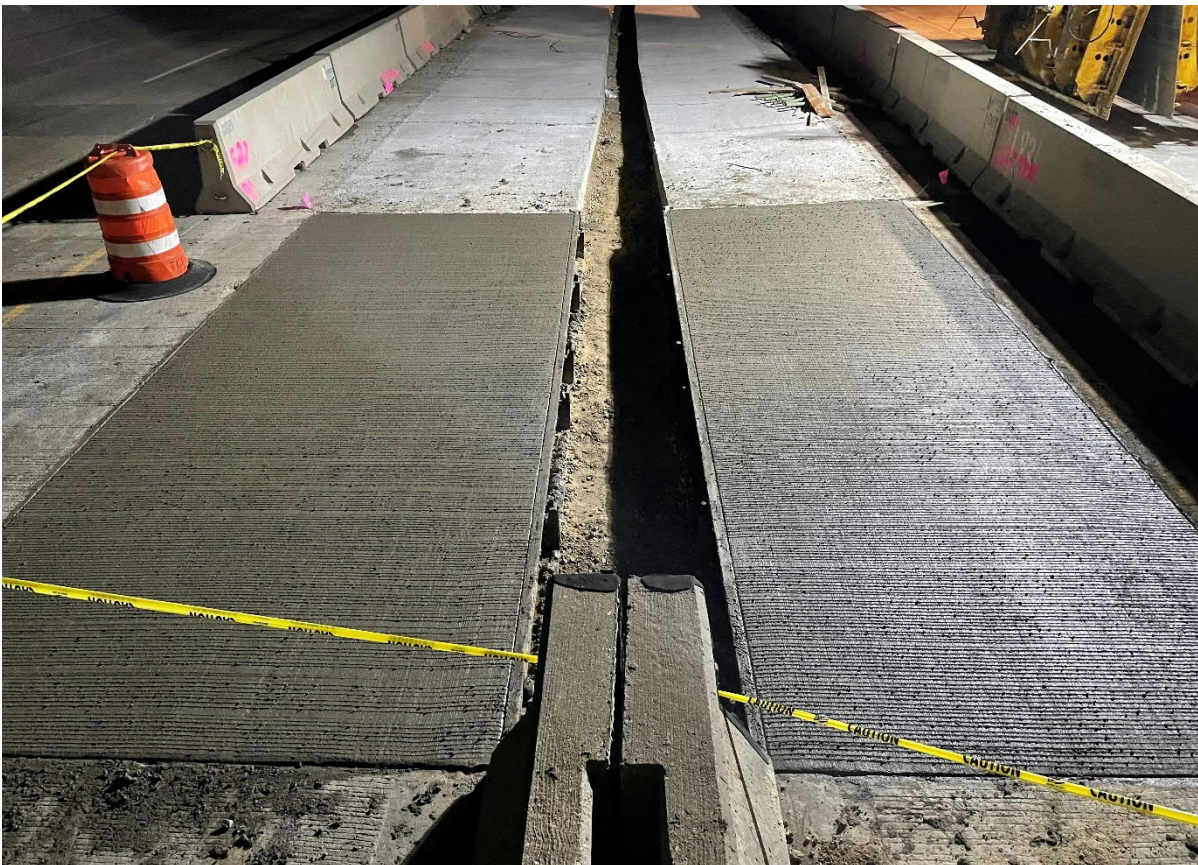

Median concrete approach slab replacement.
