



Update Date: October 14, 2021

State Project ID: 1206-06-79 US 12, Dane County Whitney Way to I-39/90 Madison

Project Weekly Update (Madison Beltline Construction)

General Project Information –

WisDOT is making the following improvements on the Madison Beltline (US 12) between the Whitney Way exit and I-39/90 interchange.

- · Resurface to address deteriorating pavement,
- Improve existing drainage deficiencies,
- Replace the existing median barrier wall, and
- Upgrade the Beltline median shoulders to be used part-time as travel lanes.

Traffic Impacts:

- Nighttime single and double lane closures will be occurring from approximately I-39 to Whitney Way for the EB and WB Beltline from 6:30 PM to 6:00 AM. Daytime shoulder closures will also be taking place for the EB and WB Beltline between Agricultural Drive to Fish Hatchery Road.
- Various ramp closures from Seminole Highway to Stoughton Road will also be taking place throughout any given night.
- Median daytime lane and ramp closures from 9am to 2pm are anticipated for the EB and WB Beltline from approximately John Nolan Drive to approximately Verona Road starting Monday through Thursday, October 18 - October 21. In addition, daytime ramp closures may occur Monday through Thursday for the Fish Hatchery Road and Todd Drive ramps to the westbound Beltline as well as the Todd Drive ramp to the eastbound Beltline.
- Nighttime rolling slowdowns utilizing Wisconsin State Patrol will be utilized October 19 through October 21 for erection of new overhead sign structures and removal of old sign structures. The nighttime rolling slowdowns are anticipated from approximately 11:30pm to approximately 2am.

Please refer to the following website link for anticipated specific closure locations (https://projects.511wi.gov/flexlane/closures/). Please note that work is weather dependent and may be subject to change.


Work this week (week of 10/18/21)

- Crews will continue survey and layout operations throughout the project.
- Crews will continue barrier wall transition grinding and rubbing operations.
- Crews will complete HMA paving EB and WB between Whitney Way and Fish Hatchery Road.
- Crews will continue placing overhead Type I signs and installing overhead sign structures along with other Type II sign items.
- Crews will continue electrical installations throughout the project.
- Crews will continue to install new guardrail and adjust existing guardrail between Seminole Highway and South Towne Drive.
- Crews will continue placing permanent pavement markings from Seminole Highway to IH 39 both EB and WB.





Crews will continue final cleanup of the project.

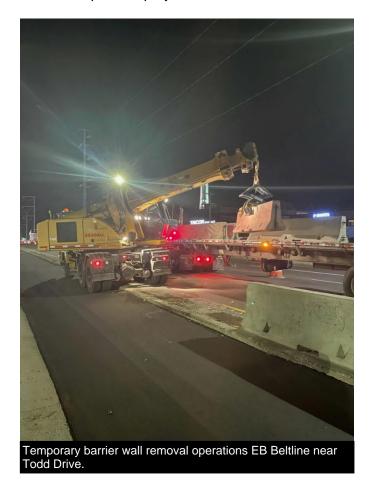

Work scheduled for the next week (week of 10/25/2021)

- Crews will continue electrical installations throughout the project.
- Crew may continue guardrail adjustments throughout project.
- Crews will continue overhead sign structure and sign installations throughout the project.
- Crews will continue any final cleanup of the project site.

Contact information

Trenton Diehl, Strand Associates, Inc.- Project Leader

Email: trenton.diehl@strand.com

If you would like to be added to the weekly update distribution list, please email your name and email address to trenton.diehl@strand.com. Thank you for your patience and understanding throughout this construction season.

Project Website

https://projects.511wi.gov/flexlane/







EB Beltline between Park Street and Rimrock Road (crews working on completing permanent pavement markings).
