

State Project ID: 1206-06-79
US 12, Dane County
Whitney Way to I-39/90
Madison

Update Date: **November 5, 2021**

Project Weekly Update **(Madison Beltline Construction)**

General Project Information –

WisDOT is making the following improvements on the Madison Beltline (US 12) between the Whitney Way exit and I-39/90 interchange.

- Resurface to address deteriorating pavement,
- Improve existing drainage deficiencies,
- Replace the existing median barrier wall, and
- Upgrade the Beltline median shoulders to be used part-time as travel lanes.


Traffic Impacts:

- Nighttime single and double lane closures will be occurring from approximately I-39 to Whitney Way for the EB and WB Beltline from 6:30 PM to 6:00 AM. Daytime shoulder closures will also be taking place for the EB and WB Beltline between Agricultural Drive to Fish Hatchery Road.
- Various ramp closures from Seminole Highway to Stoughton Road will also be taking place throughout any given night.
- Median daytime lane and ramp closures from 9am to 2pm are anticipated for the EB and WB Beltline from approximately John Nolan Drive to approximately Whitney Way starting Monday through Thursday, November 8– November 11 and November 15 – November 18. In addition, daytime ramp closures may occur Monday through Thursday for the Fish Hatchery Road and Todd Drive ramps to the westbound Beltline as well as the Todd Drive ramp to the eastbound Beltline.
- Nighttime rolling slowdowns utilizing Wisconsin State Patrol will be utilized November 8 through November 11 for erection of new overhead sign structures and removal of old sign structures. The nighttime rolling slowdowns are anticipated from approximately 11:30pm to approximately 2am.

Please refer to the following website link for anticipated specific closure locations (<https://projects.511wi.gov/flexlane/closures/>). Please note that work is weather dependent and may be subject to change.

Work this week (week of 11/08/21)

- Crews will continue placing overhead Type I signs and installing overhead sign structures along with other Type II sign items.
- Crews will continue electrical installations throughout the project which include wire installations as well as Lane Control Sign installations.
- Crews will continue restoration items throughout the project.
- Crews will continue running to-do list items and general cleanup of the project.

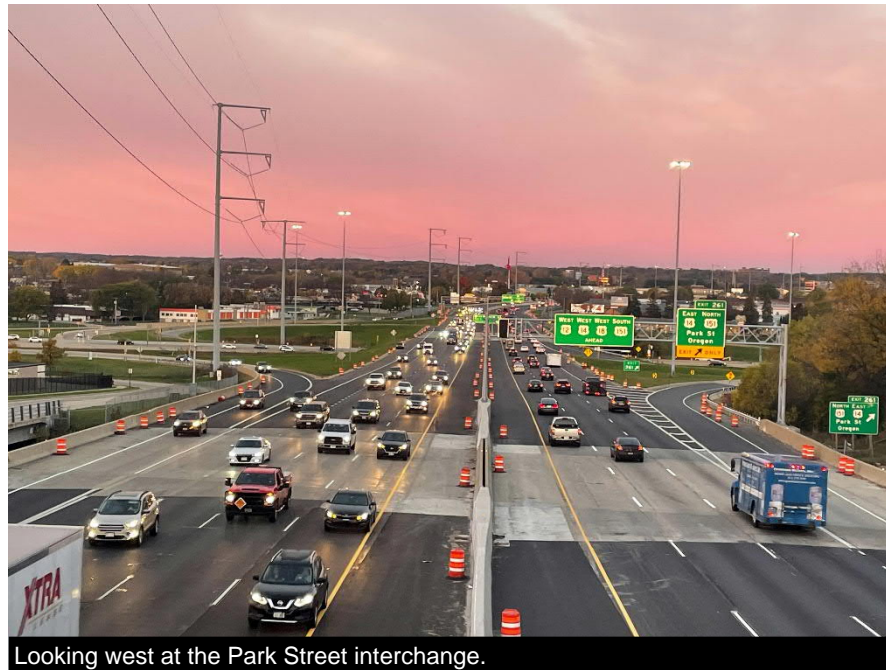

Work scheduled for the next week (week of 11/15/2021)

- Crews will continue placing overhead Type I signs and installing overhead sign structures along with other Type II sign items.
- Crews will continue electrical installations throughout the project which include wire installations and Lane Control Sign installations.
- Crews will continue restoration items throughout the project.
- Crews will continue running to-do list items and general cleanup of the project.

Contact information

Trenton Diehl, Strand Associates, Inc.- Project Leader

Email: trenton.diehl@strand.com

If you would like to be added to the weekly update distribution list, please email your name and email address to trenton.diehl@strand.com. Thank you for your patience and understanding throughout this construction season.

Project Website

<https://projects.511wi.gov/flexlane/>
