



ROCK RIVER BRIDGE STAGING

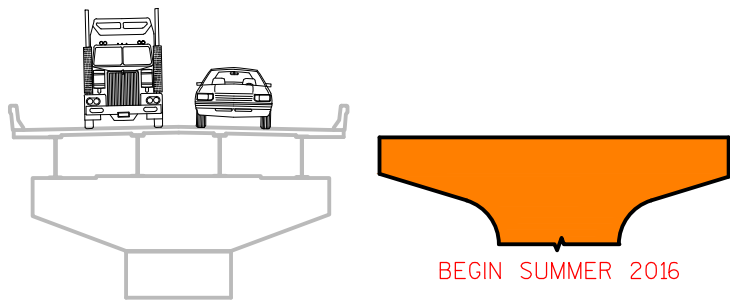

EXISTING SOUTHBOUND BRIDGE

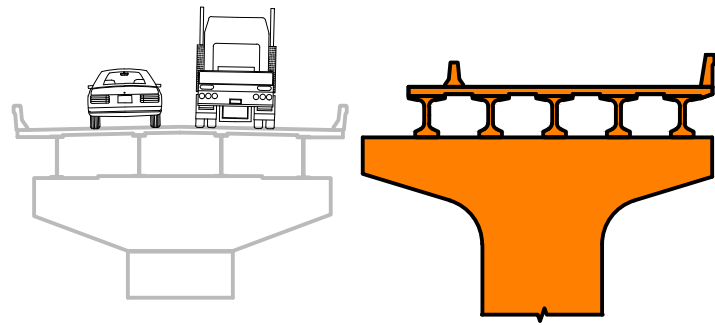


EXISTING NORTHBOUND BRIDGE


BEGIN SUMMER 2016

BEGIN WINTER/SPRING 2016


STAGE 1/2 - CONSTRUCT PARTIAL NEW NORTHBOUND BRIDGE TO EAST
LOOKING NORTH

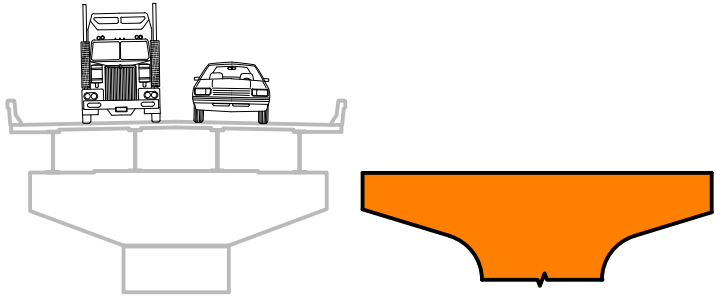

EXISTING SOUTHBOUND BRIDGE




EXISTING NORTHBOUND BRIDGE

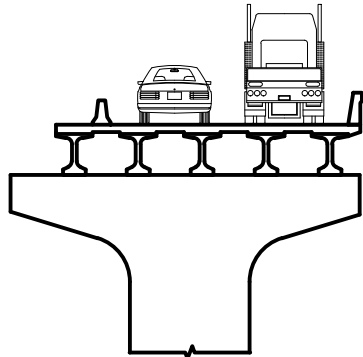


COMPLETED 10/2016

REMOVE 10 & 11/2016

STAGE 3 - REMOVE EXISTING NORTHBOUND BRIDGE
LOOKING NORTH

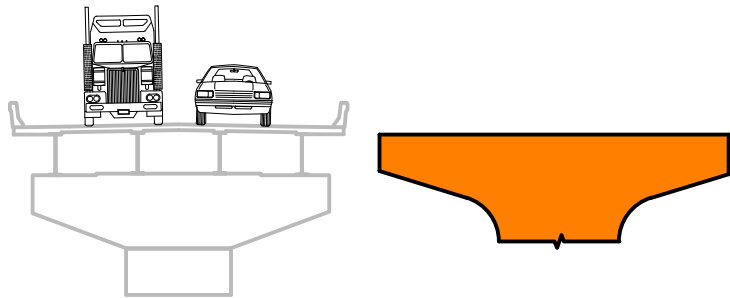


EXISTING SOUTHBOUND BRIDGE

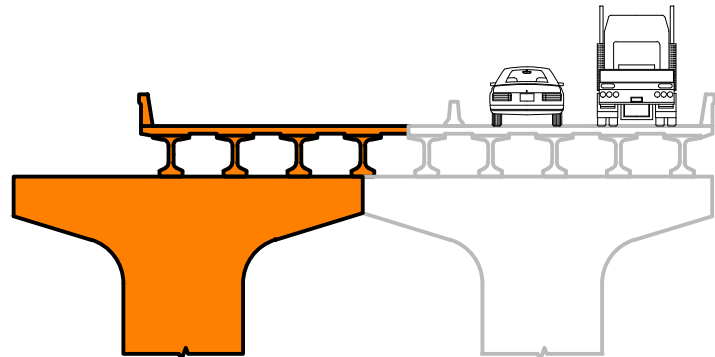


BEGIN 12/2016

STAGE 3 (CONT'D) - CONSTRUCT REMAINING NEW NORTHBOUND BRIDGE & PARTIAL NEW SOUTHBOUND BRIDGE TO EAST
LOOKING NORTH



EXISTING SOUTHBOUND BRIDGE


REMOVE 9 & 10/2017

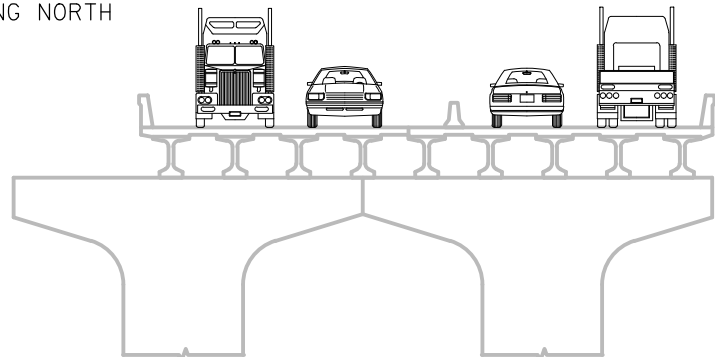

PROPOSED NEW NORTHBOUND BRIDGE


COMPLETED 8/2017

STAGE 4 - REMOVE EXISTING SOUTHBOUND BRIDGE
LOOKING NORTH




PROPOSED NEW SOUTHBOUND BRIDGE

BEGIN 9/2017

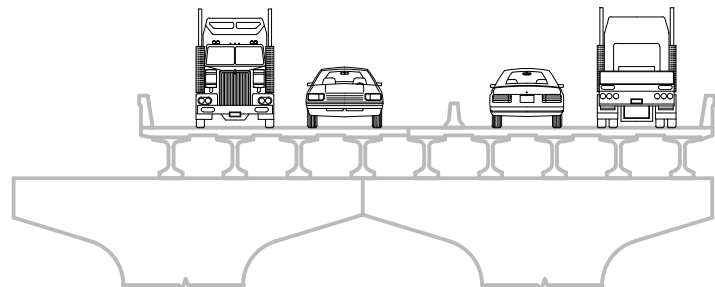


PROPOSED NEW NORTHBOUND BRIDGE

STAGE 4 (CONT'D) - CONSTRUCT REMAINING NEW SOUTHBOUND BRIDGE
LOOKING NORTH

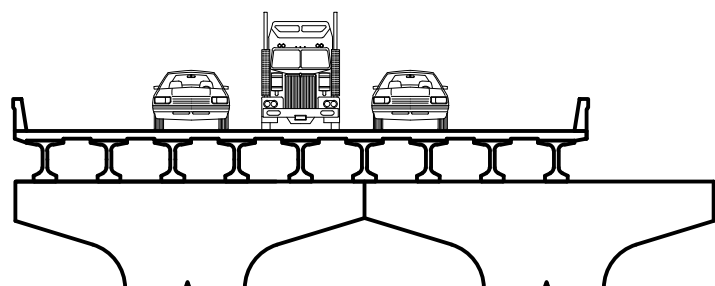

PROPOSED NEW SOUTHBOUND BRIDGE

COMPLETED SUMMER 2018

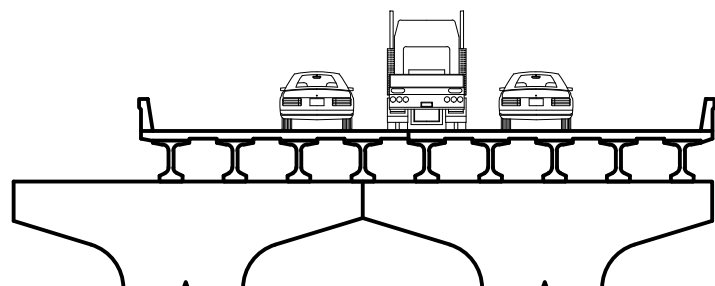

PROPOSED NEW NORTHBOUND BRIDGE

STAGE 4 (CONT'D) - FINAL BRIDGES
LOOKING NORTH
