



STH 140 Weekly Update

May 28, 2025

Illinois State Line to Village of Clinton
Rock County

GENERAL PROJECT INFORMATION

The reconstruction of STH 140 includes a full roadway reconstruction of mainline from the Illinois state line to the south village limits of the Village of Clinton. The project is split into two stages, stage 1 includes work from the Illinois state line to just north of STH 67. As part of stage 1 a new round-a-bout will be constructed at the intersection of STH 67 and STH 140 along with a new box culvert south of STH 67. Work for stage 1 is anticipated to be completed by August 4, 2025.

Stage 2 work consists of reconstruction of STH 140 north of STH 67 including a new box culvert just north of the STH 67 intersection, along with realignment of the CTH P intersection. This portion of the roadway is anticipated to be completed by October 11, 2025.

PROJECT SCHEDULE

- Stage 1: Illinois State Line to north of STH 67
 - Week of May 26, 2025
 - Crews will continue common excavation and placement of select crushed material along STH 140 just south of STH 67.
 - Excavation of STH 67 including removal of pavement will begin Tuesday May 28, 2025 weather dependent.
 - Crews will seed and mulch ditches south of STH 67 that are finished.
 - Week of June 2, 2025
 - Crews will continue common excavation and placement of select crushed material along STH 67.
 - Pipe crews will be on-site installing new driveway and cross culvert pipes at various locations on STH 140. During culvert placement, the roadway will be impassable until backfilled.
- Stage 2: North of STH 67 to Village of Clinton
 - Week of May 26, 2025
 - No work anticipated.
 - Crews will be hauling through this area utilizing large off road trucks.

- Week of June 2, 2025
 - Crews will be hauling through this area utilizing large off road trucks.

Overall Project Completion: October 11, 2025.

TRAFFIC IMPACTS

STH 140 will be closed and detoured for the duration of roadway reconstruction.

- Detour route: See Attachment A
- STH 140 will have a soft closure from the Village of Clinton to CTH P. A soft closure is when the roadway is still closed but local traffic can get through fairly easily. Local traffic is anyone that lives on the closed portion of the roadway or doing business at a property within the closed roadway.
- STH 140 will have a hard closure from STH 67 south to the Illinois State Line. A hard closure is when the roadway is virtually impassable due to the contractor's work activities.

STH 67 will be closed and detoured for the duration of roadway reconstruction.

- Detour route: See Attachment B
- STH 67 will have a **hard closure** at the project limits in both directions. **Starting May 27, 2025.**

Please be alert when traveling the STH 140 corridor. Please note that work is weather dependent and may be subject to change. The use of the detour routes is recommended. Thank you to everyone for your continued patience and understanding throughout the construction season.

CONTACT INFORMATION

Tim Sina, Strand Associates, Inc. - Project Leader

Email: tim.sina@strand.com

If you would like to be added or removed from the weekly update distribution list, please email your name and email address to tim.sina@strand.com.

2

LEGEND

- ◆ STH 140 DETOUR ROUTE
- STH 67 DETOUR ROUTE
- ▨ WORK AREA
- ▤ NEARBY PROJECT WORK AREA
- ⊙ TC SIGN ON POST
- ⊞ EXISTING TYPE II SIGN LOCATION
- ▤ EXISTING FULL SPAN SIGN BRIDGE
- EXISTING CANTILEVER SIGN BRIDGE
- ⊞ TC BARRICADE TYPE III WITH TC SIGN
- * TC SIGN ON LEFT SIGN BRIDGE SUPPORT
- ** TC SIGN ON RIGHT SIGN BRIDGE SUPPORT
- *** TC SIGN ON LIGHT POLE

NOTES




COORDINATE DETOUR SIGNING WITH PROJECT 3320-02-71 TO ENSURE CONSISTENCY IN DETOUR MESSAGING.

ALL SIGNS 48"X48" UNLESS NOTED.

NOT ALL EXISTING SIGN LOCATIONS ARE SHOWN.

STH 67 DETOUR UTILIZES IH 39, IH 43, AND USH 14.

STH 140 DETOUR UTILIZES IL-173, IL-251, USH 51, IH 39, AND IH 43.

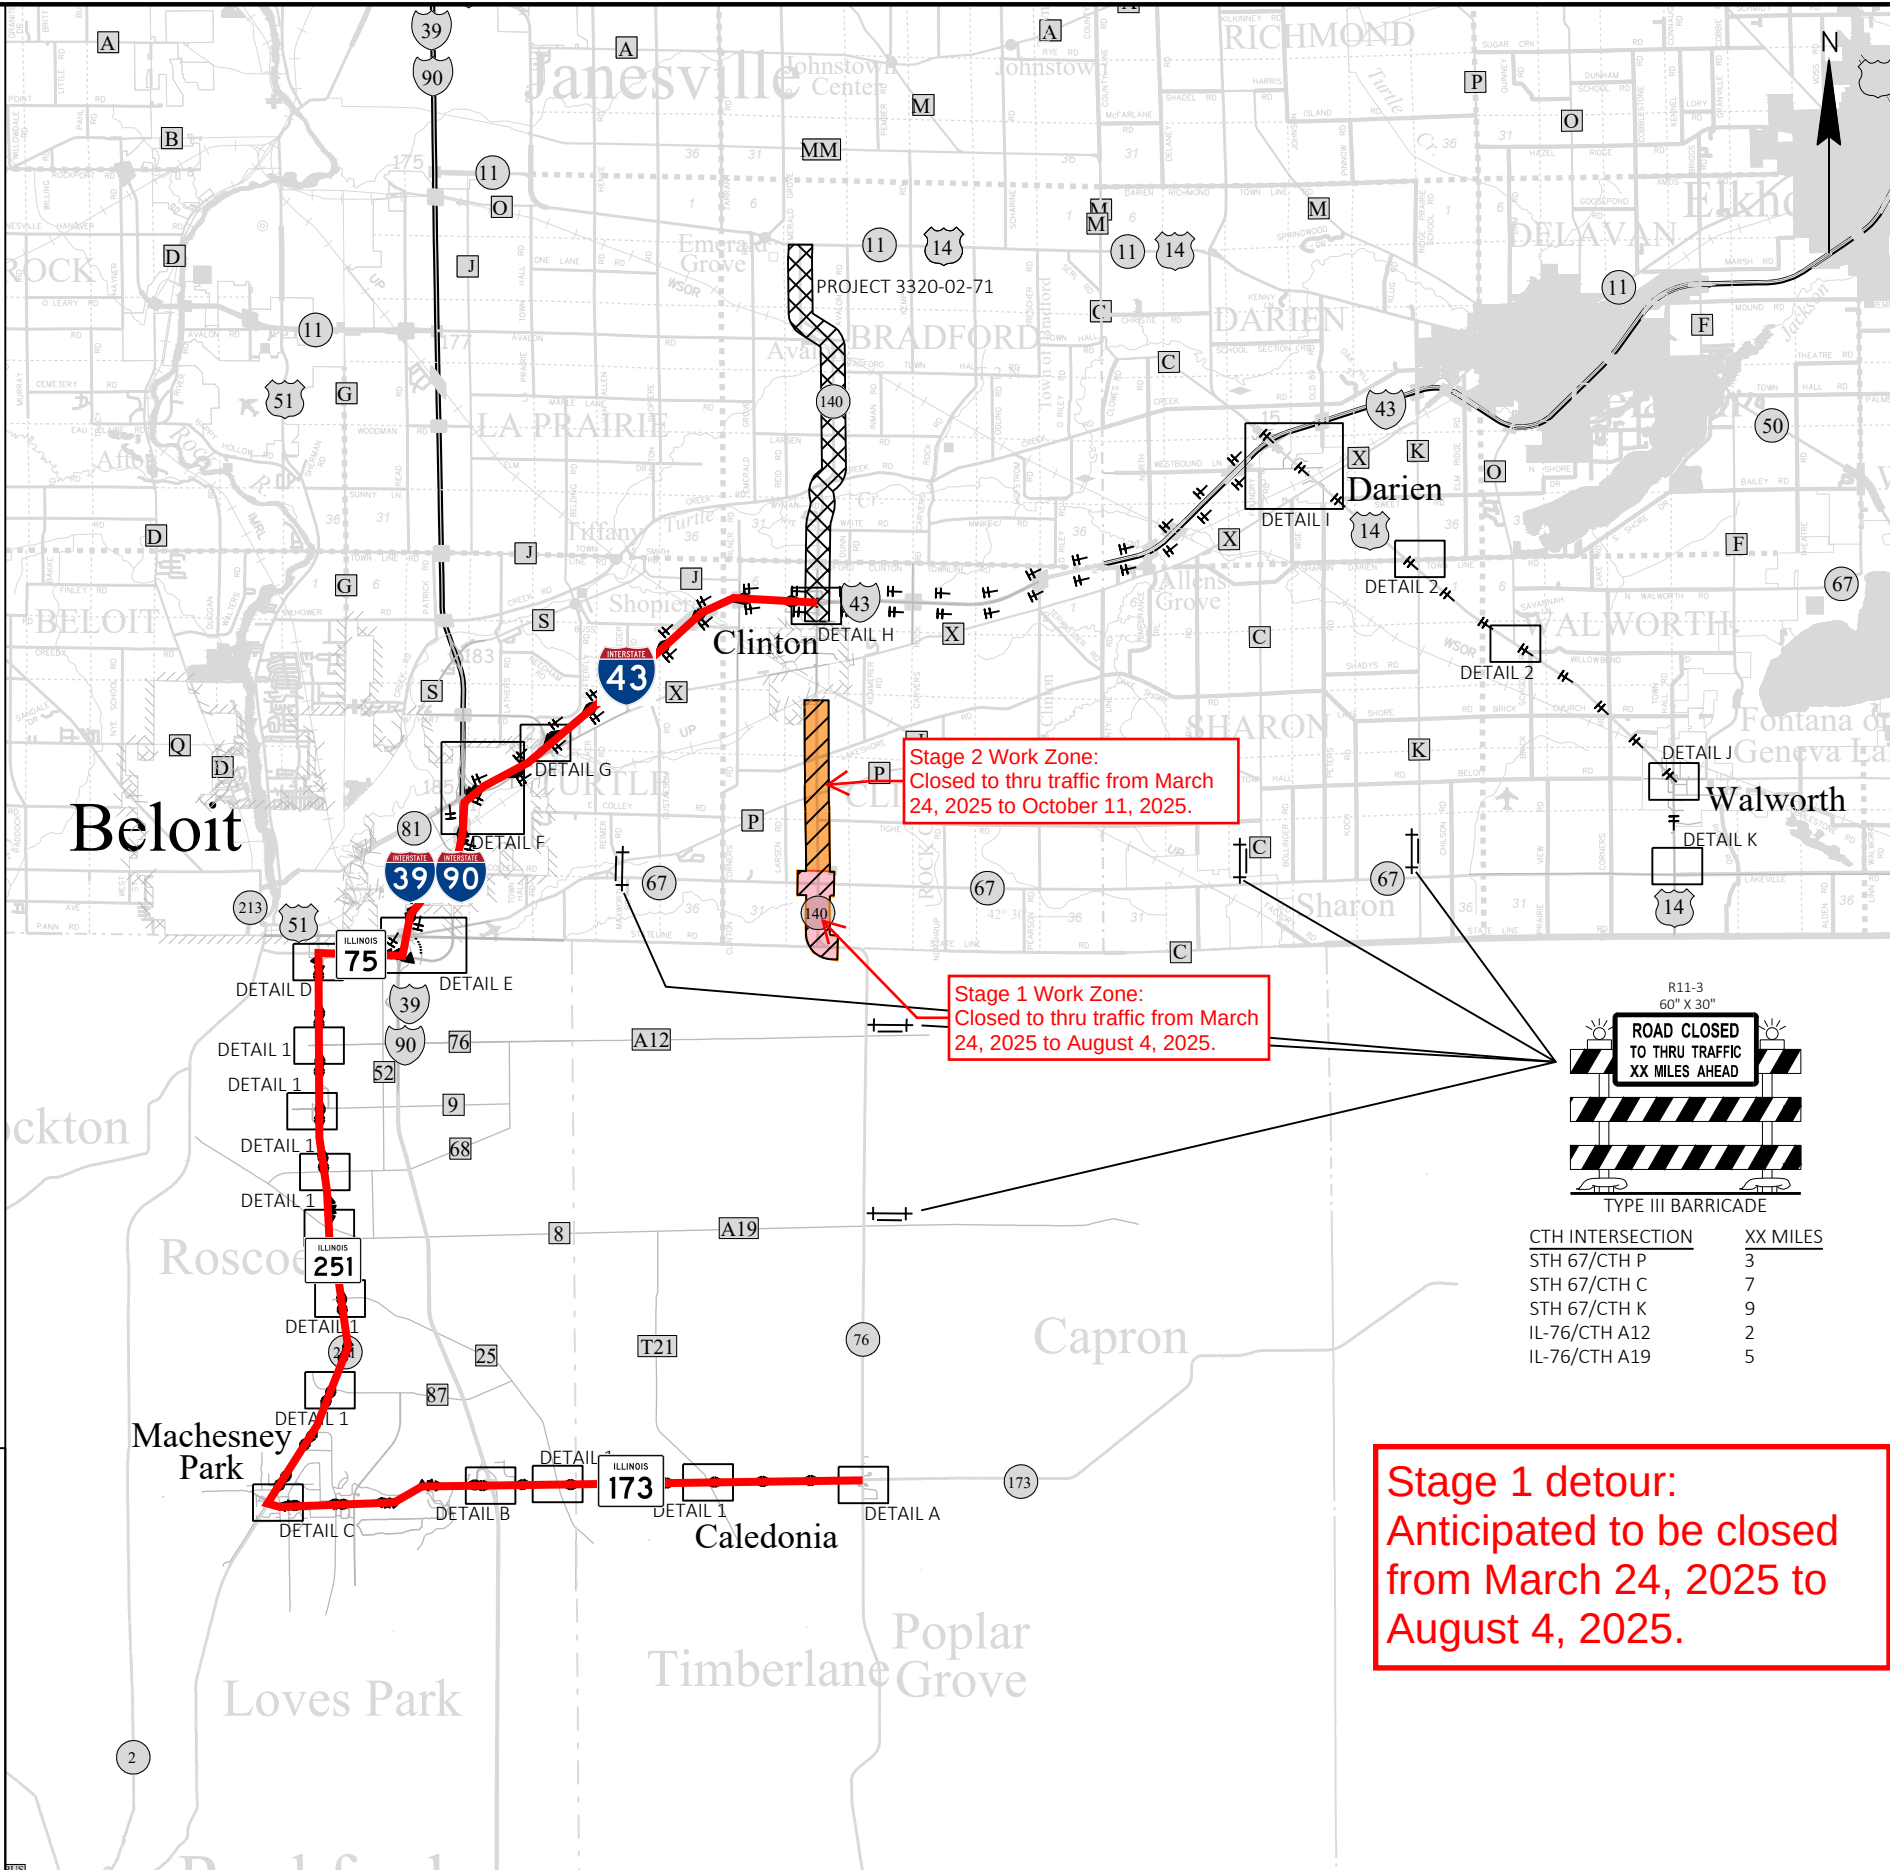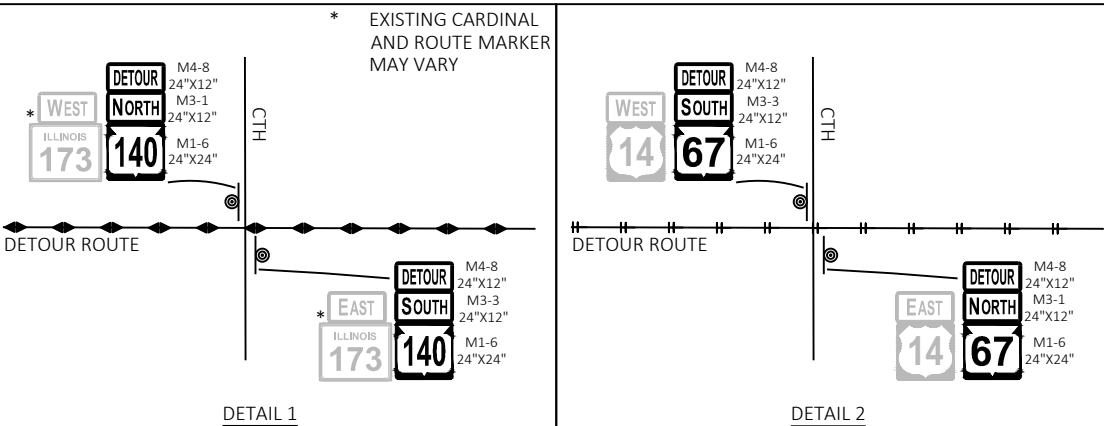

CTH INTERSECTION	XX MILES
STH 67/CTH P	3
STH 67/CTH C	7
STH 67/CTH K	9
IL-76/CTH A12	2
IL-76/CTH A19	5

Stage 1 detour:
Anticipated to be closed
from March 24, 2025 to
August 4, 2025.

PROJECT NO: 3320-02-70

HWY: STH 140

COUNTY: ROCK

DETOUR PLAN - STAGE 1 - STH 140 & STH 67

SHEET

99

E

2

- LEGEND
- ◆ STH 140 DETOUR ROUTE
 - STH 67 DETOUR ROUTE
 - ▨ WORK AREA
 - ▤ NEARBY PROJECT WORK AREA
 - ⊙ TC SIGN ON POST
 - ⊞ EXISTING TYPE II SIGN LOCATION
 - ▤ EXISTING FULL SPAN SIGN BRIDGE
 - EXISTING CANTILEVER SIGN BRIDGE
 - ⊞ TC BARRICADE TYPE III WITH TC SIGN
 - * TC SIGN ON LEFT SIGN BRIDGE SUPPORT
 - ** TC SIGN ON RIGHT SIGN BRIDGE SUPPORT
 - *** TC SIGN ON LIGHT POLE

NOTES



COORDINATE DETOUR SIGNING WITH PROJECT 3320-02-71 TO ENSURE CONSISTENCY IN DETOUR MESSAGING.

ALL SIGNS 48"X48" UNLESS NOTED.

NOT ALL EXISTING SIGN LOCATIONS ARE SHOWN.

STH 67 DETOUR UTILIZES IH 39, IH 43, AND USH 14.

STH 140 DETOUR UTILIZES IL-173, IL-251, USH 51, IH 39, AND IH 43.

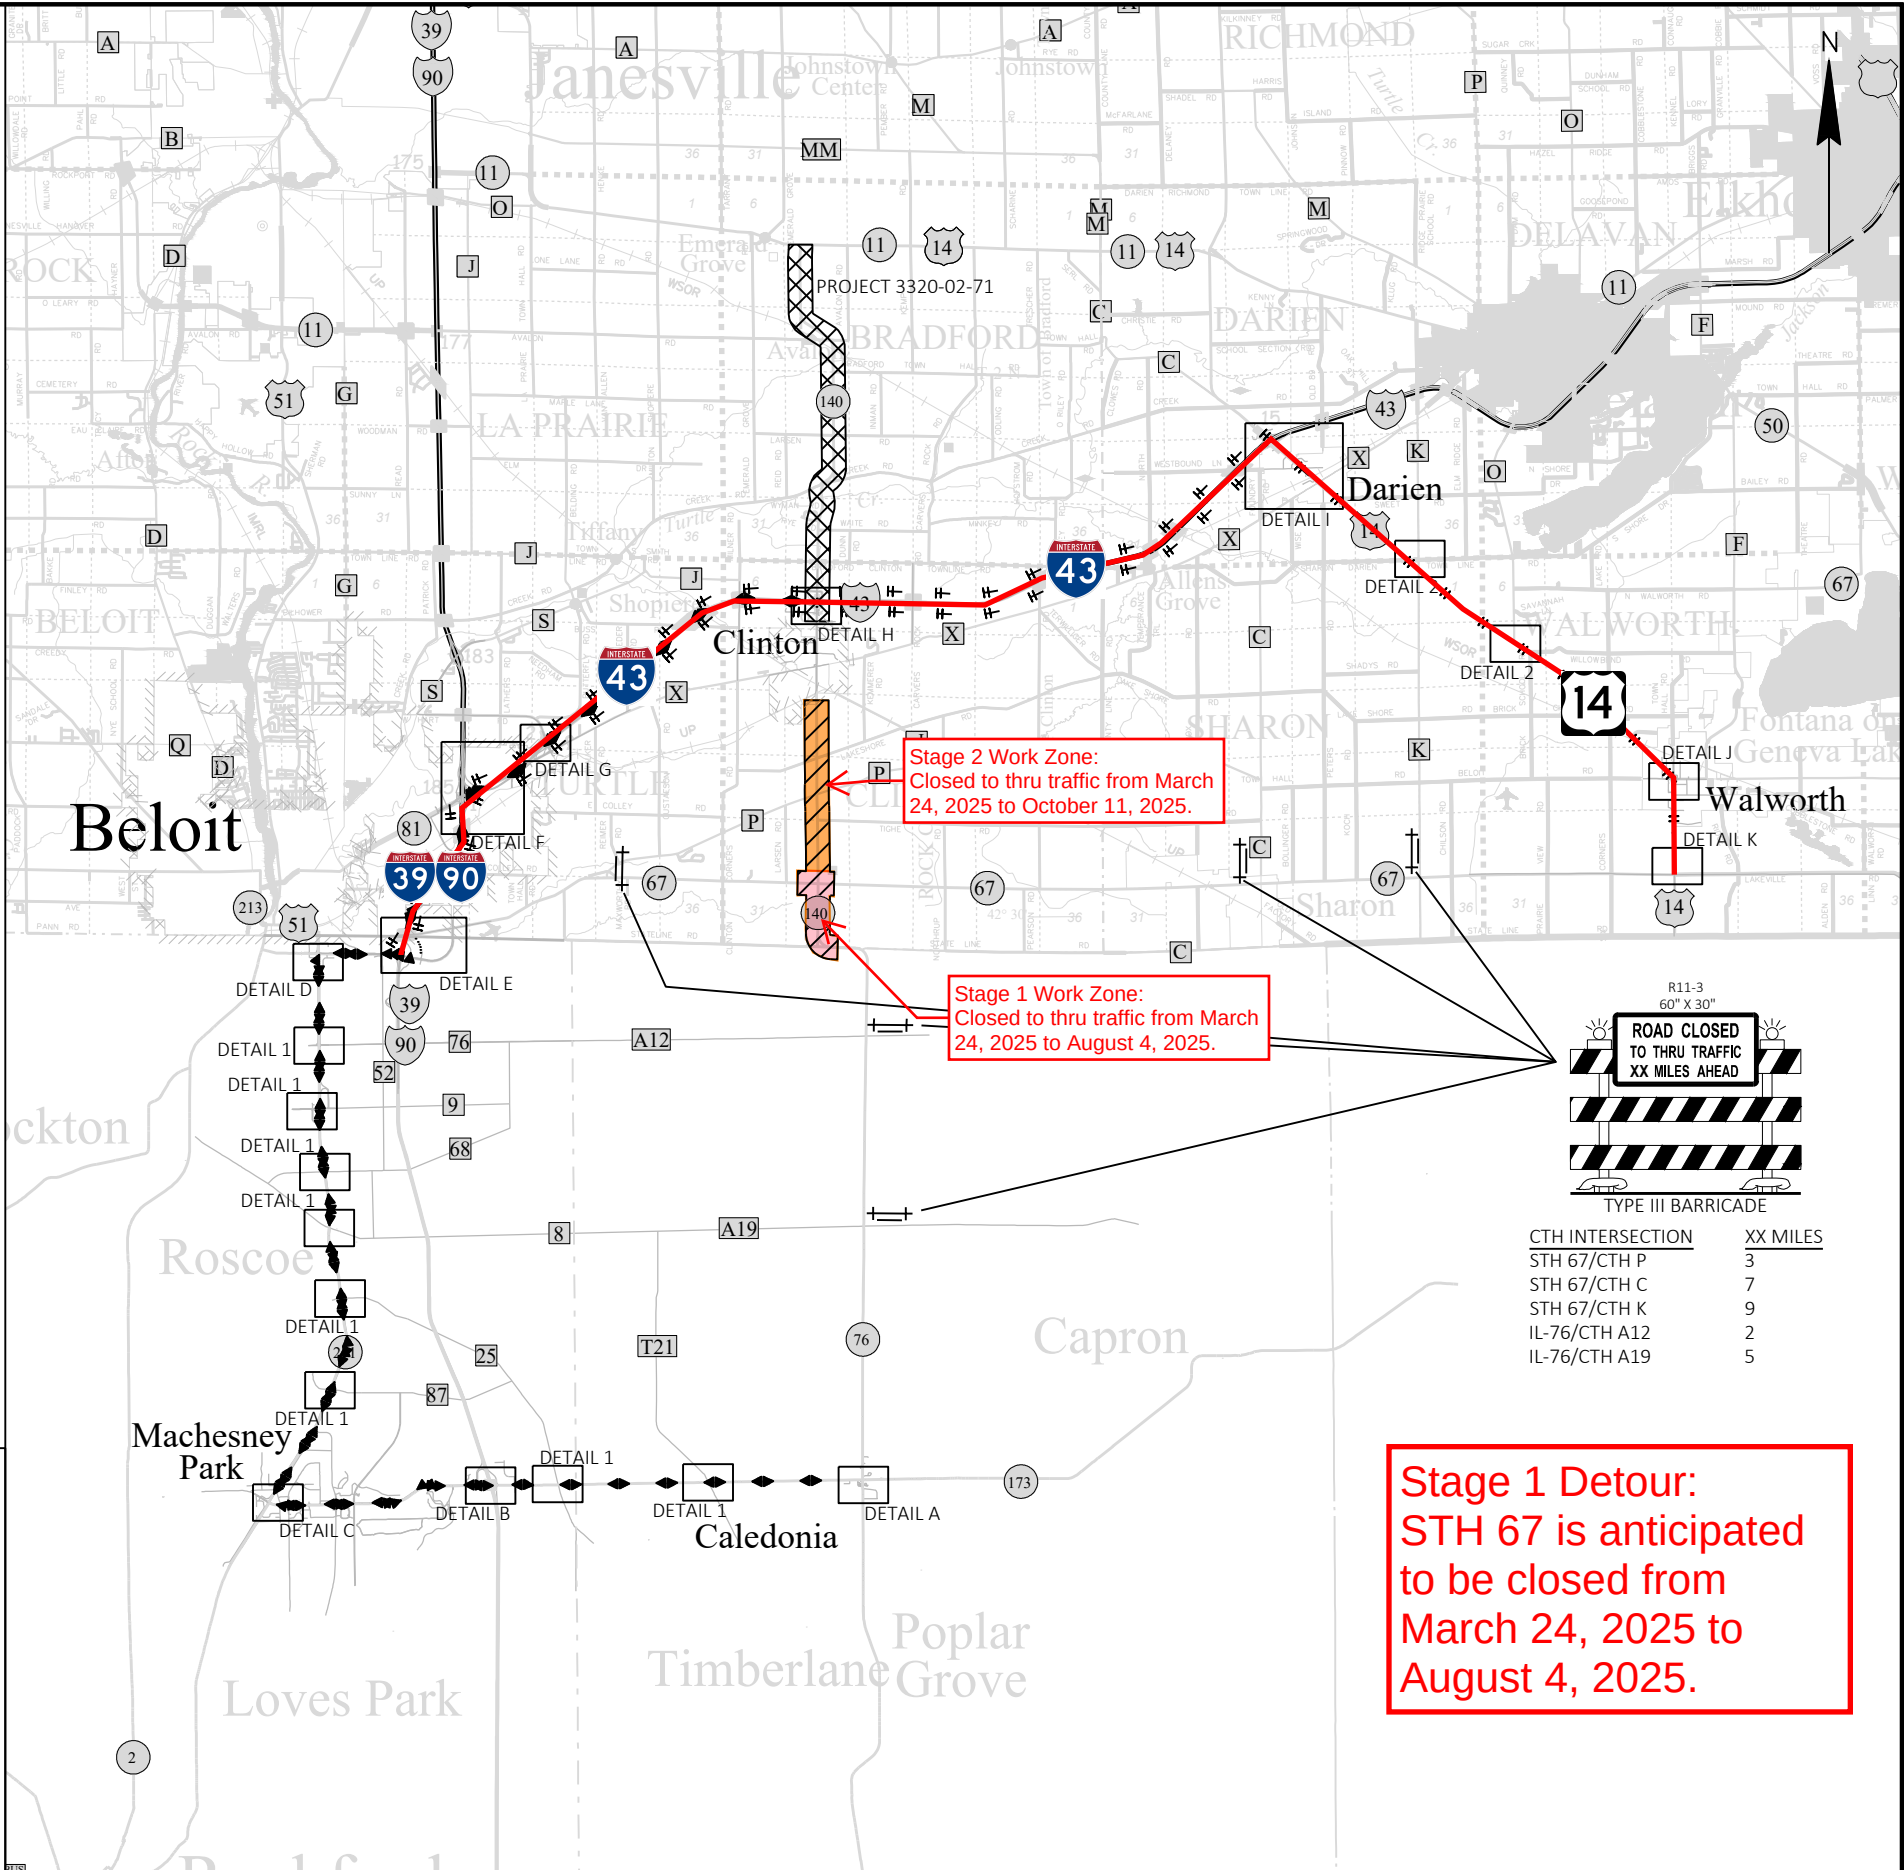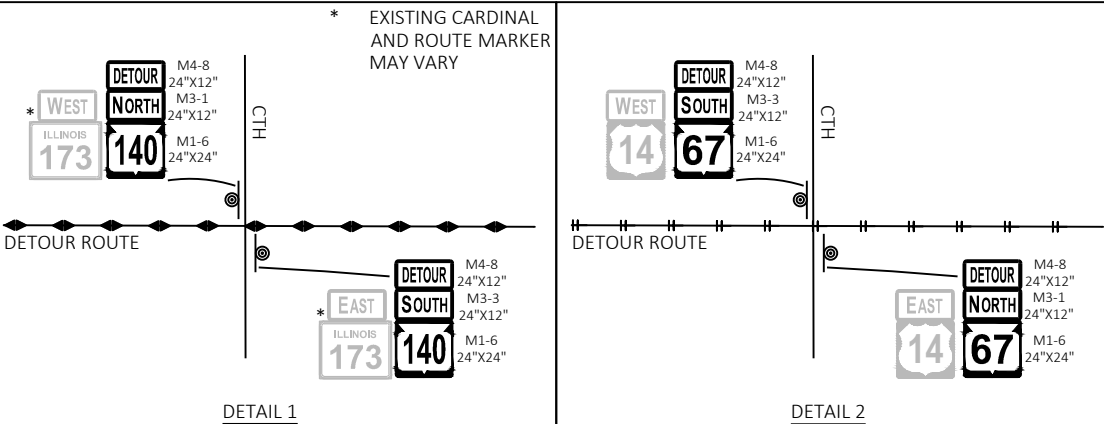

2
