


Stage 3&4

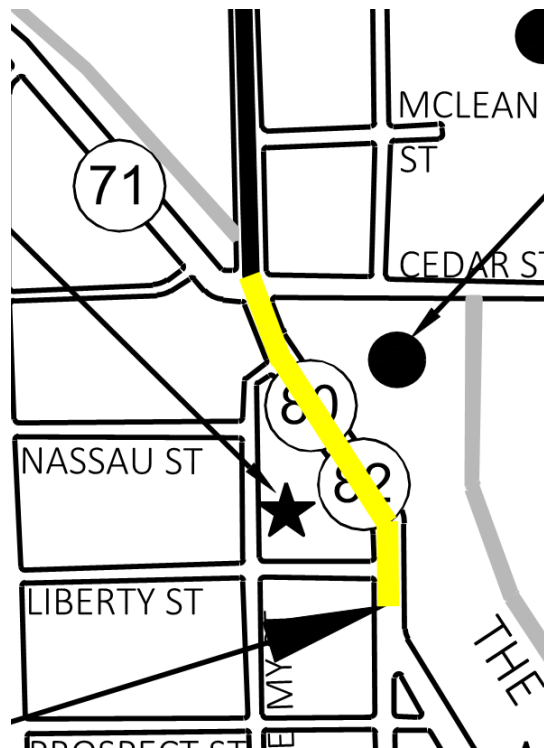

Stage 2

• Work Site

3 Week Look Ahead

We are going to be looking at finishing up most of stage 3 and 4 along with stage 2A in the next couple of weeks. Paving for stage 3 and 4 is scheduled for next week. When doing so we will be temporarily closing down the Tilmar and Kimball St intersections, but not at the same time. Once paved and cooled they will be reopened. Paving for stage 2 is scheduled for the beginning of the week of Oct. 19th. Once stage 2 is paved we will be switching traffic to the west side of Academy street and doing our last stage (2B) on the east side. Also, once traffic is switched, the current detour on County PP will now be off and traffic will be running back on WIS 71. We will be closing just the intersection of Academy St. and County PP for grading purposes once the detour is off. Once grading and paving is done County PP will be reopened. We will maintain access to your homes but when work is going on directly in front of your property or concrete is curing, vehicles will have to be parked elsewhere. If you have access to WIS 80, access will be restored once work is past your driveway. If you are disabled or have other health issues, please feel free to get a hold of me. My information is listed below, and the crew onsite will work with you to figure out a solution. Thank you for your cooperation.



Trae Ness

608.387.0621 Cell

tpn@gerkeexcavating.com
