
June 1-June 17, 2018

WisDOT

- » Freeway work zone prep complete on June 9, 2018
- » Frontage roads between KR and WIS 20 complete or very near completion
- » WIS 20, CTH H, and CTH A resurfacing complete

Foxconn

- » Continued mobilization
- » Site work, Phase 1a
- » LCM construction, Phase 1b

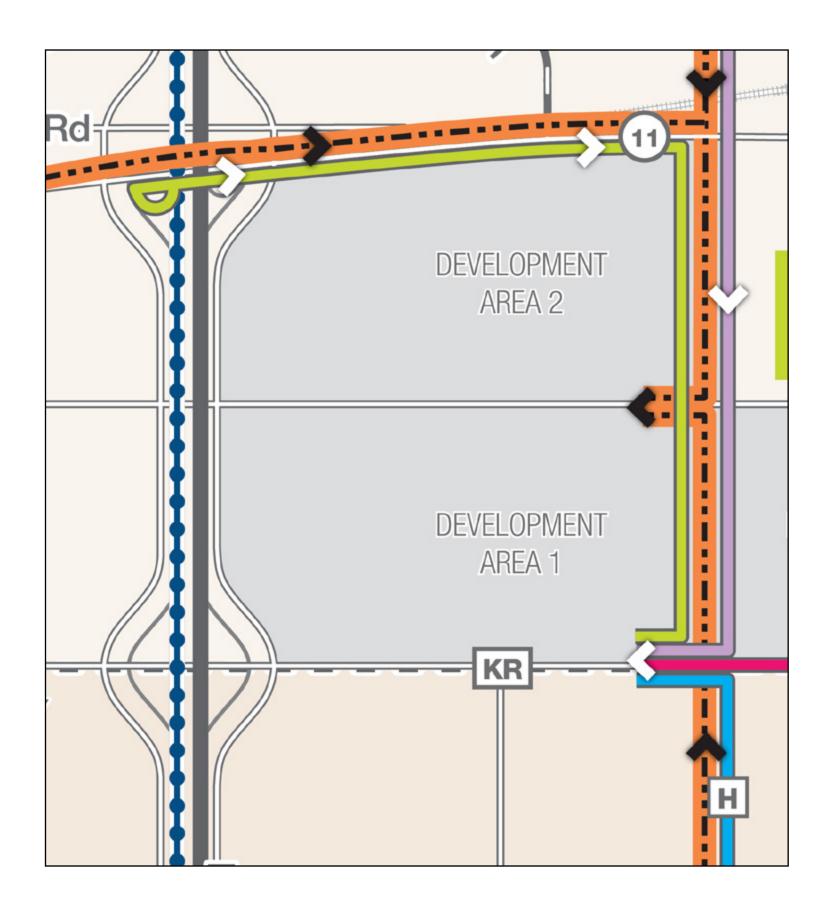

LEGEND

••• Freeway or development road construction

ACCESS ROUTES

General access route (workers)


Haul route

Return trips to the west shall use the controlled intersection at County H/WIS 11

CLOSURES

Roadway closed (under I-94 mainline)

Ramp closed (I-94 entrance/exit)

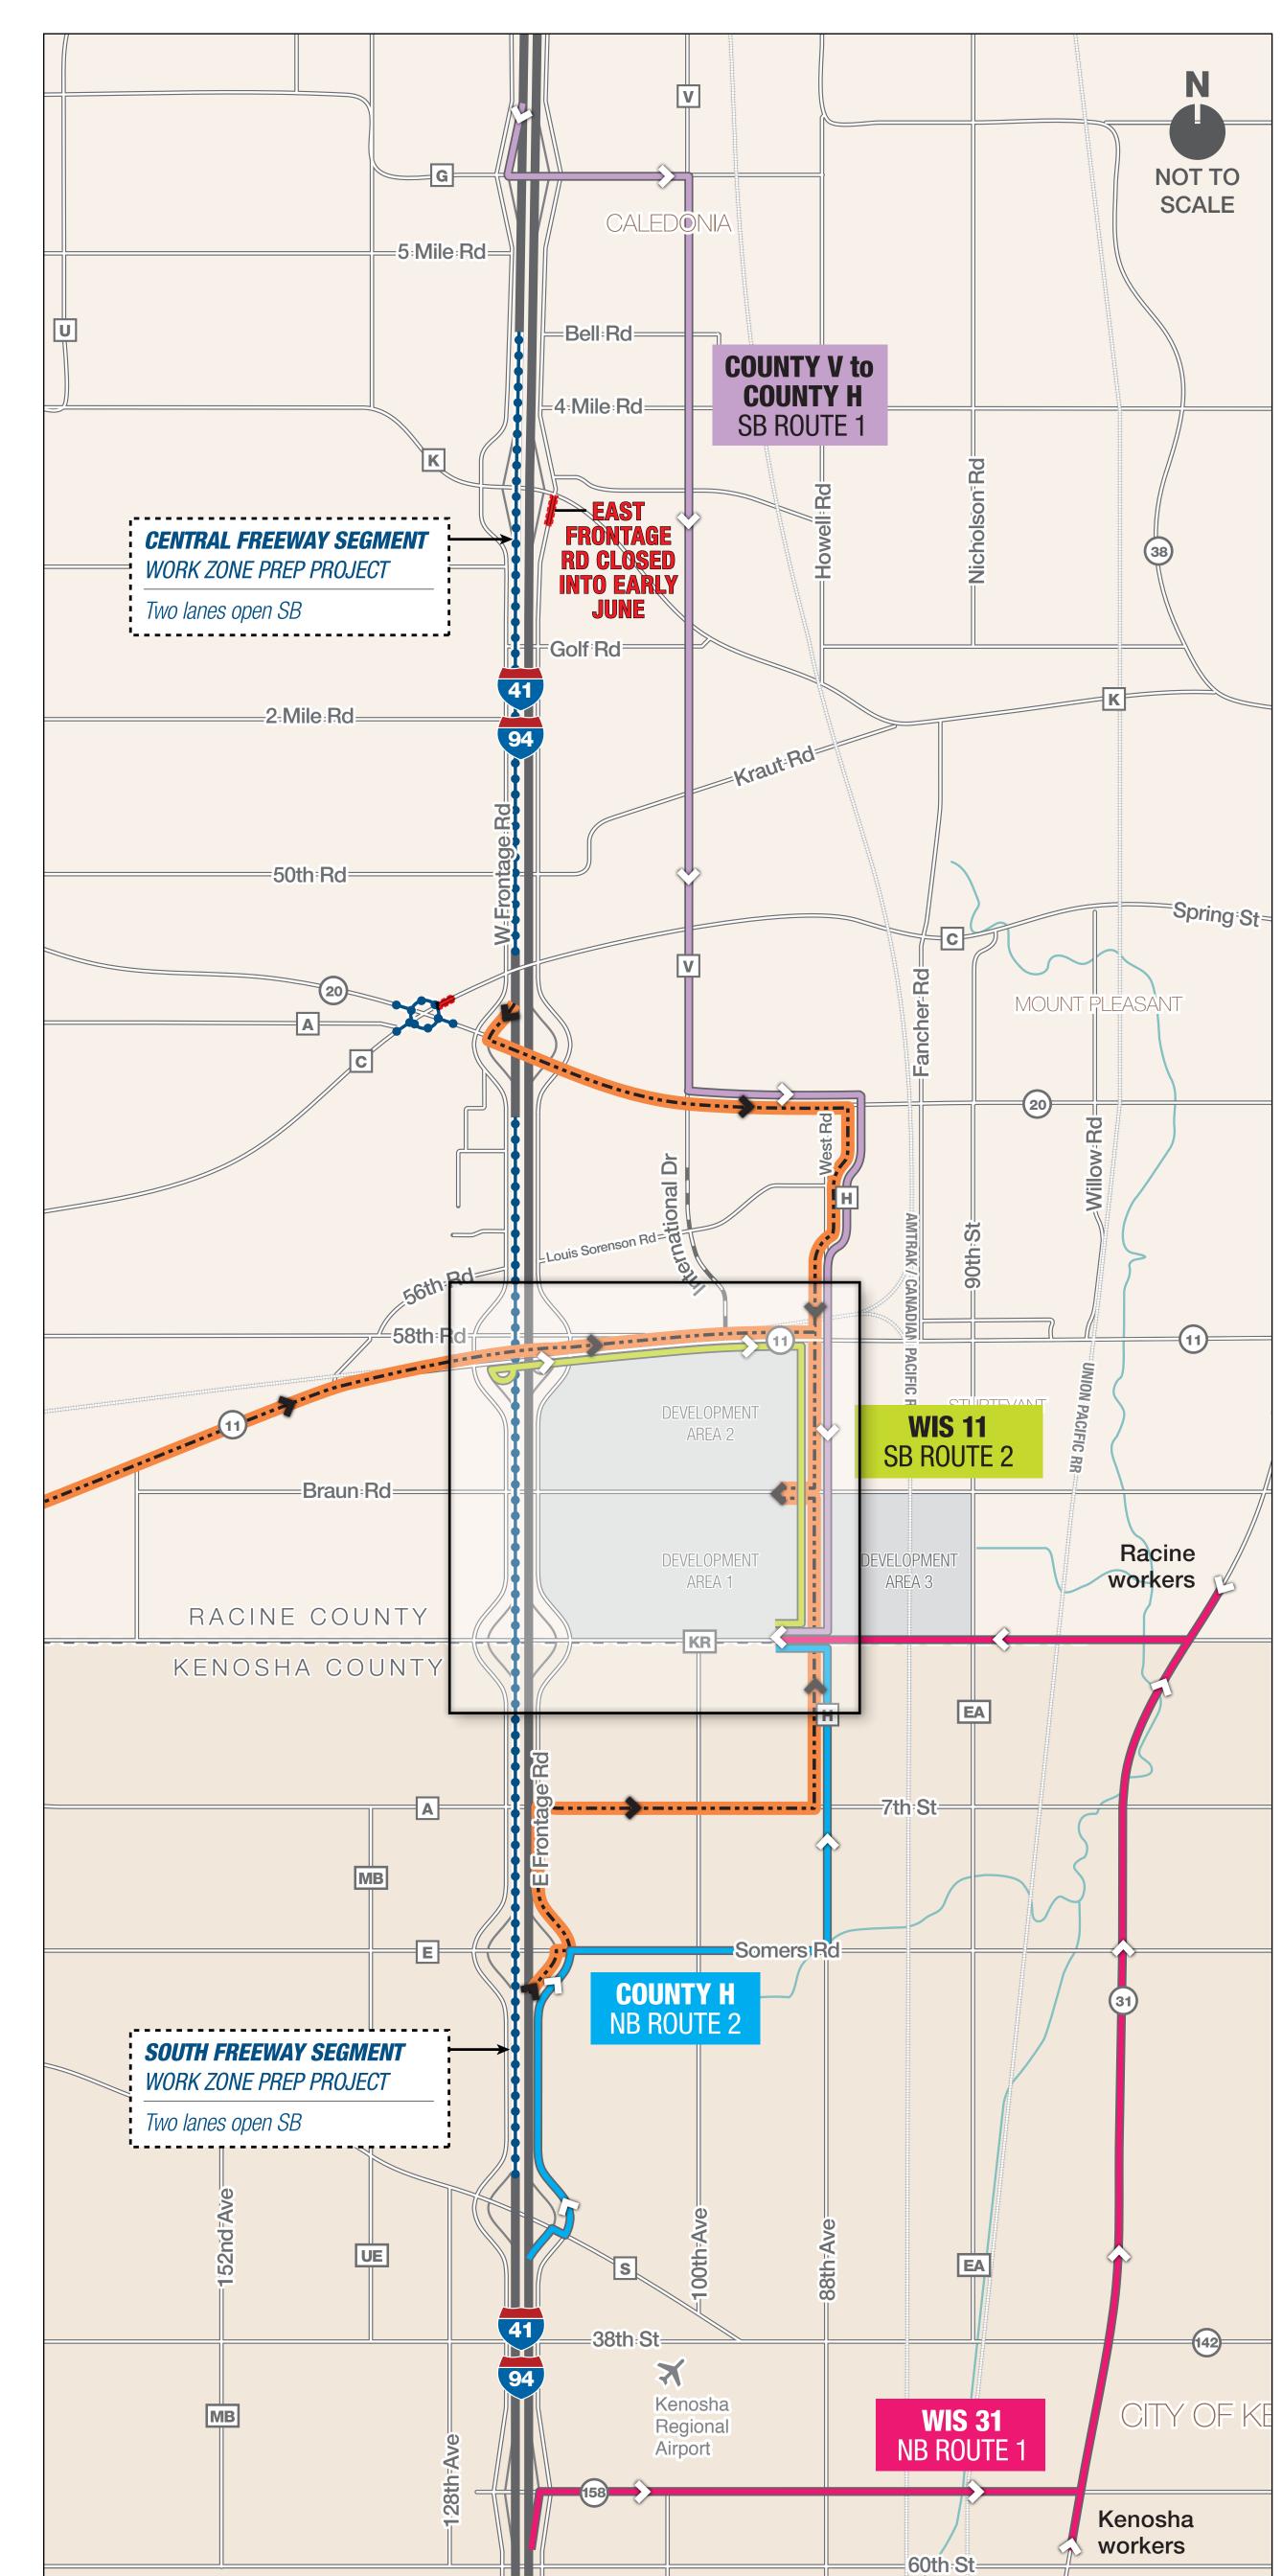








June 18-July 31, 2018

WisDOT

- » Freeway NB reconstruction
- » Braun Rd EB reconstruction
- » International Dr NB construction

Foxconn

- » Continued mobilization
- » Site work, Phase 1a
- » LCM construction, Phase 1b

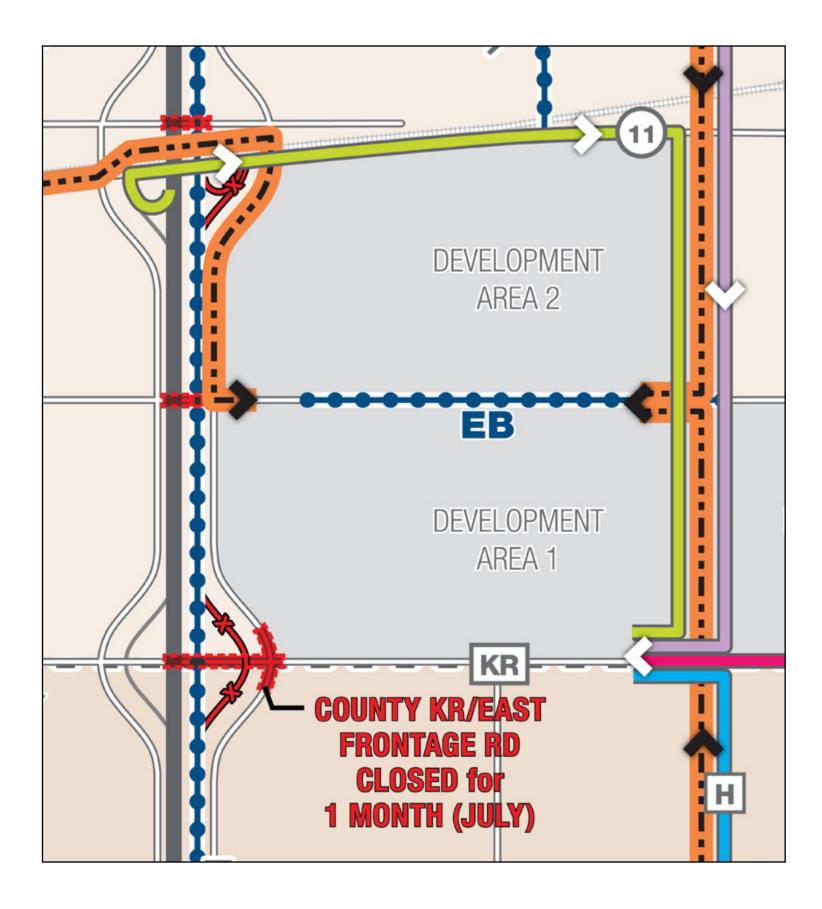

LEGEND

••• Freeway or development road construction

ACCESS ROUTES

General access route (workers)


Haul route

Return trips to the west shall use the controlled intersection at County H/WIS 11

CLOSURES

Roadway closed (under I-94 mainline)

Ramp closed (I-94 entrance/exit)

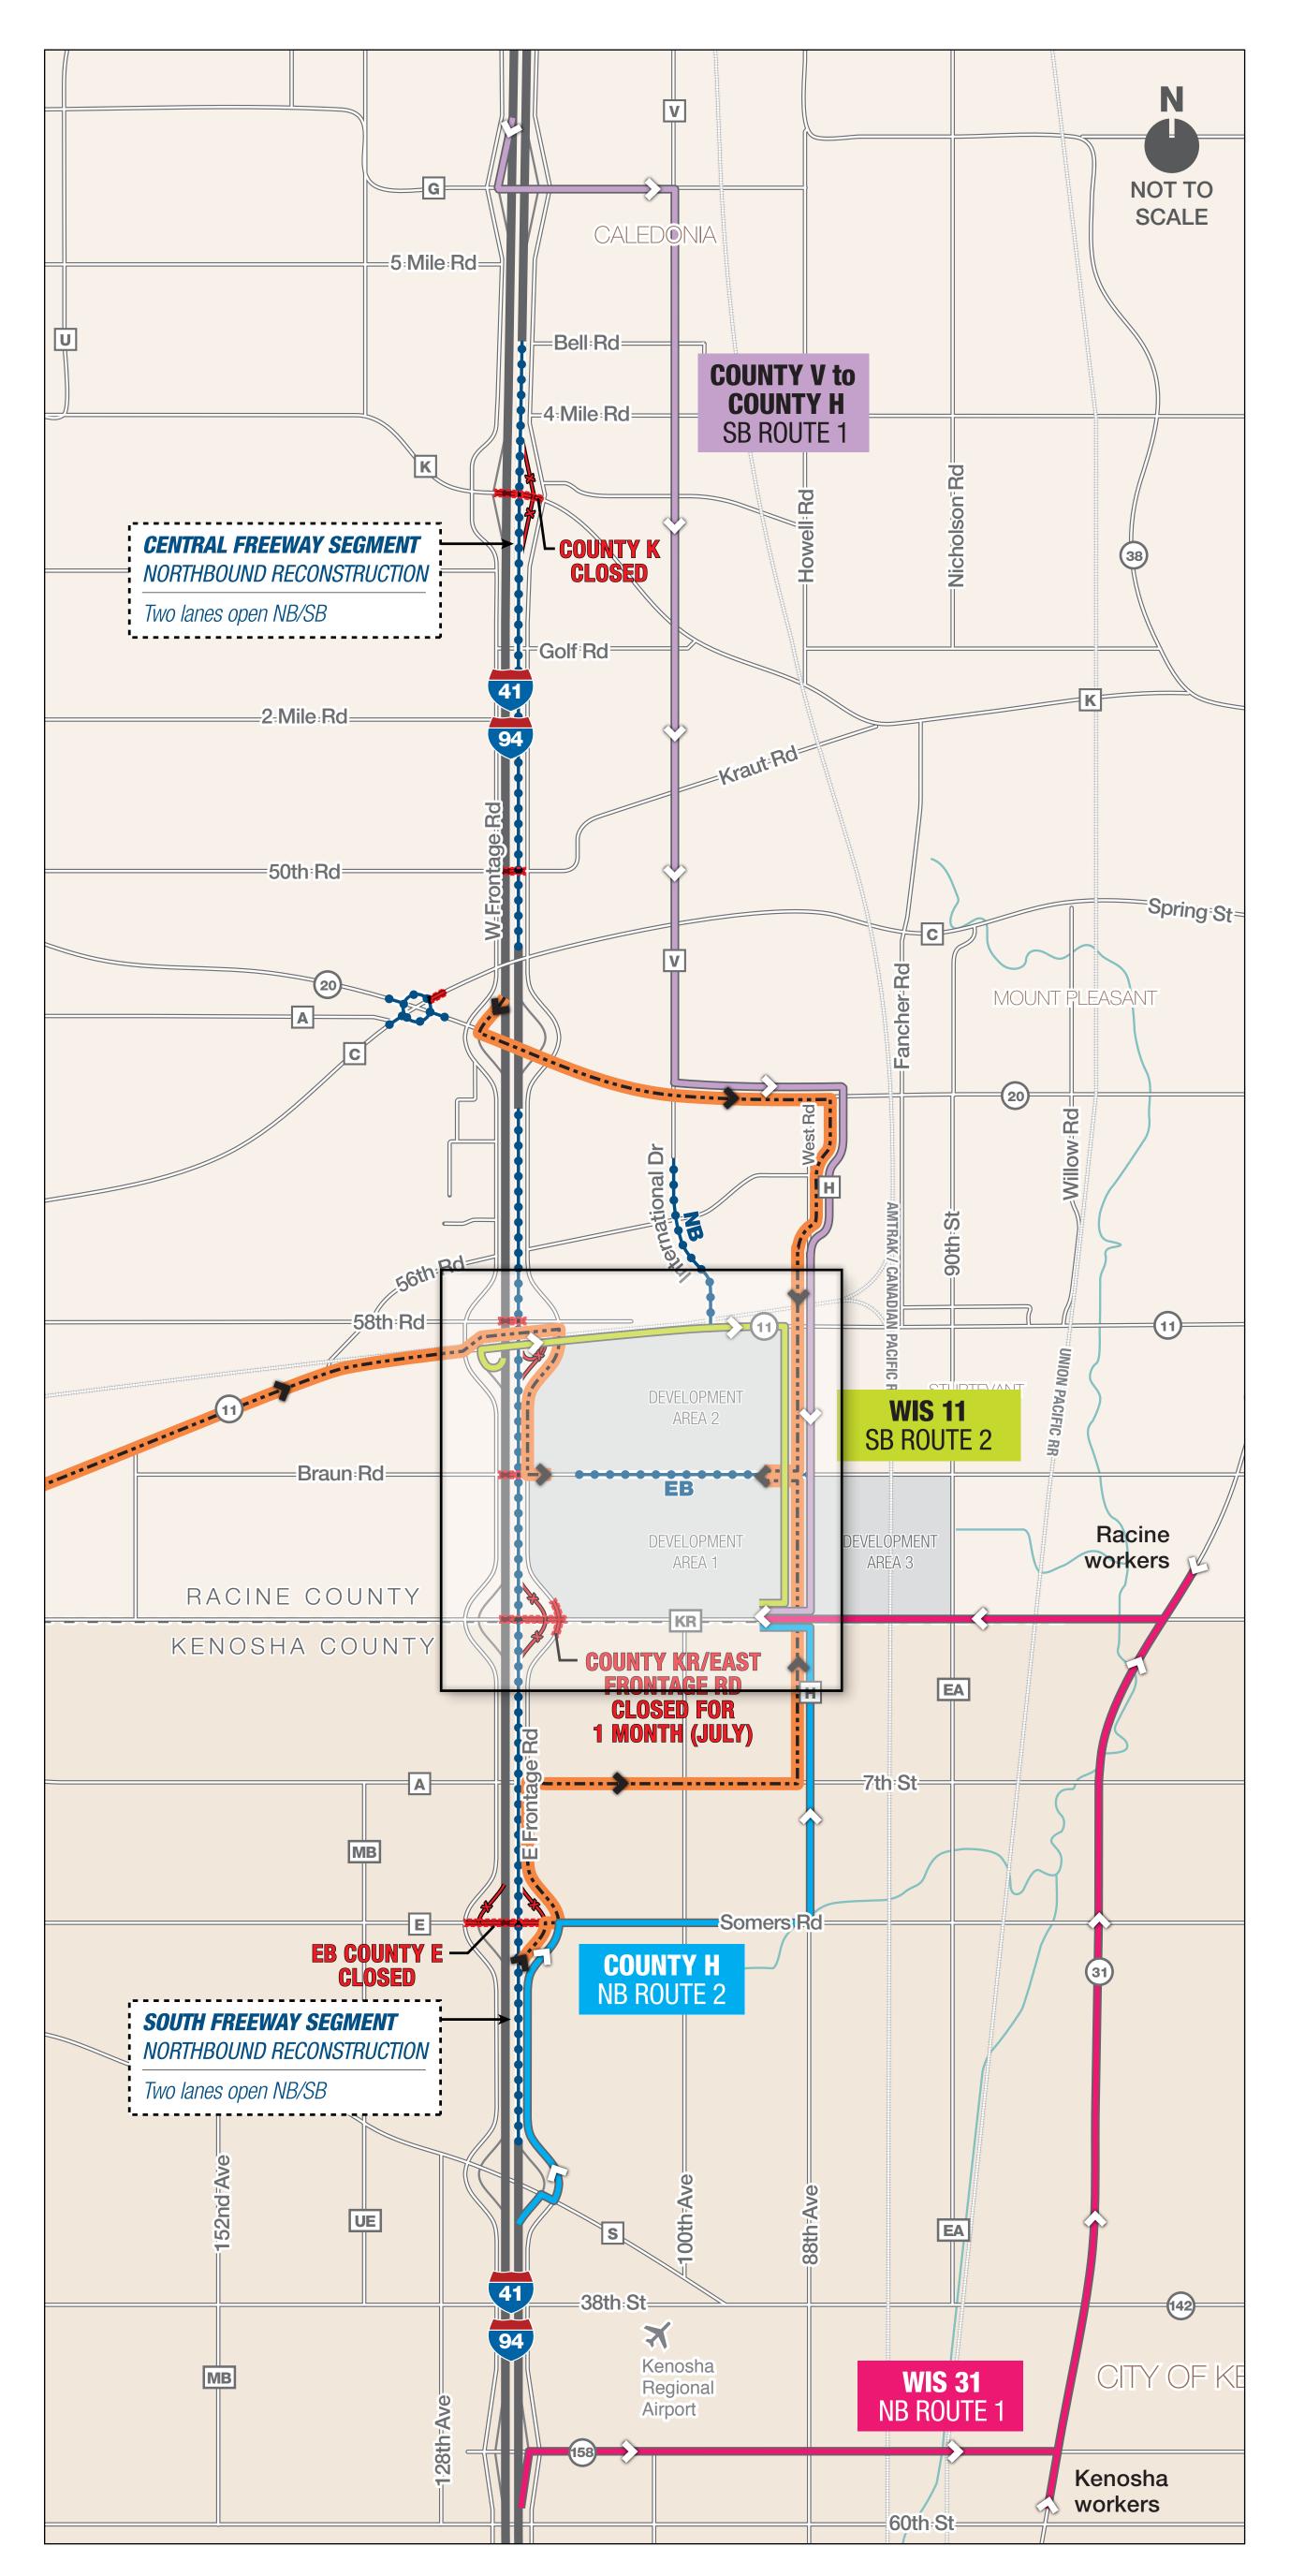








August 1-August 30, 2018

WisDOT

- » Freeway NB reconstruction
- » Braun Rd box culvert reconstruction
- » Braun Rd EB reconstruction
- » International Dr NB construction

Foxconn

- » Continued mobilization
- » Site work, Phase 1a
- » LCM construction, Phase 1b

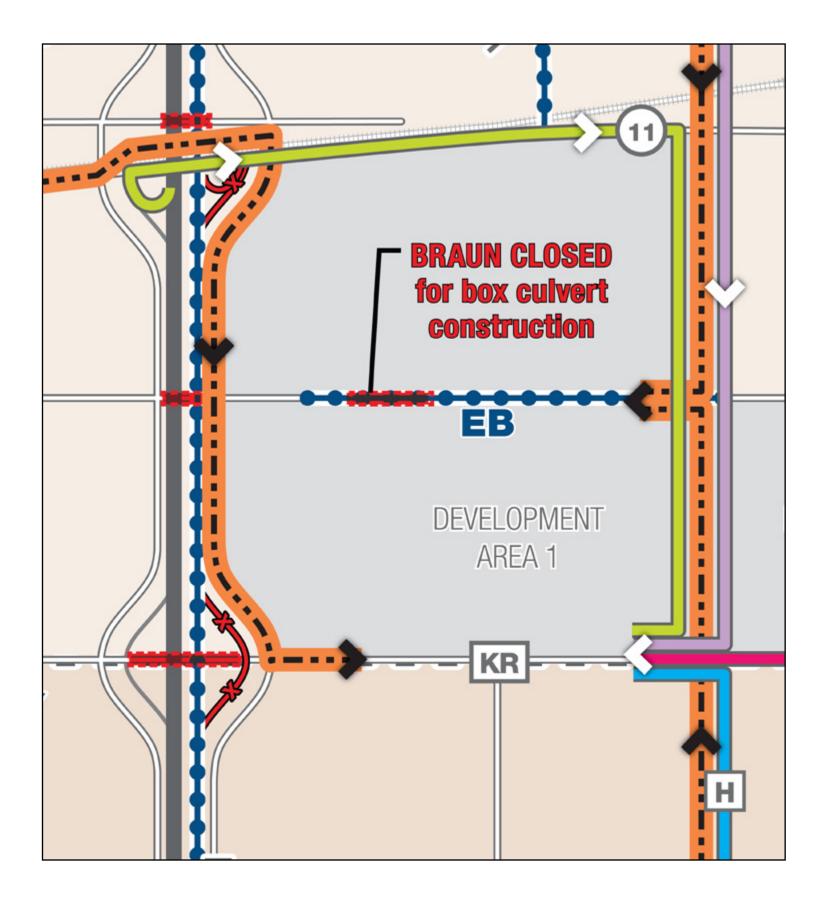

LEGEND

••• Freeway or development road construction

ACCESS ROUTES

General access route (workers)

Haul route

Return trips to the west shall use the controlled intersection at County H/WIS 11

CLOSURES

Roadway closed (under I-94 mainline)

Ramp closed (I-94 entrance/exit)










September-November 2018

WisDOT

- » Freeway NB reconstruction
- County KR box culvert construction
- Braun Rd EB reconstruction
- International Dr NB construction

Foxconn

- Continued mobilization
- Site work, Phase 1a
- LCM construction, Phase 1b
- Batch plant construction

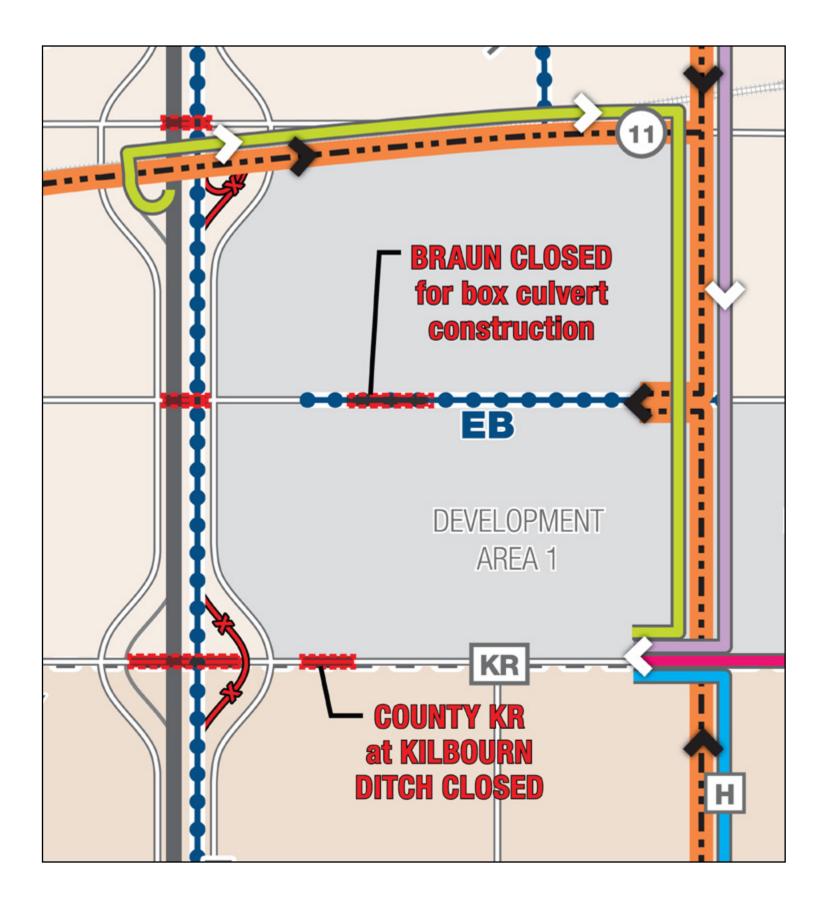

LEGEND

••• Freeway or development road construction

ACCESS ROUTES


General access route (workers)

---> Haul route Return trips to the west shall use the controlled intersection at County H/WIS 11

CLOSURES

Roadway closed (under I-94 mainline)

Ramp closed (I-94 entrance/exit)

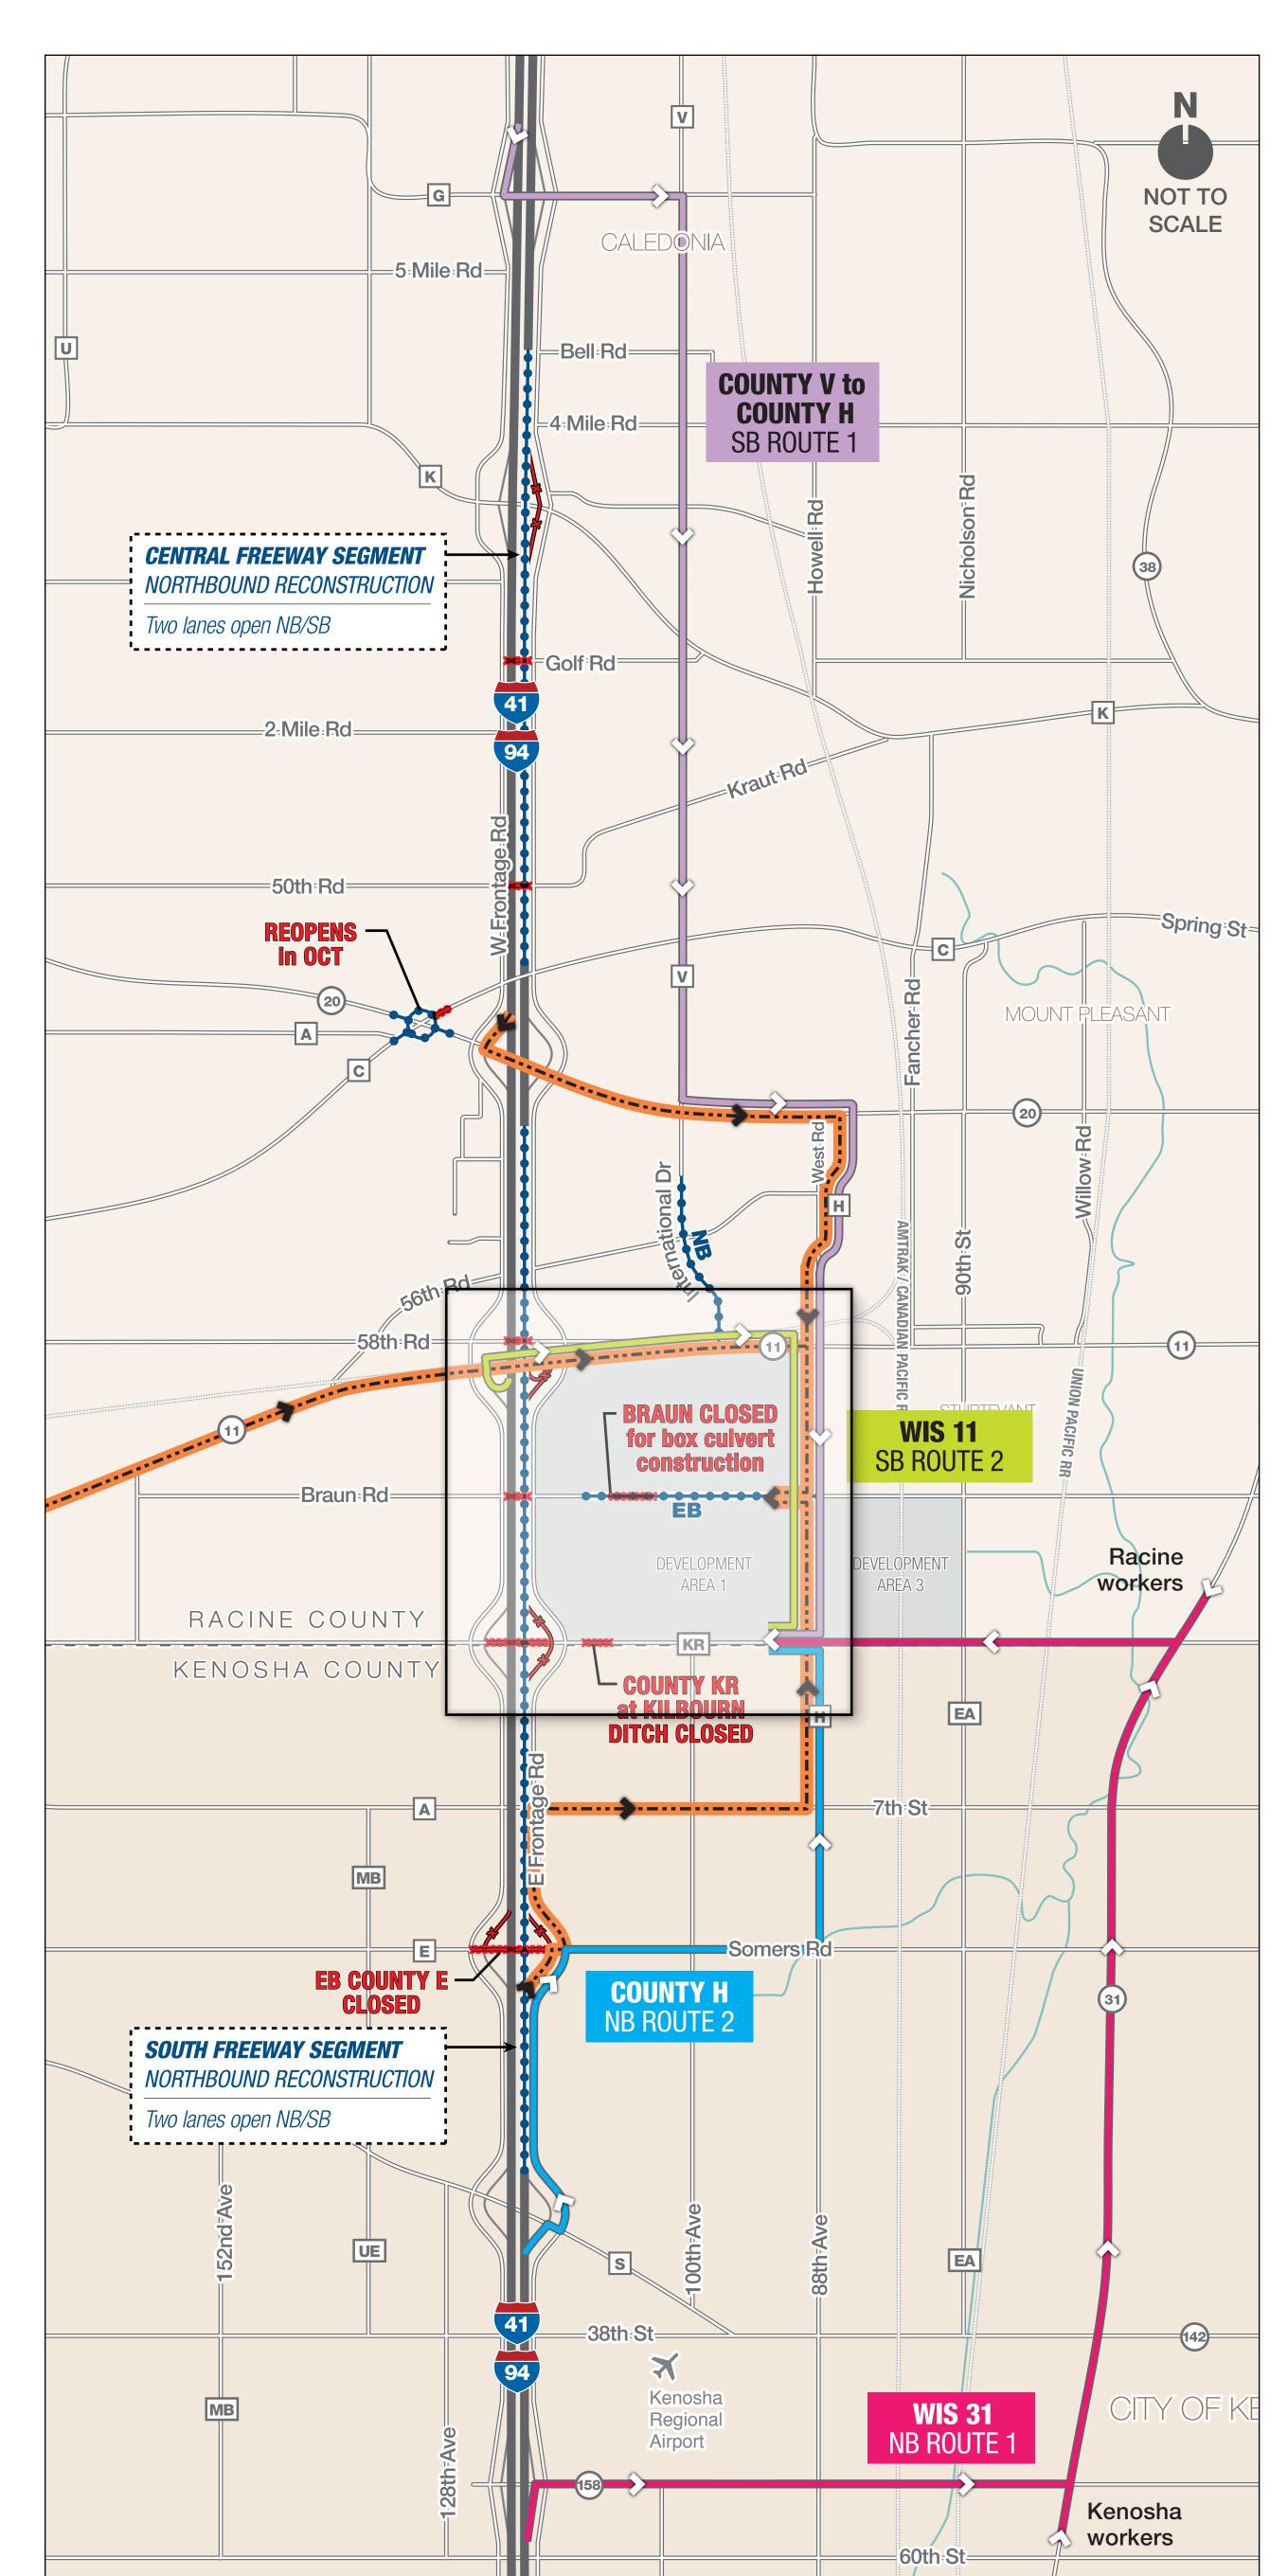






December 2018-January 2019

WisDOT

- » Freeway median reconstruction
- » Braun Rd EB & WB reconstruction
- » International Dr NB & SB construction

Foxconn

» Permanent trucking LCM roadways (Q4 2018)

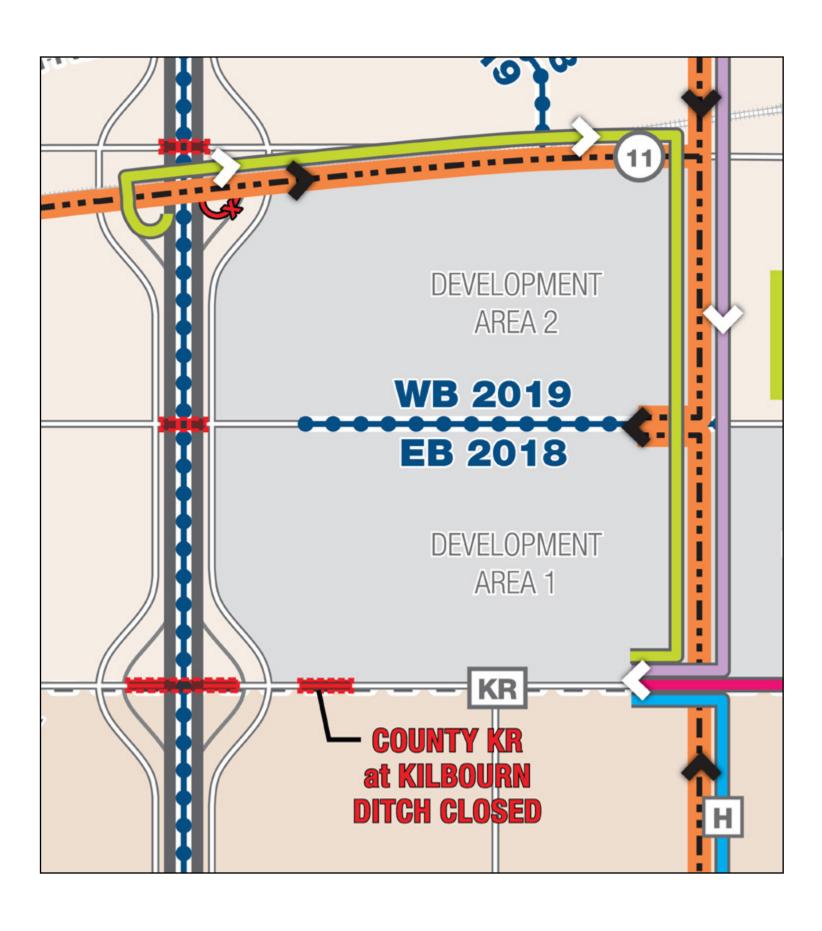

LEGEND

••• Freeway or development road construction

ACCESS ROUTES

General access route (workers)


Haul route

Return trips to the west shall use the controlled intersection at County H/WIS 11

CLOSURES

Roadway closed (under I-94 mainline)

Ramp closed (I-94 entrance/exit)

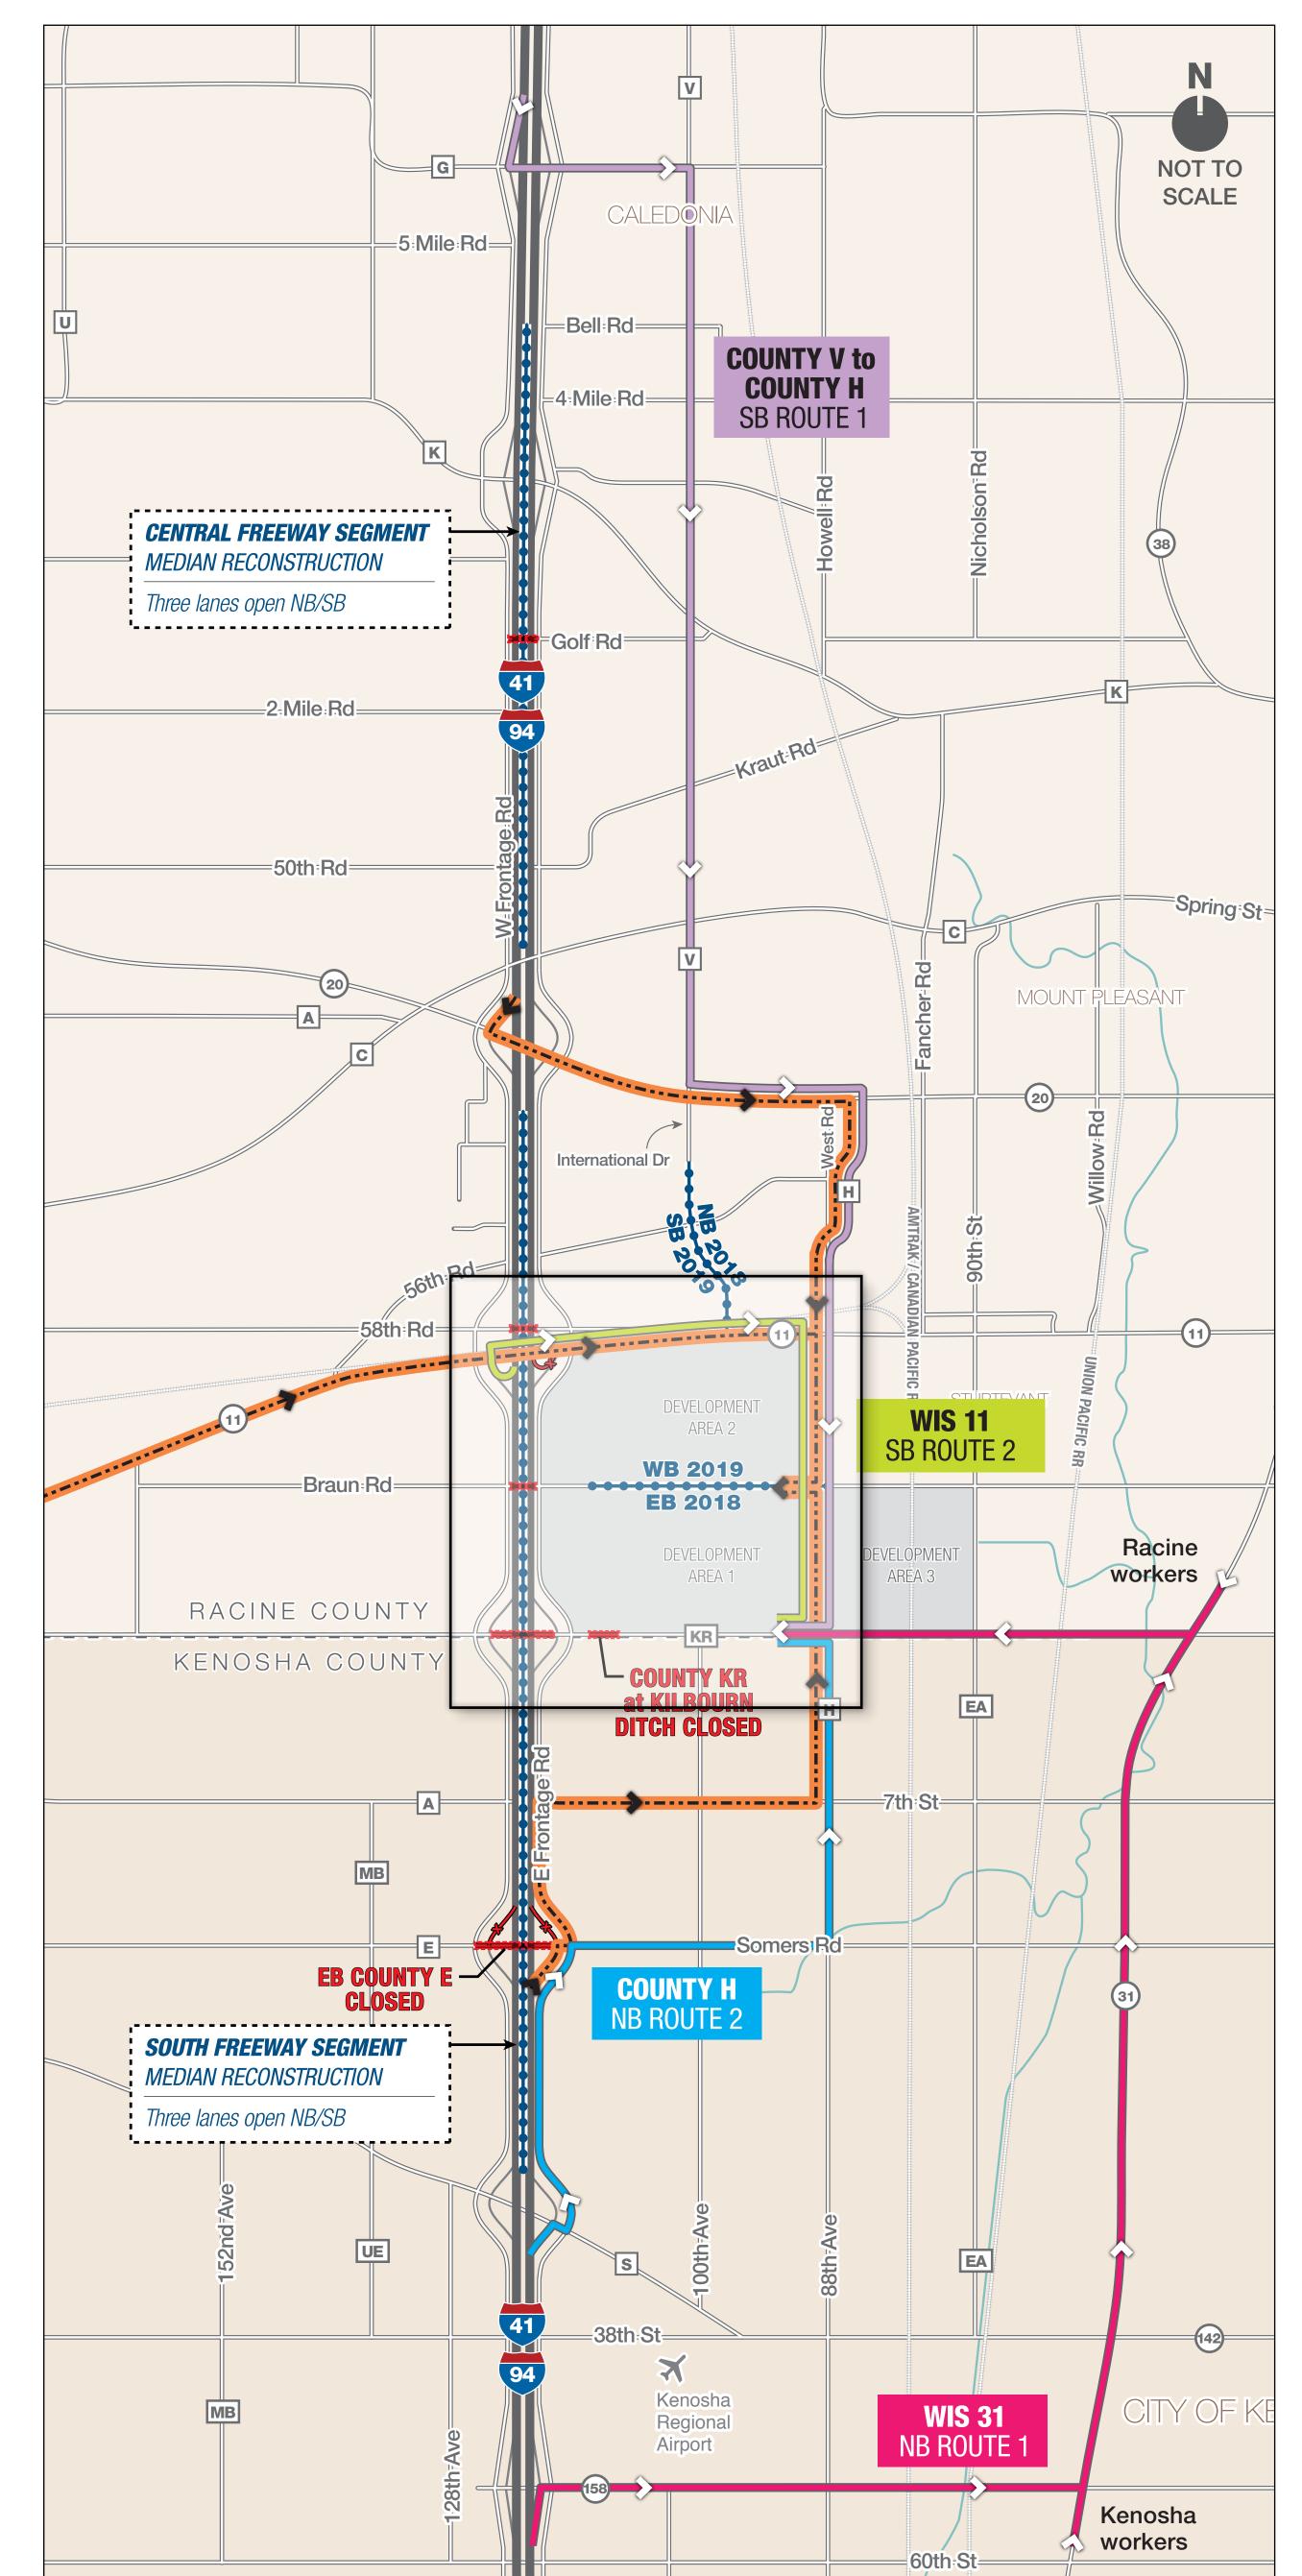








February-April 2019

WisDOT

- » Freeway median reconstruction
- » Braun Rd EB & WB reconstruction
- » County KR EB & WB reconstruction
- » International Dr NB & SB construction

Foxconn

- » LCM ready for equipment (Q1 2019)
- LCD manufacturing, Phase 1 (Q1 2019, foundations start)

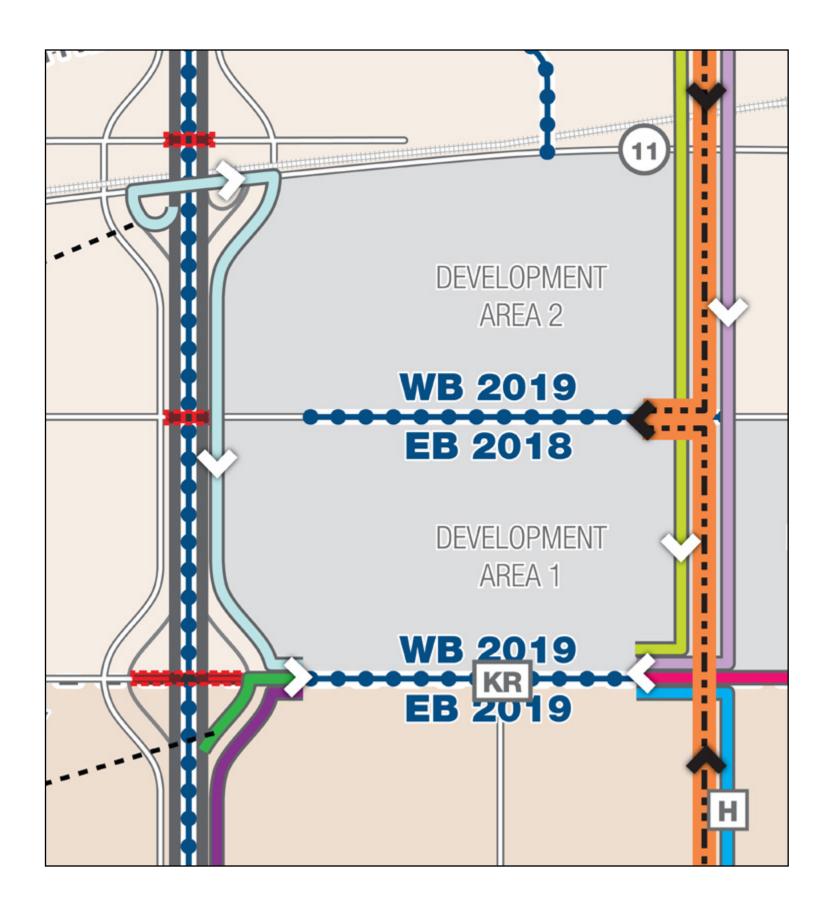

LEGEND

••• Freeway or development road construction

ACCESS ROUTES

General access route (workers)


Haul route

Return trips to the west shall use the controlled intersection at County H/WIS 11

CLOSURES

Roadway closed (under I-94 mainline)

Ramp closed (I-94 entrance/exit)

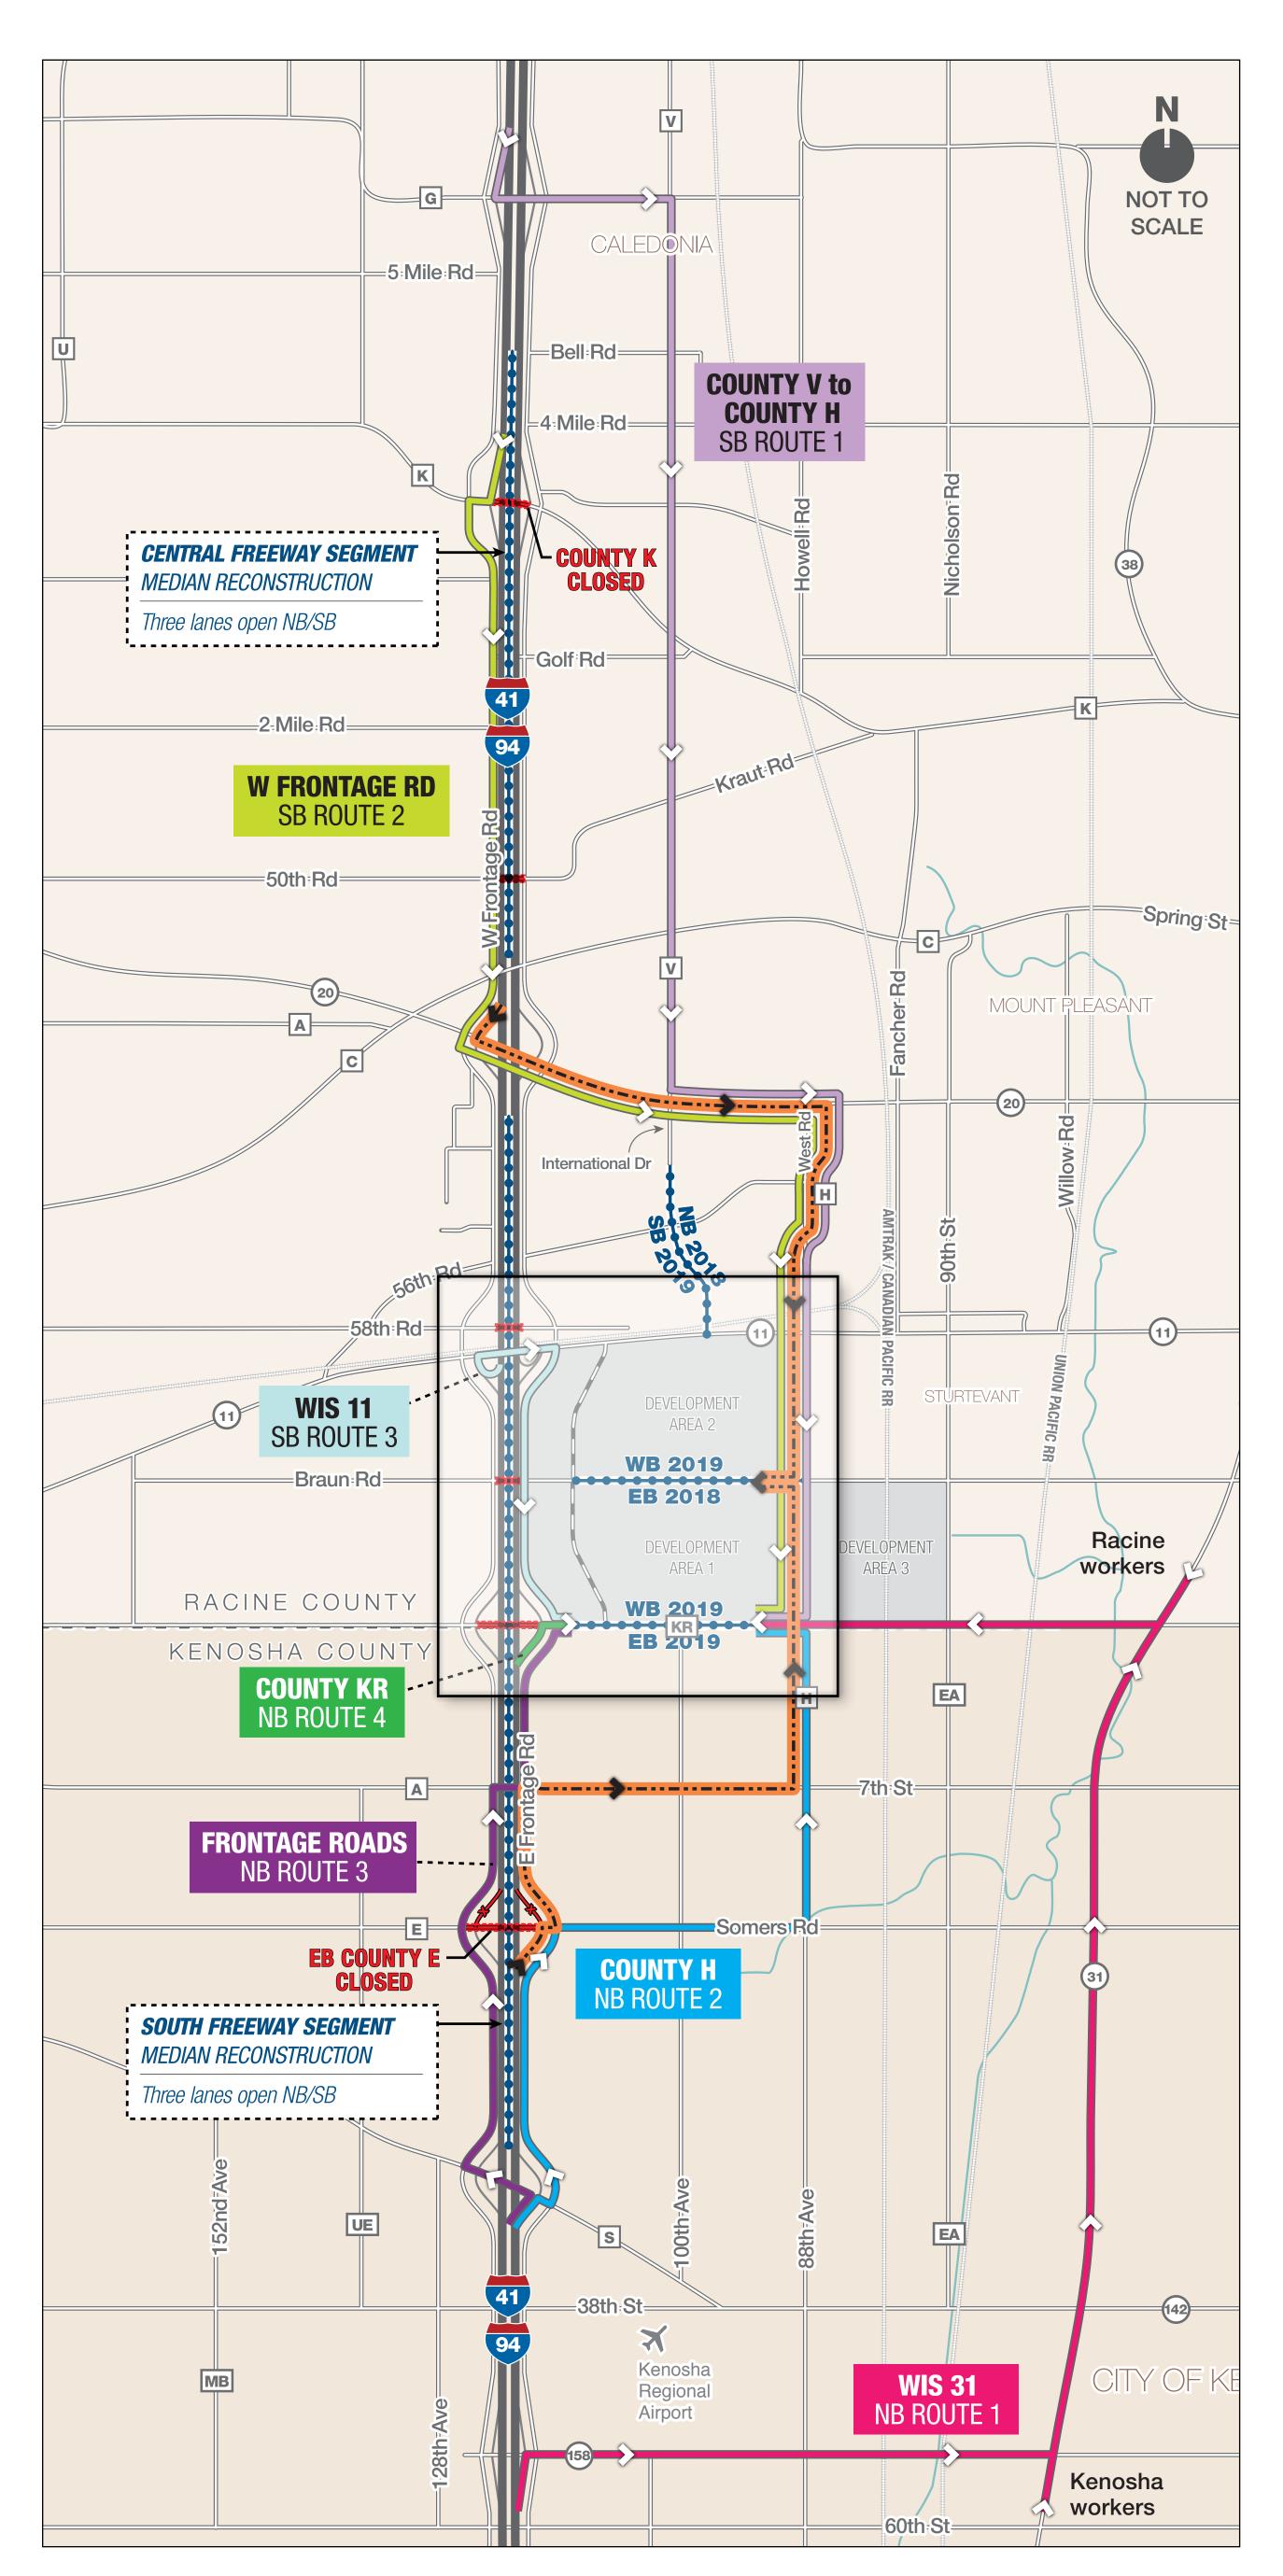








May-November 2019

WisDOT

- » Mainline SB reconstruction
- » WIS 11 EB & WB reconstruction
- » Braun Rd WB reconstruction
- » County KR EB/WB reconstruction
- » Wisconn Valley Way construction

Foxconn

- » Continue Phase 1 construction
- LCD manufacturing, utilities, gas, electric, water, sanitary (Q4 2019)

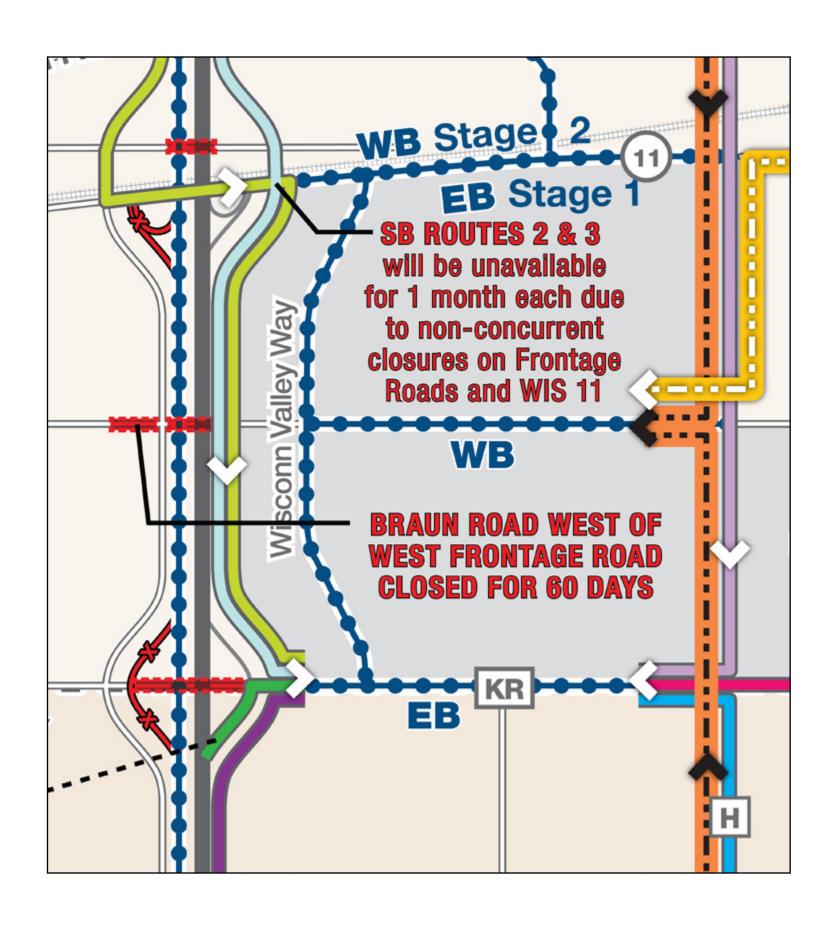

LEGEND

••• Freeway or development road construction

ACCESS ROUTES

General access route (workers)

---> Haul route

Overheight route

CLOSURES

Roadway closed (under I-94 mainline)

Ramp closed (I-94 entrance/exit)

