# US 18/151 PROJECT (COUNTY G TO WIS 69) Weekly Construction Update


The Wisconsin Department of Transportation (WisDOT) is continuing construction along US 18/151 between County G and WIS 69 to address emerging traffic growth and operational deficiencies. Auxiliary lanes will be added, along with interchange and safety improvements. Construction began in March and is scheduled to be complete in late 2025.

#### WORK PROGRESS

- *Military Ridge State Trail box culvert extensions*: Tieback installation for temporary shoring at the south extension ongoing, partial structure demolition to begin next week
- **County G/Dairy Ridge Road bridge:** Deck forming and rebar installation continue and the concrete deck pour scheduled for late next week or early the week of June 30th
- W. Verona Avenue/Epic Lane entrance ramp to eastbound US 18/151: Abutment grading work completed this week, foundation grout drilling for the north abutment to start next week
- **Sugar River bridge widenings:** Pier construction underway with cofferdam installation, pile driving, and footing and column construction to follow

#### TRAFFIC ACCESS IMPACTS

- The speed limit on US 18/151, between Spring Rose Road and WIS 69, is reduced to 55 mph when work is taking place
- US 18/151, between County G and W. Verona Ave./Epic Lane, reduced to one lane in each direction through
  fall 2025
- County G/ Dairy Ridge Road over US 18/151 and the eastbound and westbound US 18/151 ramps at County G are closed through fall 2025
- Military Ridge Trail closed through
  *late summer*

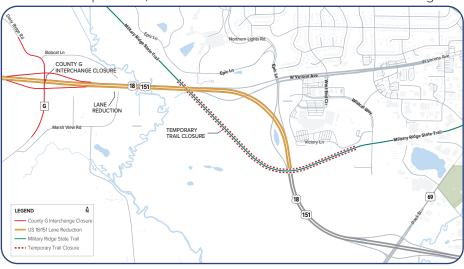



FOR PROJECT UPDATES, SCAN THE QR CODE OR VISIT https://projects.511wi.gov/us18151danecounty/

### CONTACT:

Barry Larson BLarson@hntb.com (608) 209-1626



## US 18/151 PROJECT (COUNTY G TO WIS 69) Weekly Construction Update



Above: Cofferdam complete, pile driving to begin at the east pier for the eastbound Sugar River Bridge widening



Above: County G deck forming, with rebar installation and concrete deck pour to follow



The project team thanks you for your patience and cooperation throughout this project!
