

## US 18/151 PROJECT (COUNTY G TO WIS 69)

# Weekly Construction Update


The Wisconsin Department of Transportation (WisDOT) is continuing construction along US 18/151 between County G and WIS 69 to address emerging traffic growth and operational deficiencies. Auxiliary lanes will be added, along with interchange and safety improvements. Construction began in March and is scheduled to be complete in late 2025.

### WORK PROGRESS

- **County G/Dairy Ridge Road:** Curb & gutter, concrete paving, and deck form stripping next week
- **W. Verona Avenue/Epic Lane entrance ramp to eastbound US 18/151:** Deck stripping, removals, grading and concrete pavement approach slabs next week
- **Sugar River bridge widenings:** Deck bar steel installation this week; concrete deck pours next week
- **W. Verona Avenue on-ramp to westbound US 18/151:** Asphalt paving today, remove concrete barrier block tonight, ramp to reopen tomorrow/Saturday 9/27
- **W. Verona Avenue/Epic Lane exit ramp to eastbound US 18/151:** Remove concrete barrier block tonight; pavement markings and open to traffic early next week

### TRAFFIC ACCESS IMPACTS

- **The speed limit on US 18/151, between Spring Rose Road and WIS 69, is reduced to 55 mph when work is taking place**
- US 18/151, between County G and W. Verona Ave./Epic Lane, reduced to one lane in each direction through December 2025
- County G/ Dairy Ridge Road over US 18/151 and the eastbound and westbound US 18/151 ramps at County G are closed through December 2025
- **The on-ramp from W. Verona Avenue to westbound US 18/151 is scheduled to reopen Saturday 9/27**

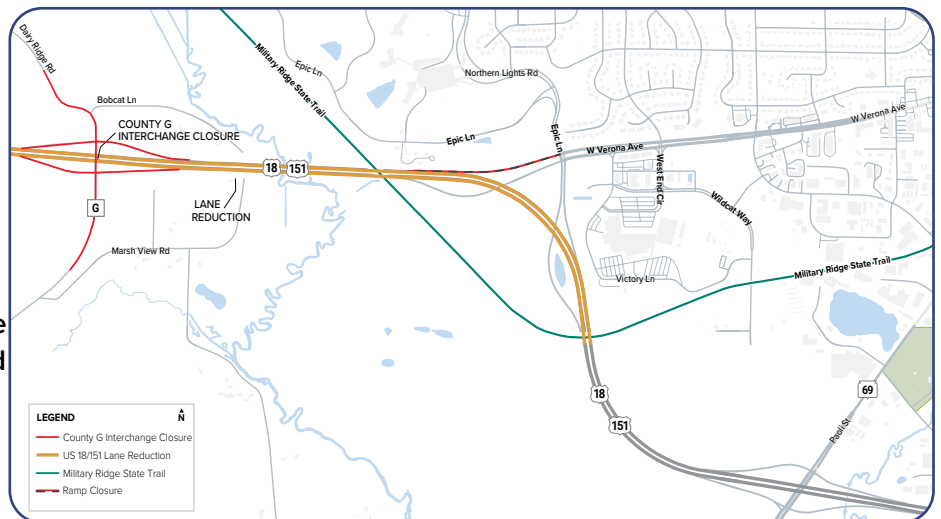

FOR PROJECT UPDATES,  
SCAN THE QR CODE OR VISIT  
<https://projects.511wi.gov/us18151-danecounty/>

CONTACT:  
Barry Larson  
[BLarson@hntb.com](mailto:BLarson@hntb.com)  
(608) 209-1626



US 18/151 PROJECT (COUNTY G TO WIS 69)

# Weekly Construction Update



Above: Deck widening of the Sugar River bridge along US 18/151 eastbound



Above: Westbound US 18/151 concrete base paving.jpg

The project team thanks you for your patience and cooperation throughout this project!

