

## US 18/151 PROJECT (COUNTY G TO WIS 69)

# Weekly Construction Update


The Wisconsin Department of Transportation (WisDOT) is continuing construction along US 18/151 between County G and WIS 69 to address emerging traffic growth and operational deficiencies. Auxiliary lanes will be added, along with interchange and safety improvements. Construction began in March and is scheduled to be complete in late 2025.

### WORK PROGRESS

- **County G/Dairy Ridge Road:** Concrete pavement ongoing, bridge deck polymer overlay next week, rock grading to begin next week
- **W. Verona Avenue/Epic Lane entrance ramp to eastbound US 18/151:** Concrete paving and restoration completed this week, rock grading and asphalt shoulder paving next week
- **Eastbound US 18/151 auxiliary lane, County G to W. Verona Ave:** Roadway grading, rock placement, and restoration in progress; concrete paving to start late next week
- **Bridge Work:** Construction completed; deck form stripping, final backfilling, rip-rap placement in progress

### TRAFFIC ACCESS IMPACTS

- **The speed limit on US 18/151, between Spring Rose Road and WIS 69, is reduced to 55 mph when work is taking place**
- US 18/151, between County G and W. Verona Ave./Epic Lane, reduced to one lane in each direction through December 2025
- County G/ Dairy Ridge Road over US 18/151 and the eastbound and westbound US 18/151 ramps at County G are closed through December 2025

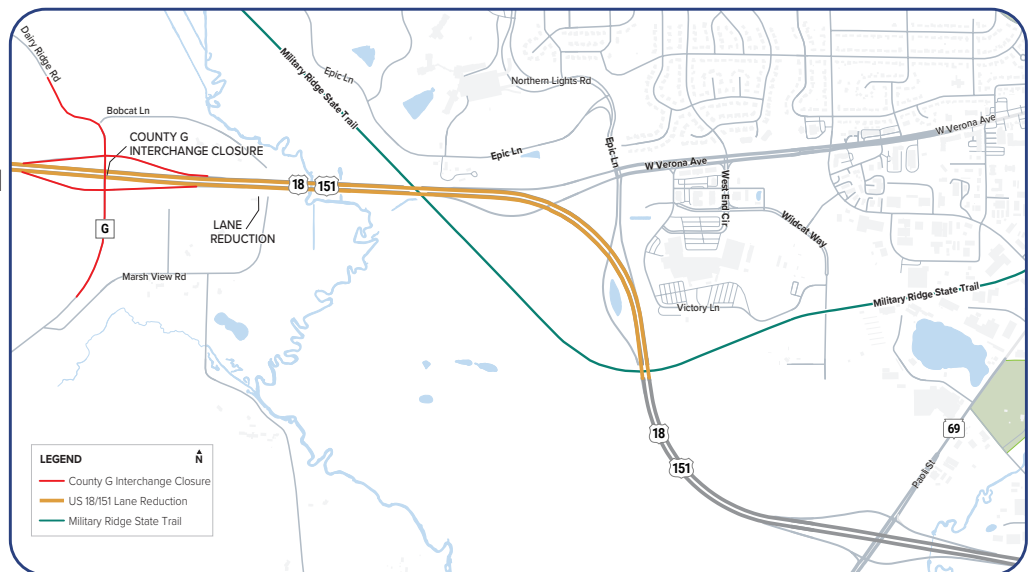

FOR PROJECT UPDATES,  
SCAN THE QR CODE OR VISIT  
<https://projects.511wi.gov/us18151-danecounty/>

CONTACT:  
Barry Larson  
[BLarson@hntb.com](mailto:BLarson@hntb.com)  
(608) 209-1626



US 18/151 PROJECT (COUNTY G TO WIS 69)

# Weekly Construction Update



Above: Concrete paving on County G and Dairy Ridge Road



Above: Completed eastbound Sugar River bridge widening



Above: Completed westbound Sugar River bridge widening
