

Jason Geurts

WisDOT Project Construction Lead

jason.geurts@dot.wi.gov

(920) 366-3816


Field office location, 2301 State Highway 32, across from S&L Motors

LEGEND

WORK AREA



**Contractor's Proposed Schedule -
As of April 2022:**
4/18/22 - 7/27/22

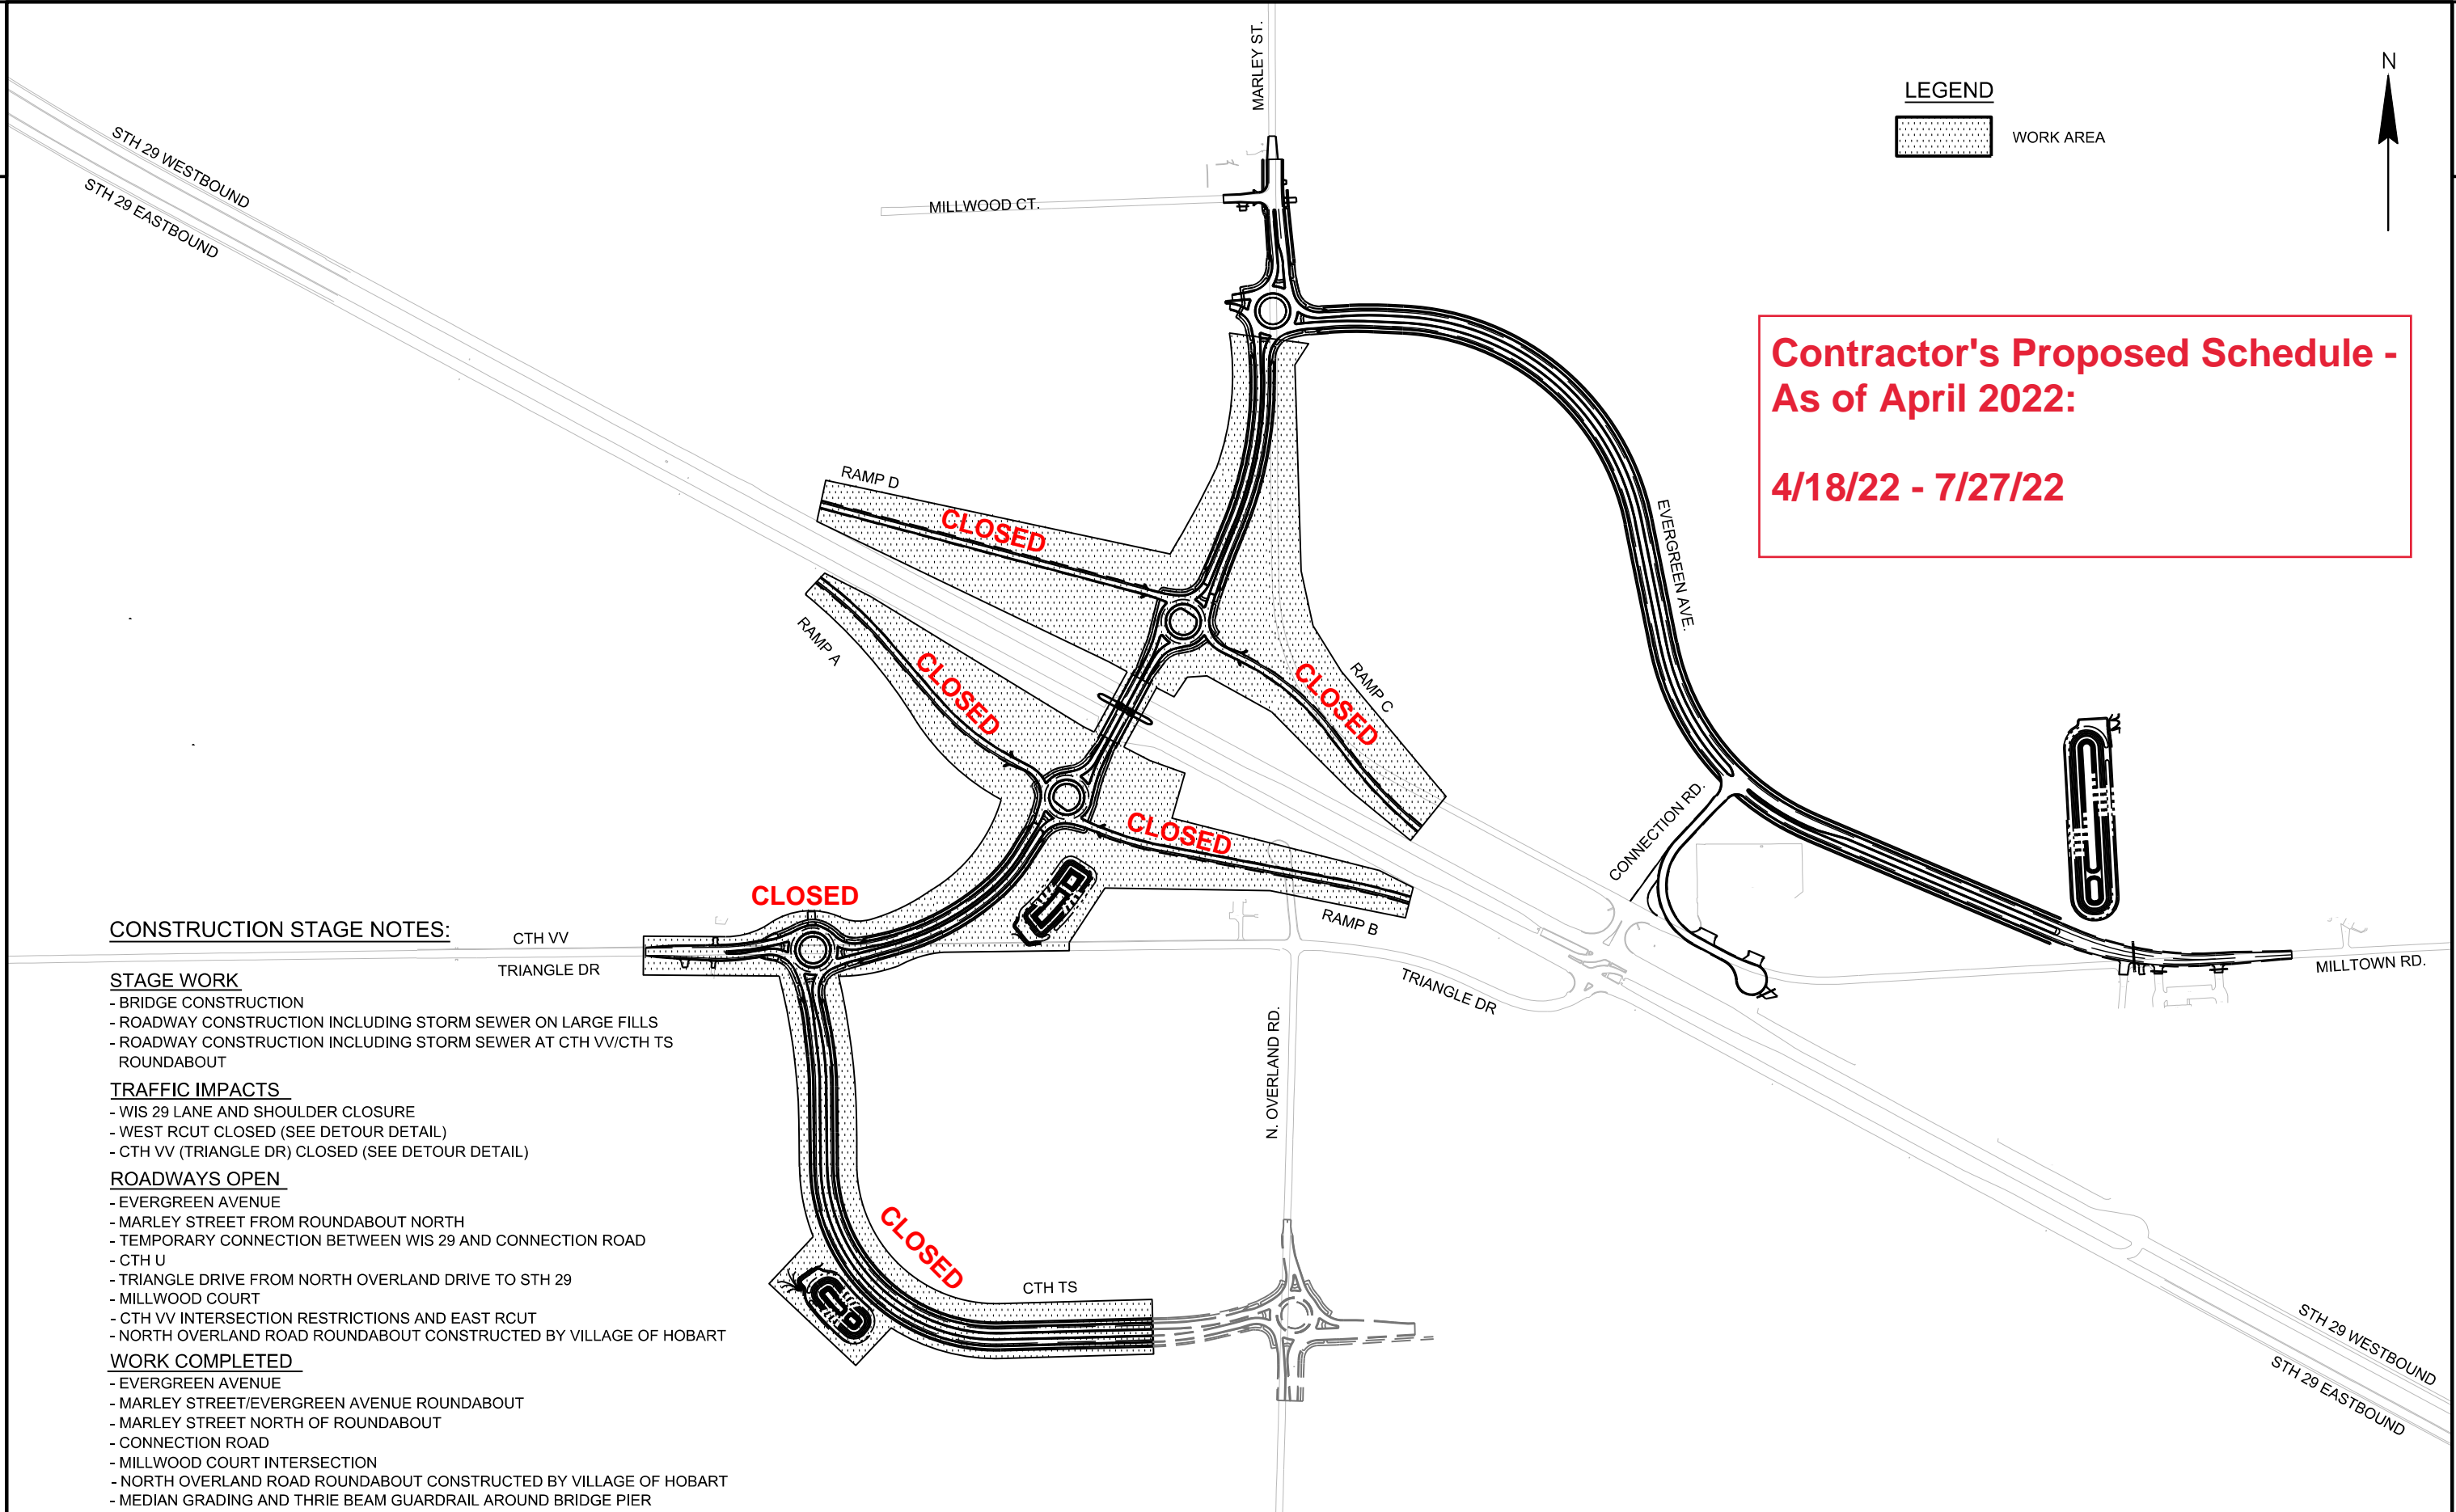

CONSTRUCTION STAGE NOTES:

STAGE WORK

- BRIDGE CONSTRUCTION
- ROADWAY CONSTRUCTION INCLUDING STORM SEWER ON LARGE FILLS
- ROADWAY CONSTRUCTION INCLUDING STORM SEWER AT CTH VV/CTH TS ROUNDABOUT

TRAFFIC IMPACTS

- WIS 29 LANE AND SHOULDER CLOSURE
- WEST RCUT CLOSED (SEE DETOUR DETAIL)
- CTH VV (TRIANGLE DR) CLOSED (SEE DETOUR DETAIL)

ROADWAYS OPEN

- EVERGREEN AVENUE
- MARLEY STREET FROM ROUNDABOUT NORTH
- TEMPORARY CONNECTION BETWEEN WIS 29 AND CONNECTION ROAD
- CTH U
- TRIANGLE DRIVE FROM NORTH OVERLAND DRIVE TO STH 29
- MILLWOOD COURT
- CTH VV INTERSECTION RESTRICTIONS AND EAST RCUT
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART

WORK COMPLETED

- EVERGREEN AVENUE
- MARLEY STREET/EVERGREEN AVENUE ROUNDABOUT
- MARLEY STREET NORTH OF ROUNDABOUT
- CONNECTION ROAD
- MILLWOOD COURT INTERSECTION
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART
- MEDIAN GRADING AND THRIE BEAM GUARDRAIL AROUND BRIDGE PIER

PROJECT NO: 9200-10-71

HWY: STH 29

COUNTY: BROWN


STAGE CONSTRUCTION-STAGE 4B

SHEET

452

E


LEGEND

 WORK AREA



**Contractor's Proposed Schedule
- As of April 2022:**

5/16/22 - 7/27/22

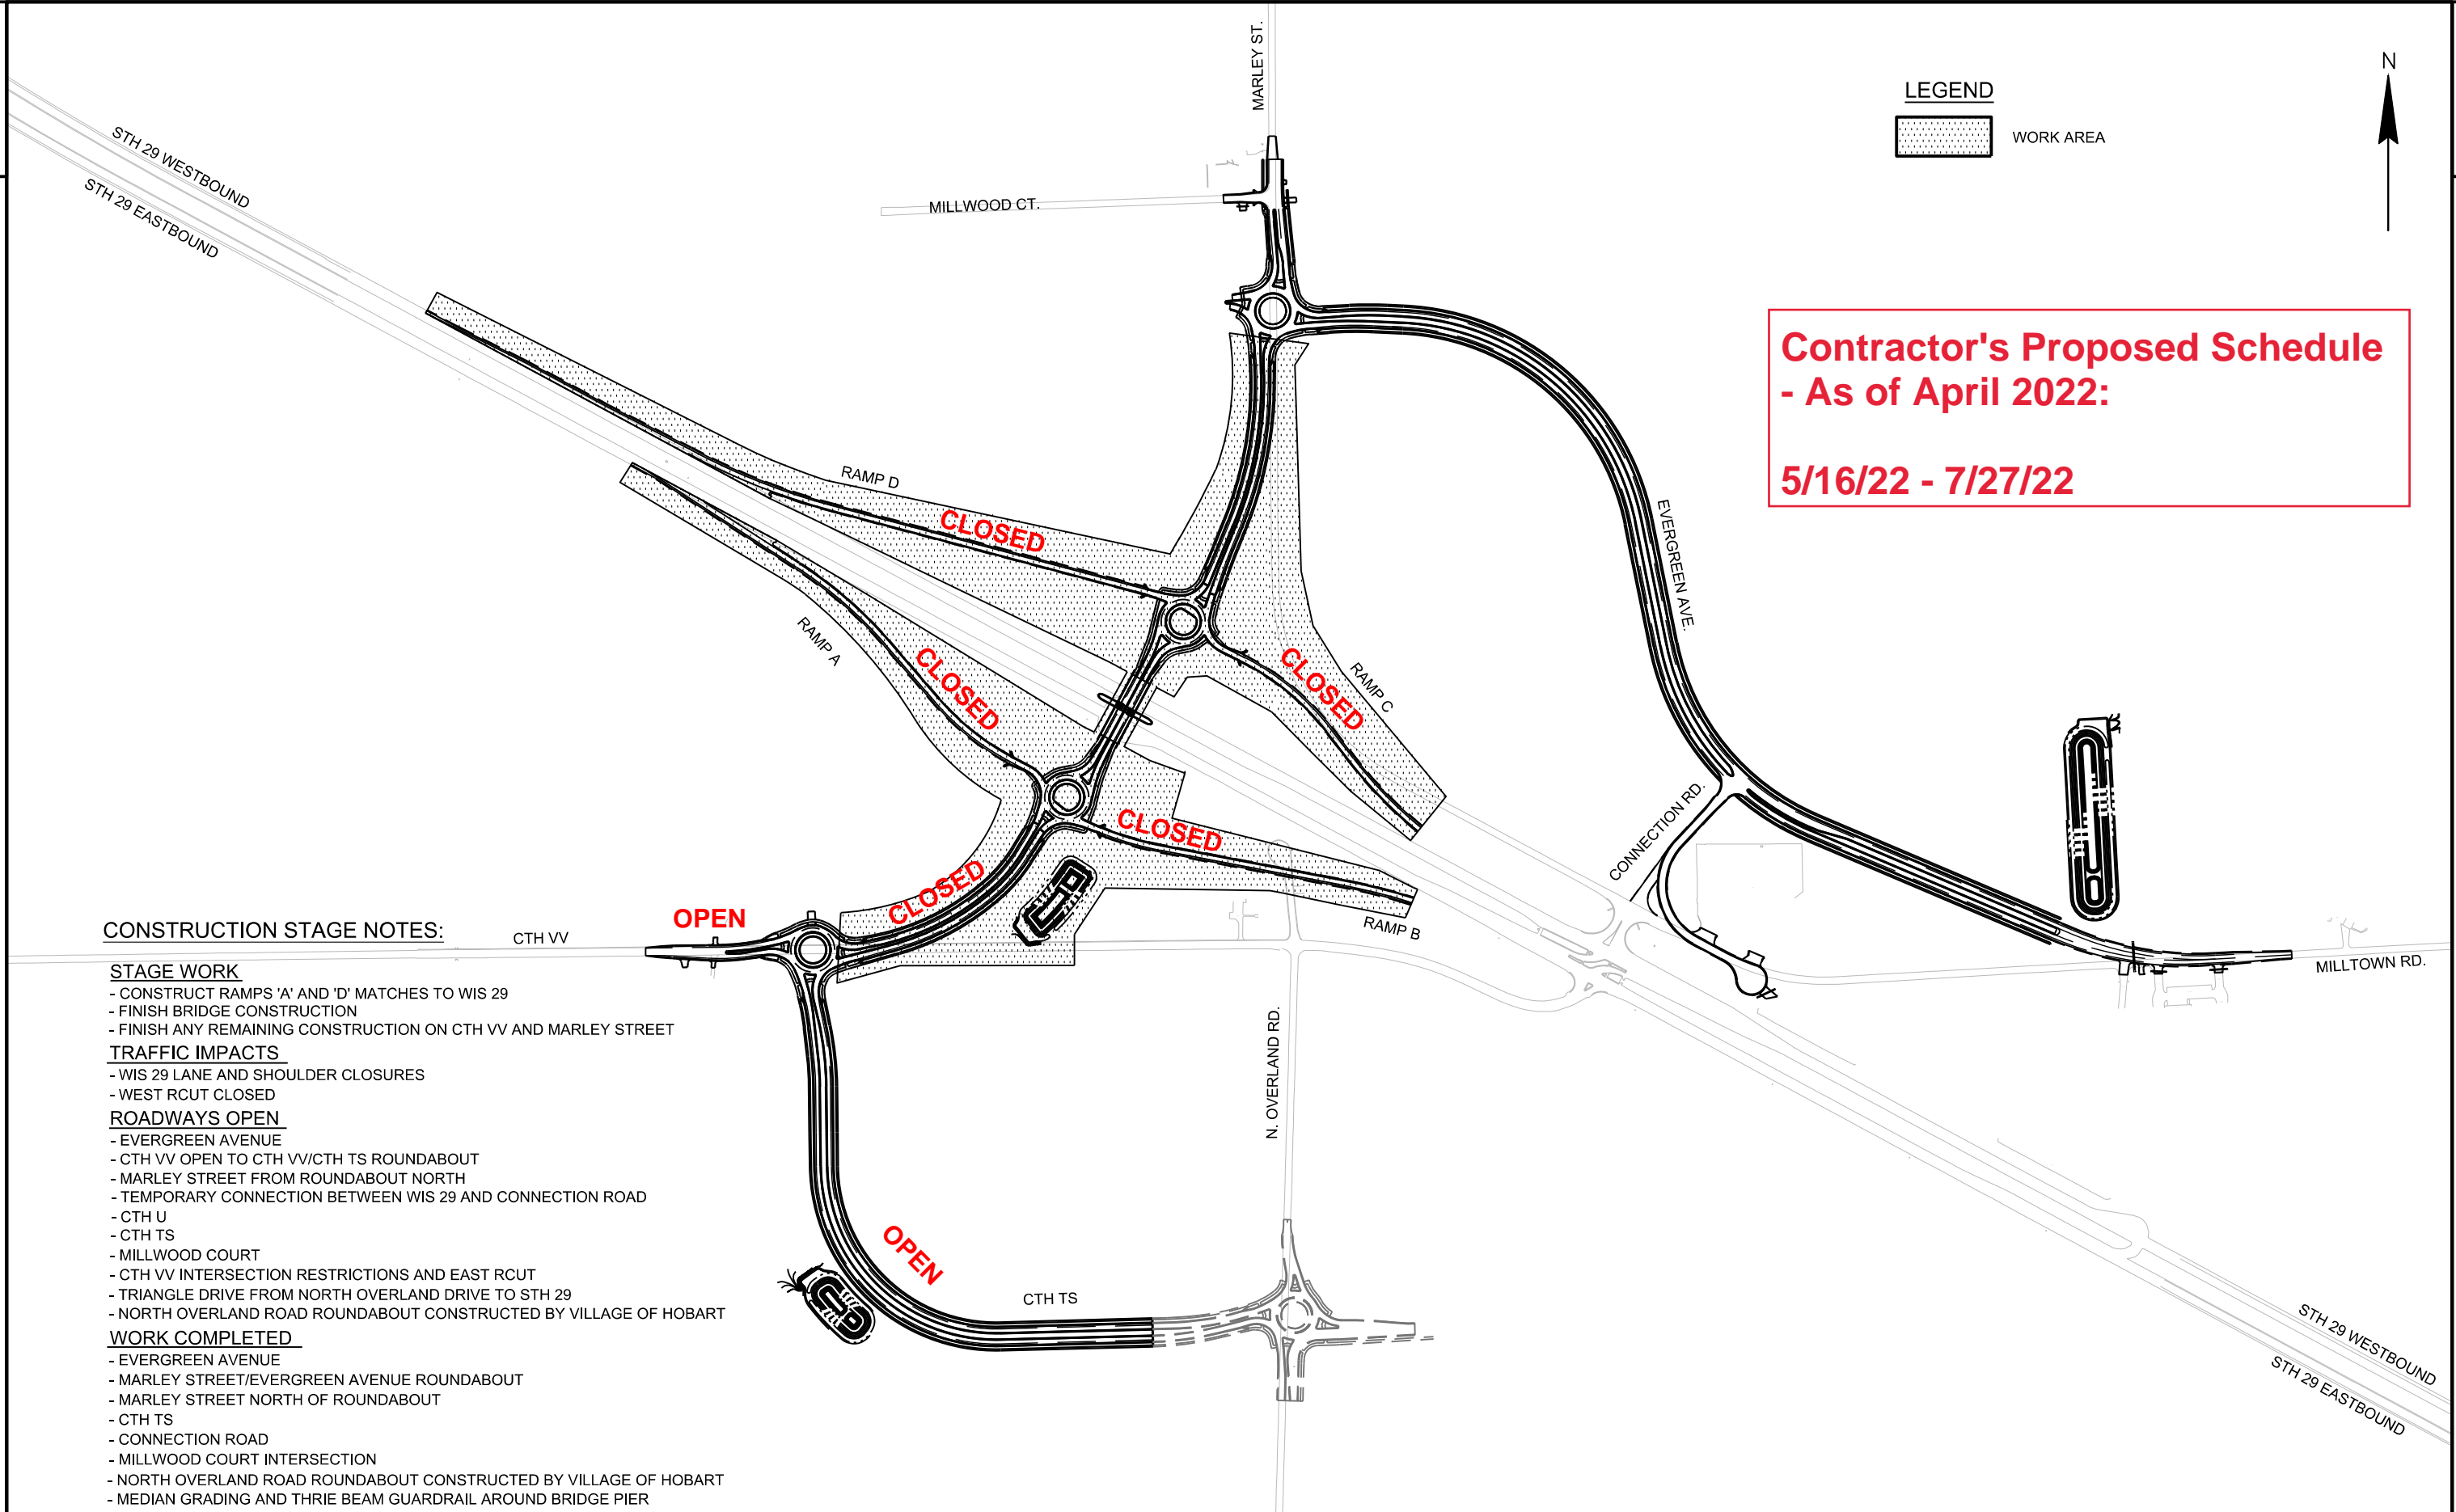

CONSTRUCTION STAGE NOTES:

STAGE WORK

- CONSTRUCT RAMPS 'A' AND 'D' MATCHES TO WIS 29
- FINISH BRIDGE CONSTRUCTION
- FINISH ANY REMAINING CONSTRUCTION ON CTH VV AND MARLEY STREET

TRAFFIC IMPACTS

- WIS 29 LANE AND SHOULDER CLOSURES
- WEST RCUT CLOSED

ROADWAYS OPEN

- EVERGREEN AVENUE
- CTH VV OPEN TO CTH VV/CTH TS ROUNDABOUT
- MARLEY STREET FROM ROUNDABOUT NORTH
- TEMPORARY CONNECTION BETWEEN WIS 29 AND CONNECTION ROAD
- CTH U
- CTH TS
- MILLWOOD COURT
- CTH VV INTERSECTION RESTRICTIONS AND EAST RCUT
- TRIANGLE DRIVE FROM NORTH OVERLAND DRIVE TO STH 29
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART

WORK COMPLETED

- EVERGREEN AVENUE
- MARLEY STREET/EVERGREEN AVENUE ROUNDABOUT
- MARLEY STREET NORTH OF ROUNDABOUT
- CTH TS
- CONNECTION ROAD
- MILLWOOD COURT INTERSECTION
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART
- MEDIAN GRADING AND THRIE BEAM GUARDRAIL AROUND BRIDGE PIER


LEGEND



**Contractor's Proposed Schedule
- As of April 2022:**

7/27/22 - 8/12/22

**-Closure for Existing CTH VV
Intersection at Ramp B from
7/27/22 - 8/12/22**

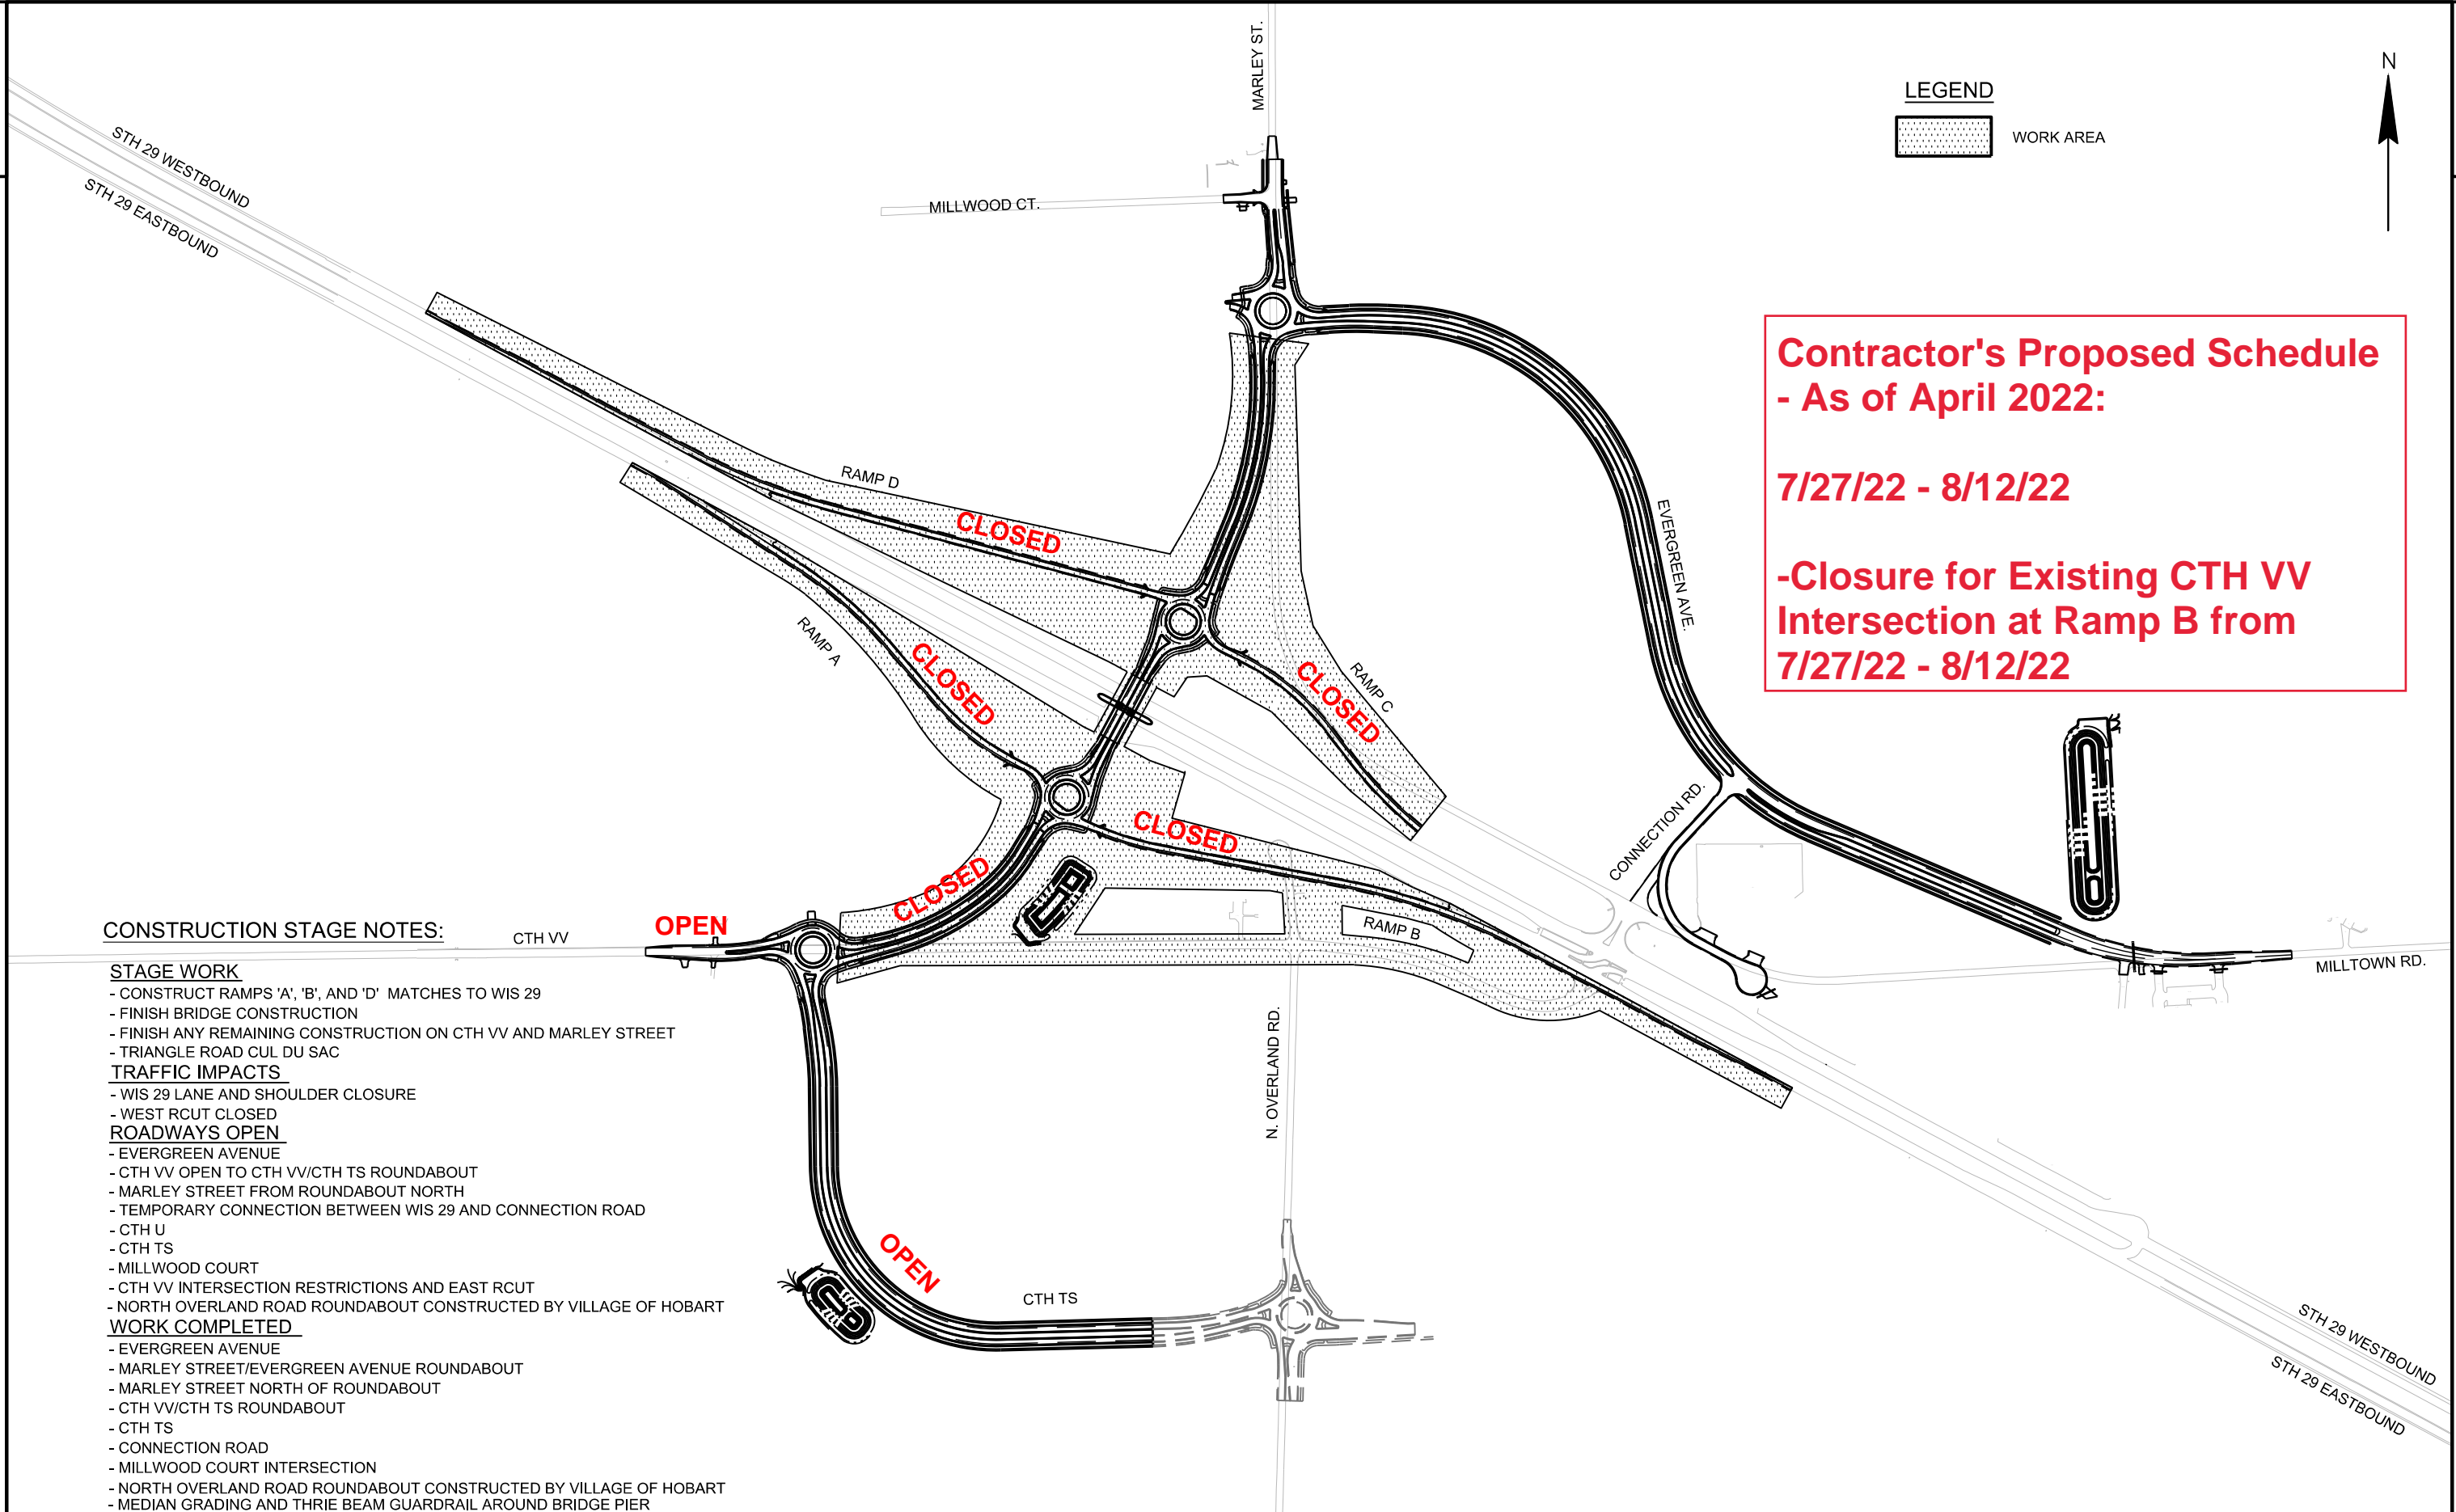

CONSTRUCTION STAGE NOTES:

STAGE WORK

- CONSTRUCT RAMPS 'A', 'B', AND 'D' MATCHES TO WIS 29
- FINISH BRIDGE CONSTRUCTION
- FINISH ANY REMAINING CONSTRUCTION ON CTH VV AND MARLEY STREET
- TRIANGLE ROAD CUL DU SAC

TRAFFIC IMPACTS

- WIS 29 LANE AND SHOULDER CLOSURE
- WEST RCUT CLOSED

ROADWAYS OPEN

- EVERGREEN AVENUE
- CTH VV OPEN TO CTH VV/CTH TS ROUNDABOUT
- MARLEY STREET FROM ROUNDABOUT NORTH
- TEMPORARY CONNECTION BETWEEN WIS 29 AND CONNECTION ROAD

- CTH U
- CTH TS

- MILLWOOD COURT

- CTH VV INTERSECTION RESTRICTIONS AND EAST RCUT
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART

WORK COMPLETED

- EVERGREEN AVENUE
- MARLEY STREET/EVERGREEN AVENUE ROUNDABOUT
- MARLEY STREET NORTH OF ROUNDABOUT
- CTH VV/CTH TS ROUNDABOUT
- CTH TS
- CONNECTION ROAD
- MILLWOOD COURT INTERSECTION
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART
- MEDIAN GRADING AND THRIE BEAM GUARDRAIL AROUND BRIDGE PIER

PROJECT NO: 9200-10-71

HWY: STH 29

COUNTY: BROWN

STAGE CONSTRUCTION-STAGE 5B

SHEET

454

E

LEGEND



WORK AREA



**Contractor's Proposed Schedule -
As of April 2022:**
8/29/22 - 9/9/22

STH 29 WESTBOUND
STH 29 EASTBOUND

CTH U

GLENDALE AVE.

OLD 29 ROAD

OPEN

CLOSED

OPEN

N. COUNTY LINE RD.

STH 29 WESTBOUND

STH 29 EASTBOUND

CONSTRUCTION STAGE NOTES:

STAGE WORK

- CONSTRUCT RAMP 'C'
- CONSTRUCT NORTH COUNTY LINE ROAD CONNECTION TO OLD 29 ROAD

TRAFFIC IMPACTS

- WIS 29 LANE AND SHOULDER CLOSURES
- WEST RCUT CLOSED
- EAST RCUT CLOSED


ROADWAYS OPEN

- RAMPS 'A', 'B', AND 'D'
- EVERGREEN AVENUE
- CTH VV
- MARLEY STREET
- CTH U
- CTH TS
- MILLWOOD COURT
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART

WORK COMPLETED

- CTH VV INTERCHANGE WITH RAMPS 'A', 'B' AND 'D'
- CTH VV
- EVERGREEN AVENUE
- MARLEY STREET/EVERGREEN AVENUE ROUNDABOUT
- MARLEY STREET NORTH OF ROUNDABOUT
- CTH TS
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART
- CONNECTION ROAD
- MILLWOOD COURT INTERSECTION
- TRIANGLE ROAD CUL DU SAC

LEGEND


 WORK AREA




**Contractor's Proposed Schedule -
As of April 2022:**


8/15/22 - 8/28/22

- CONSTRUCTION STAGE NOTES:**
- STAGE WORK**
- CONSTRUCT RAMP 'C'
 - CONSTRUCT NORTH COUNTY LINE ROAD CONNECTION TO OLD 29 ROAD
- TRAFFIC IMPACTS**
- WIS 29 LANE AND SHOULDER CLOSURES
 - WEST RCUT CLOSED
 - EAST RCUT CLOSED
- ROADWAYS OPEN**
- RAMPS 'A', 'B', AND 'D'
 - EVERGREEN AVENUE
 - CTH VV
 - MARLEY STREET
 - CTH U
 - CTH TS
 - MILLWOOD COURT
 - NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART
- WORK COMPLETED**
- CTH VV INTERCHANGE WITH RAMPS 'A', 'B' AND 'D'
 - CTH VV
 - EVERGREEN AVENUE
 - MARLEY STREET/EVERGREEN AVENUE ROUNDABOUT
 - MARLEY STREET NORTH OF ROUNDABOUT
 - CTH TS
 - NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART
 - CONNECTION ROAD
 - MILLWOOD COURT INTERSECTION
 - TRIANGLE ROAD CUL DU SAC

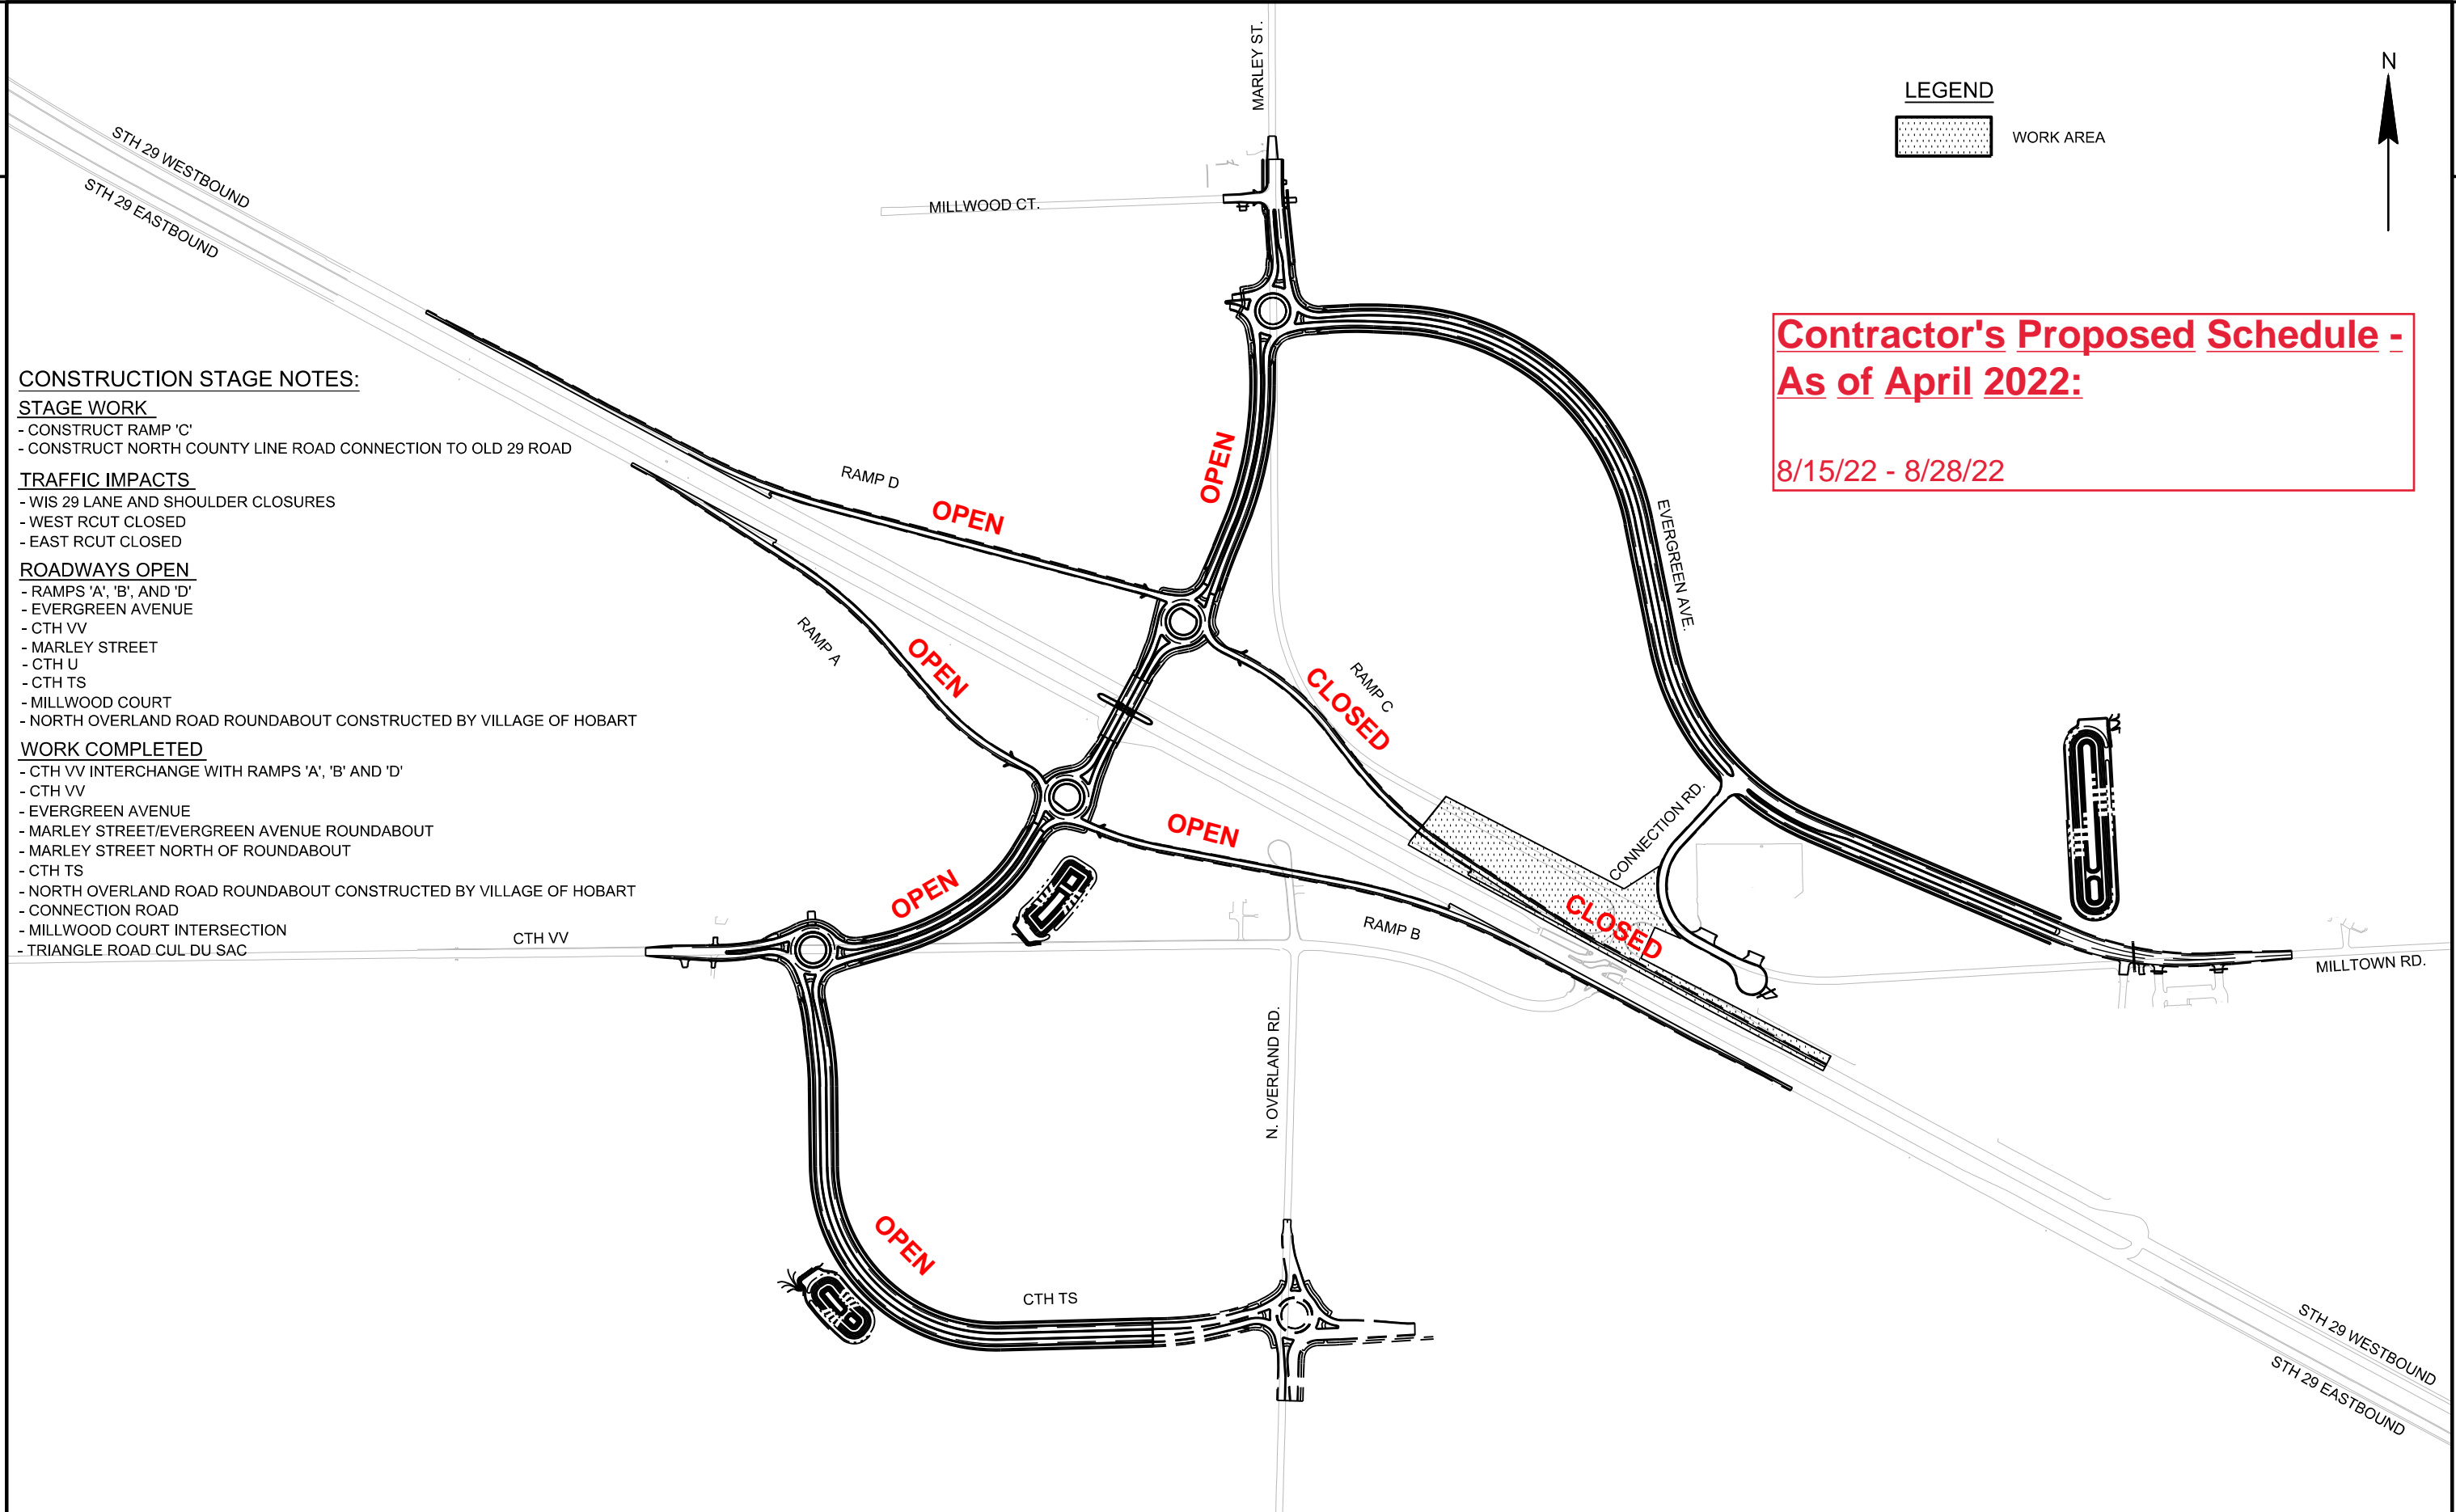

LEGEND

 WORK AREA

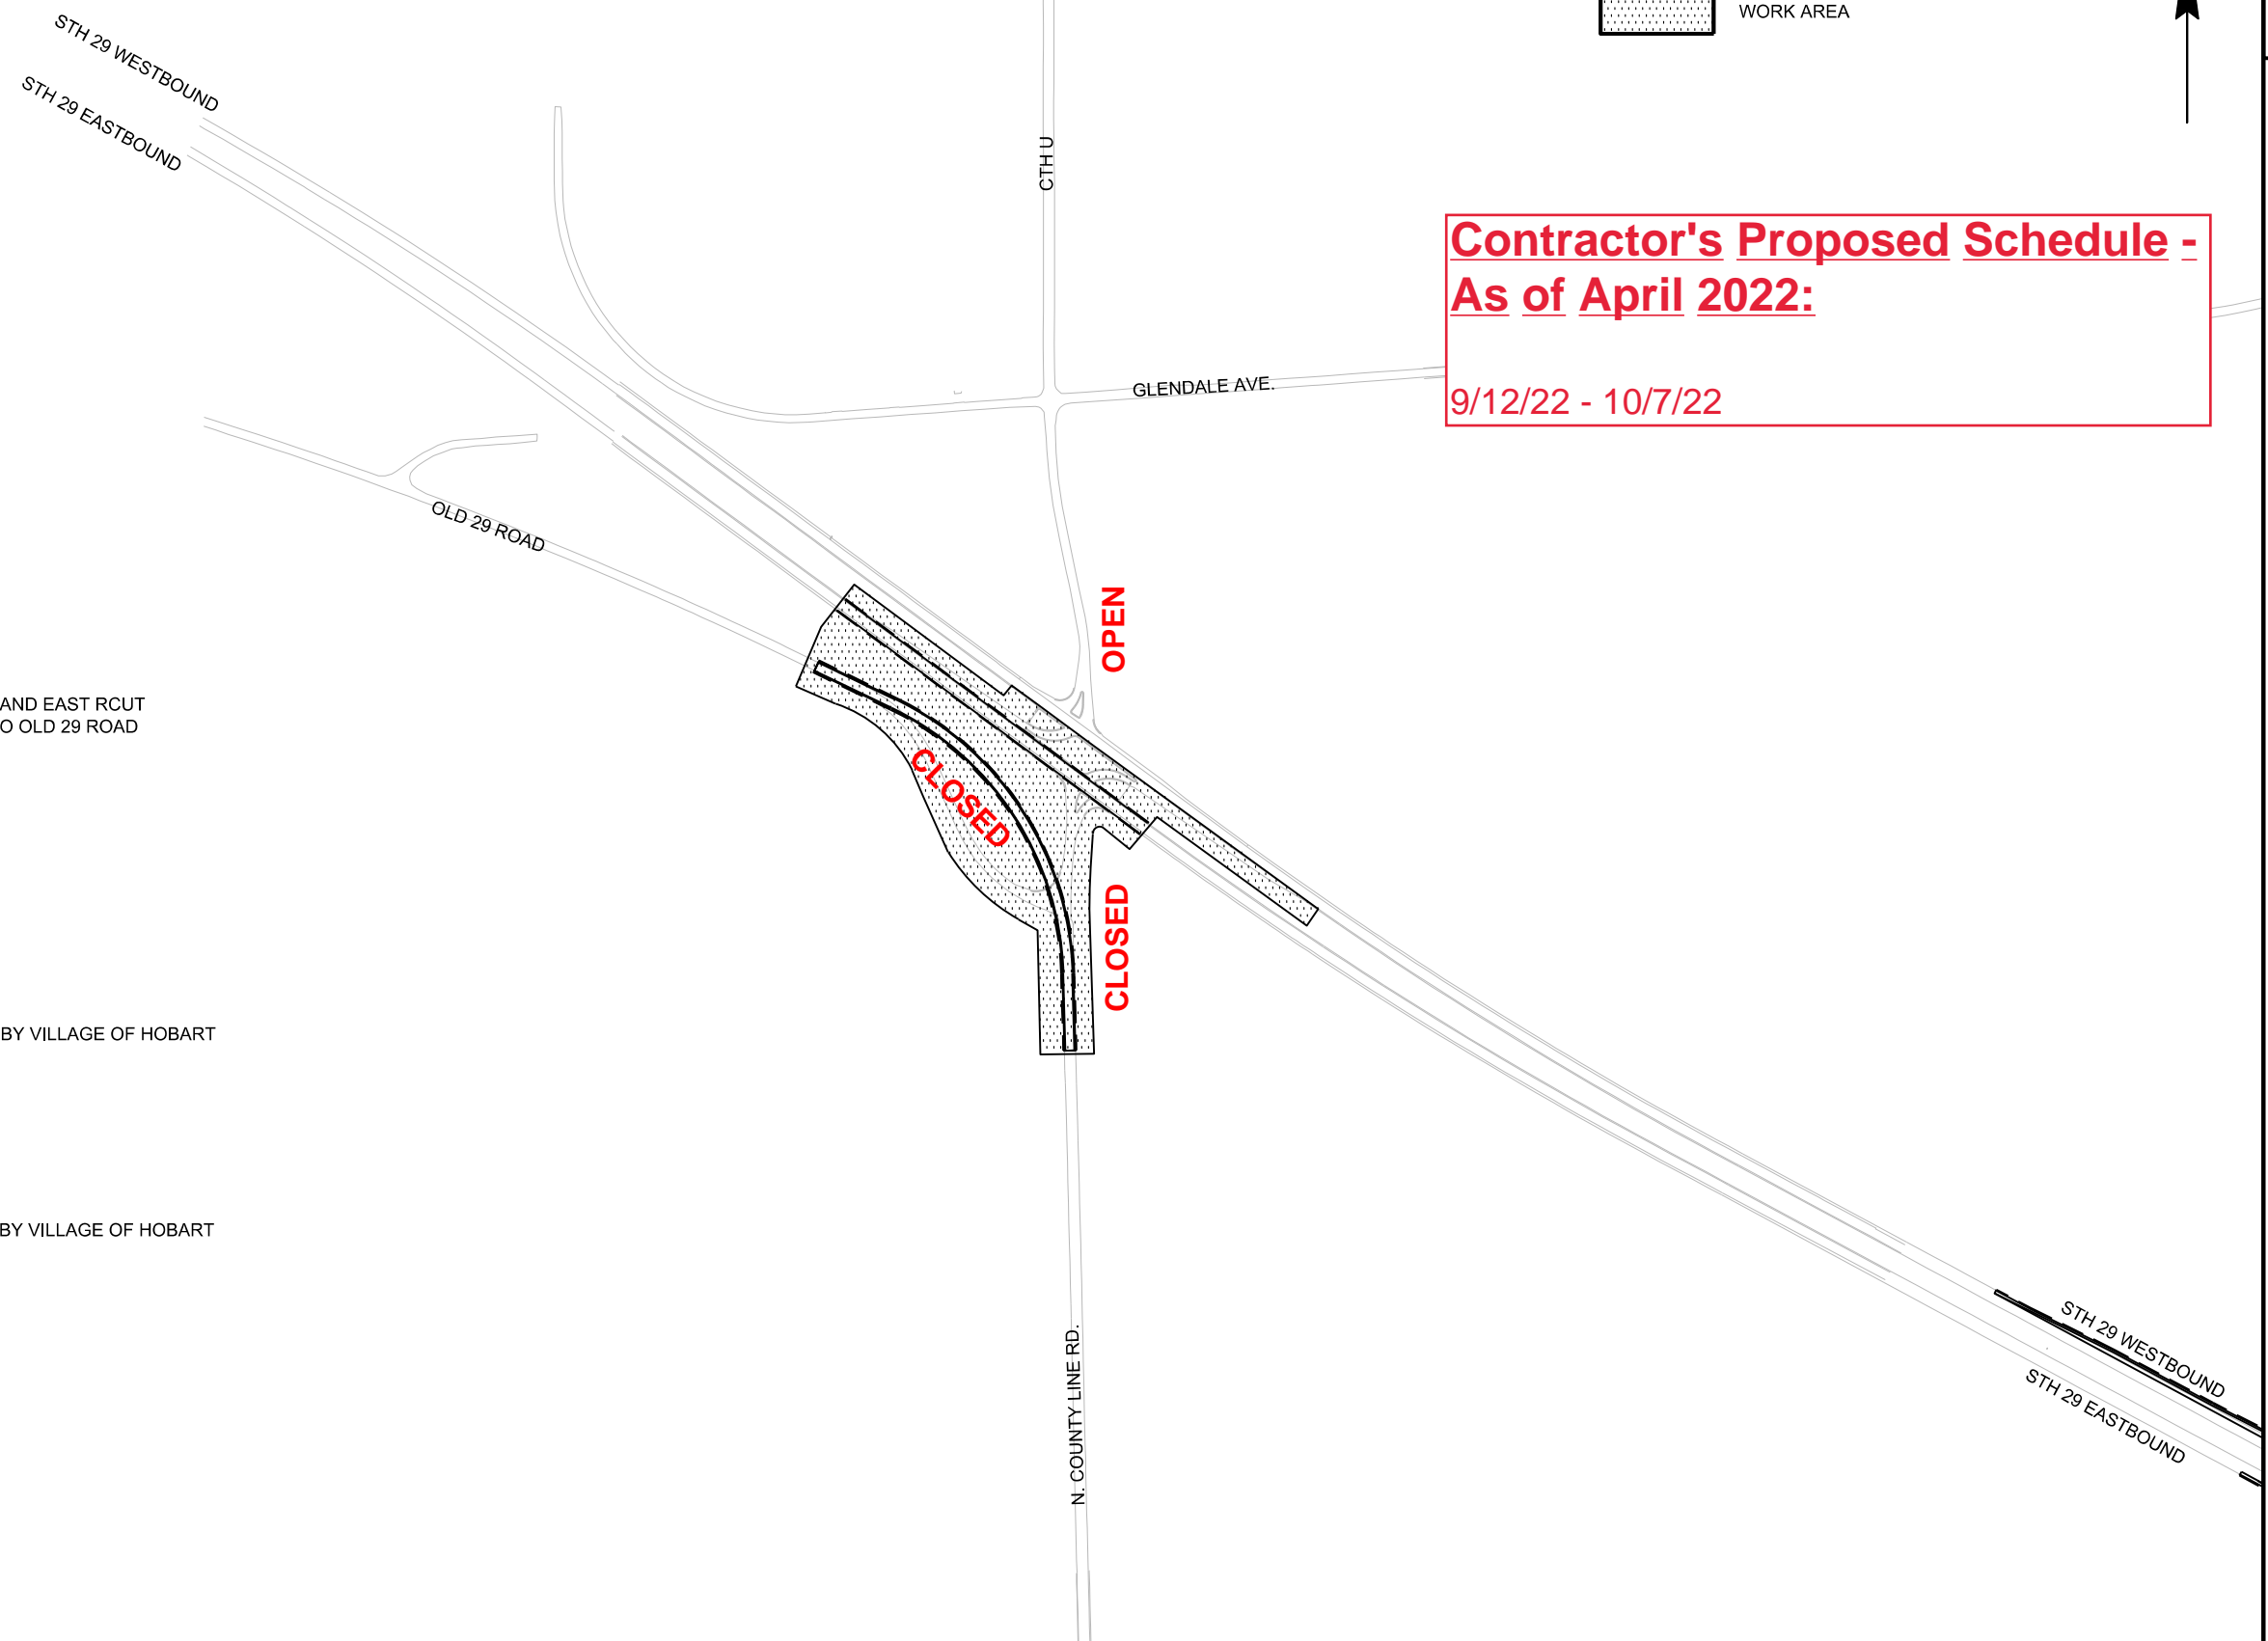

**Contractor's Proposed Schedule -
As of April 2022:**

9/12/22 - 10/7/22

CONSTRUCTION STAGE NOTES:

STAGE WORK

- REMOVE CTH U INTERSECTION
- REMOVE CTH VV MEDIAN INTERSECTION RESTRICTIONS AND EAST RCUT
- CONSTRUCT NORTH COUNTY LINE ROAD CONNECTION TO OLD 29 ROAD

TRAFFIC IMPACTS

- WIS 29 LANE AND SHOULDER CLOSURES
- WEST RCUT CLOSED
- EAST RCUT CLOSED


ROADWAYS OPEN

- RAMPS 'A', 'B', 'C', AND 'D'
- EVERGREEN AVENUE
- CTH VV
- MARLEY STREET
- CTH U
- CTH TS
- MILLWOOD COURT
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART

WORK COMPLETED

- CTH VV INTERCHANGE WITH RAMPS 'A', 'B', 'C', AND 'D'
- CTH VV
- EVERGREEN AVENUE
- MARLEY STREET/EVERGREEN AVENUE ROUNDABOUT
- MARLEY STREET NORTH OF ROUNDABOUT
- CTH TS
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART
- CONNECTION ROAD
- MILLWOOD COURT INTERSECTION
- TRIANGLE ROAD CUL DU SAC

LEGEND

 WORK AREA



CONSTRUCTION STAGE NOTES:

STAGE WORK

- REMOVE CTH U INTERSECTION
- REMOVE CTH VV MEDIAN INTERSECTION RESTRICTIONS AND EAST RCUT
- CONSTRUCT NORTH COUNTY LINE ROAD CONNECTION TO OLD 29 ROAD

TRAFFIC IMPACTS

- WIS 29 LANE AND SHOULDER CLOSURES
- WEST RCUT CLOSED
- EAST RCUT CLOSED

ROADWAYS OPEN


- RAMPS 'A', 'B', 'C', AND 'D'
- EVERGREEN AVENUE
- CTH VV
- MARLEY STREET
- CTH U
- CTH TS
- MILLWOOD COURT
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART

WORK COMPLETED


- CTH VV INTERCHANGE WITH RAMPS 'A', 'B', 'C', AND 'D'
- CTH VV
- EVERGREEN AVENUE
- MARLEY STREET/EVERGREEN AVENUE ROUNDABOUT
- MARLEY STREET NORTH OF ROUNDABOUT
- CTH TS
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART
- CONNECTION ROAD
- MILLWOOD COURT INTERSECTION
- TRIANGLE ROAD CUL DU SAC

**Contractor's Proposed Schedule -
As of April 2022:**

9/12/22 - 10/7/22

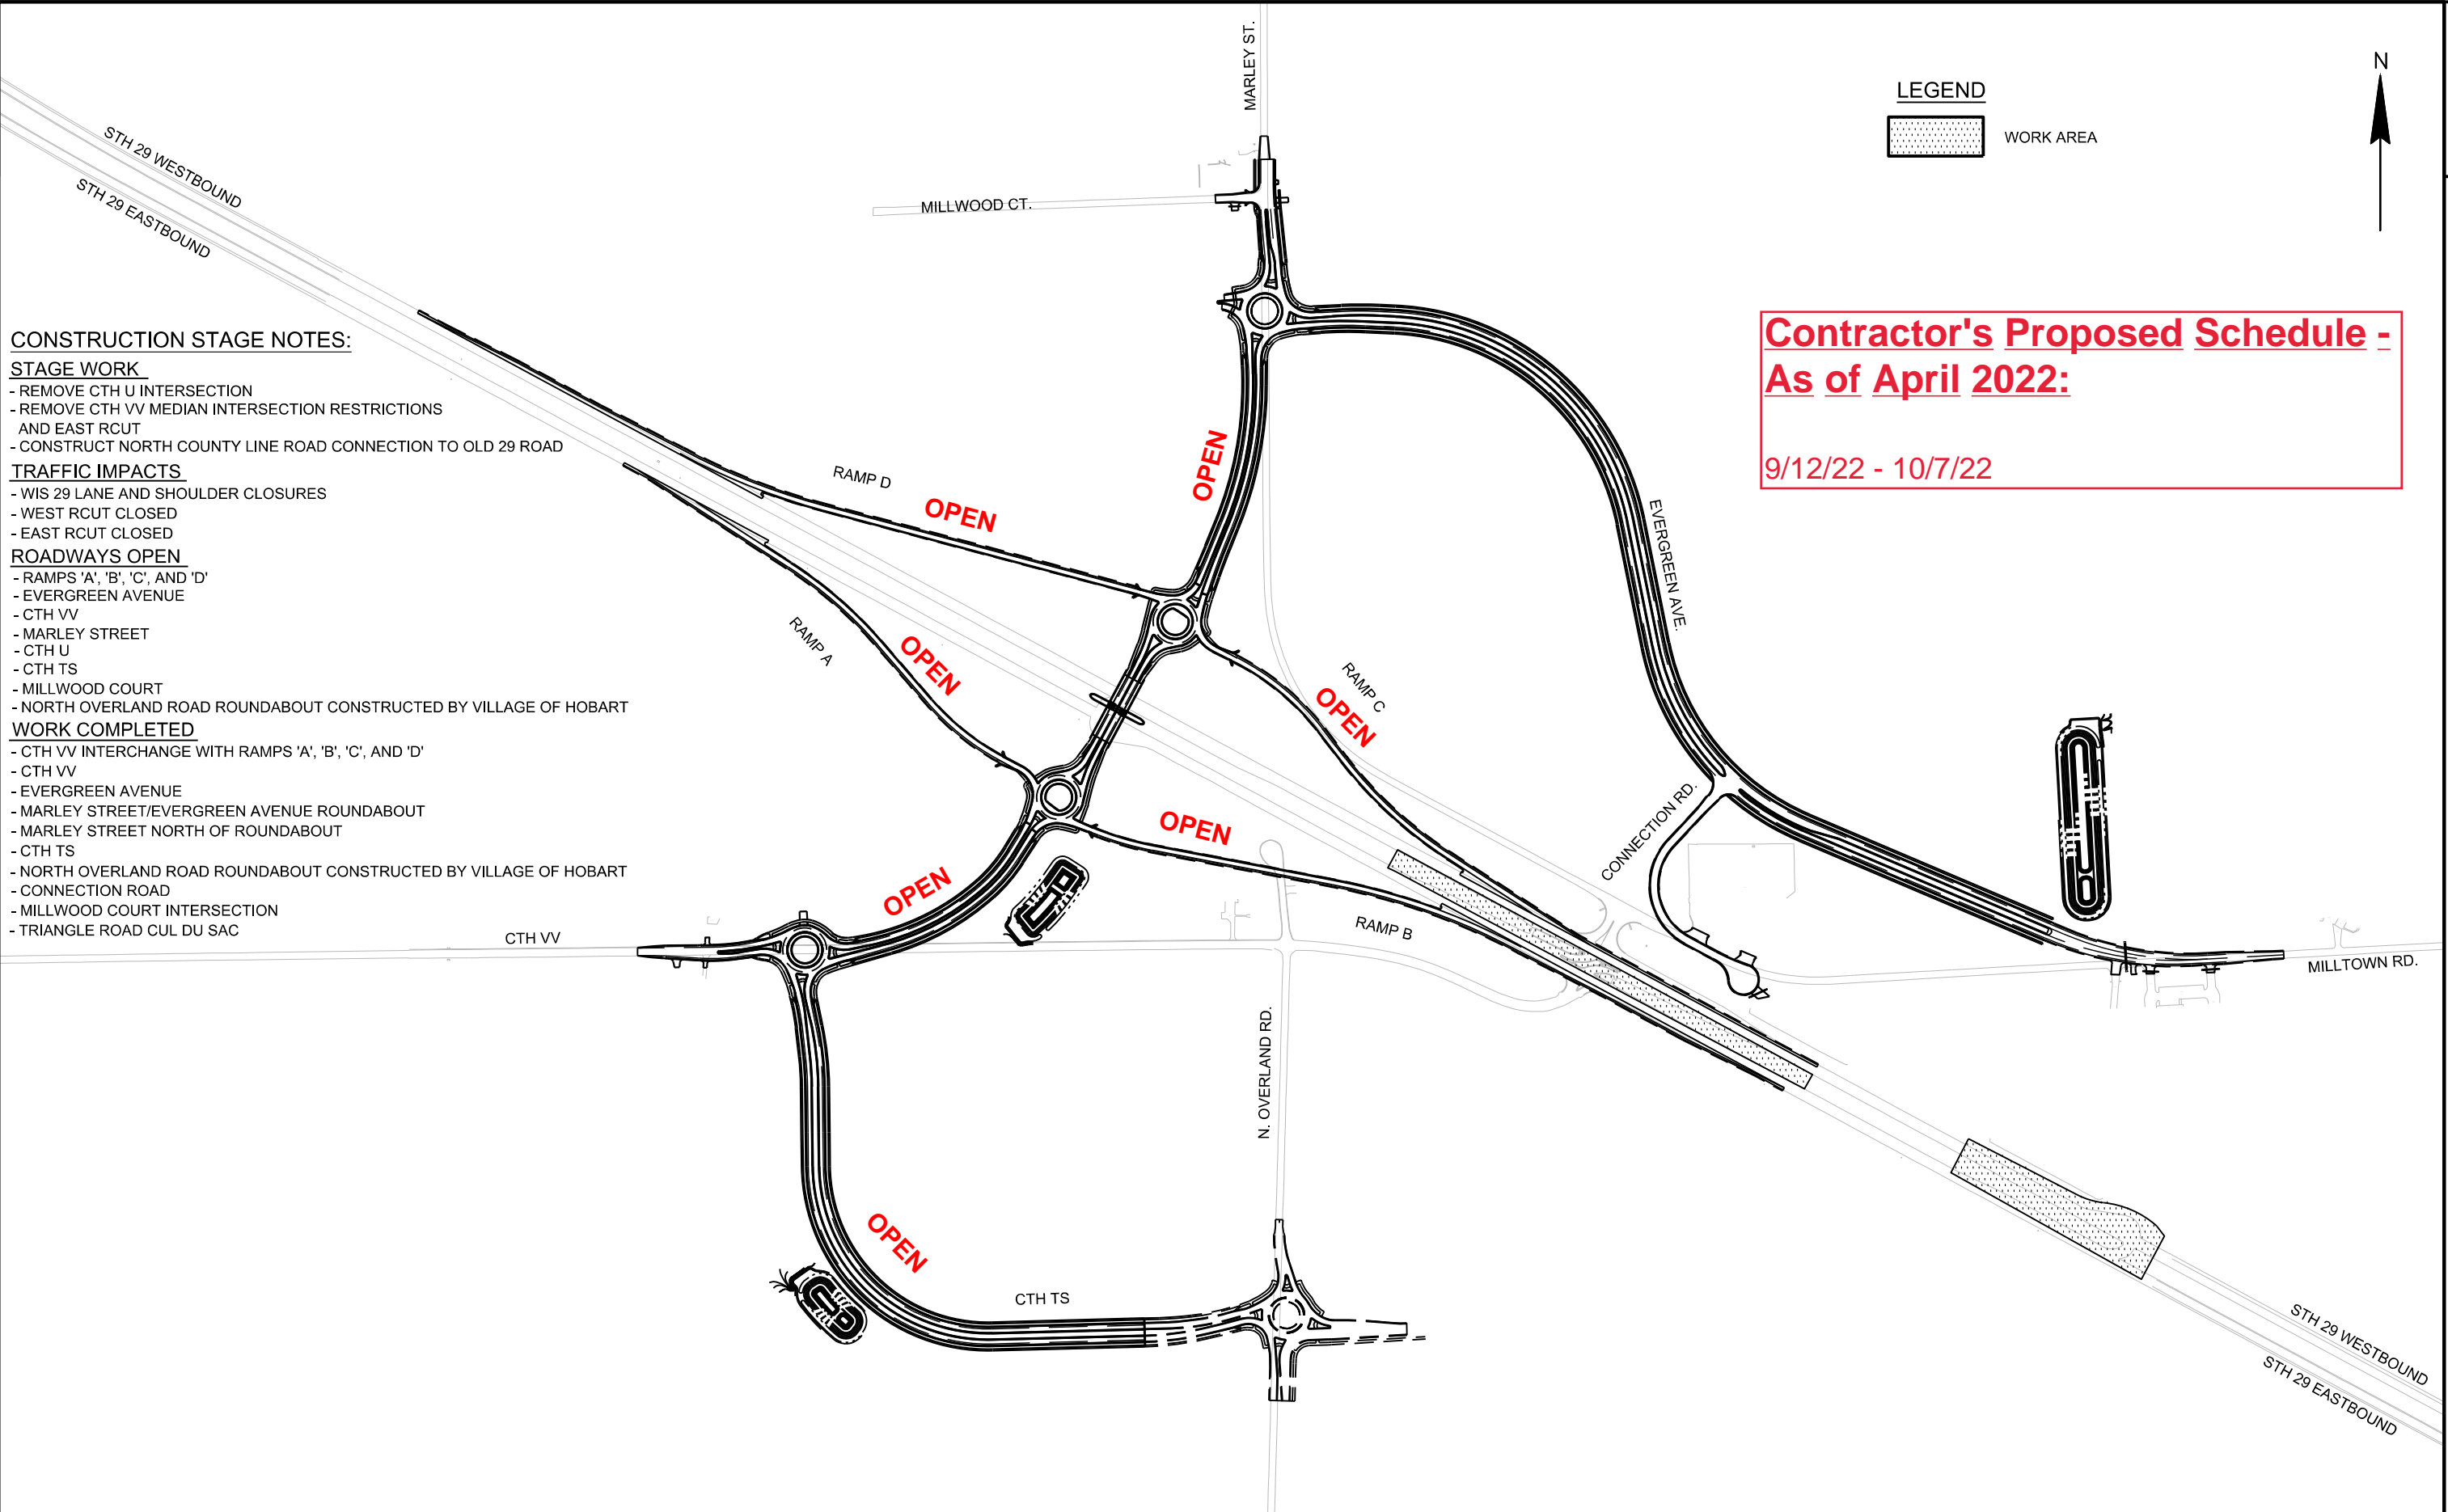


LEGEND

 WORK AREA



**Contractor's Proposed Schedule -
As of April 2022:**

10/10/22 - 10/14/22

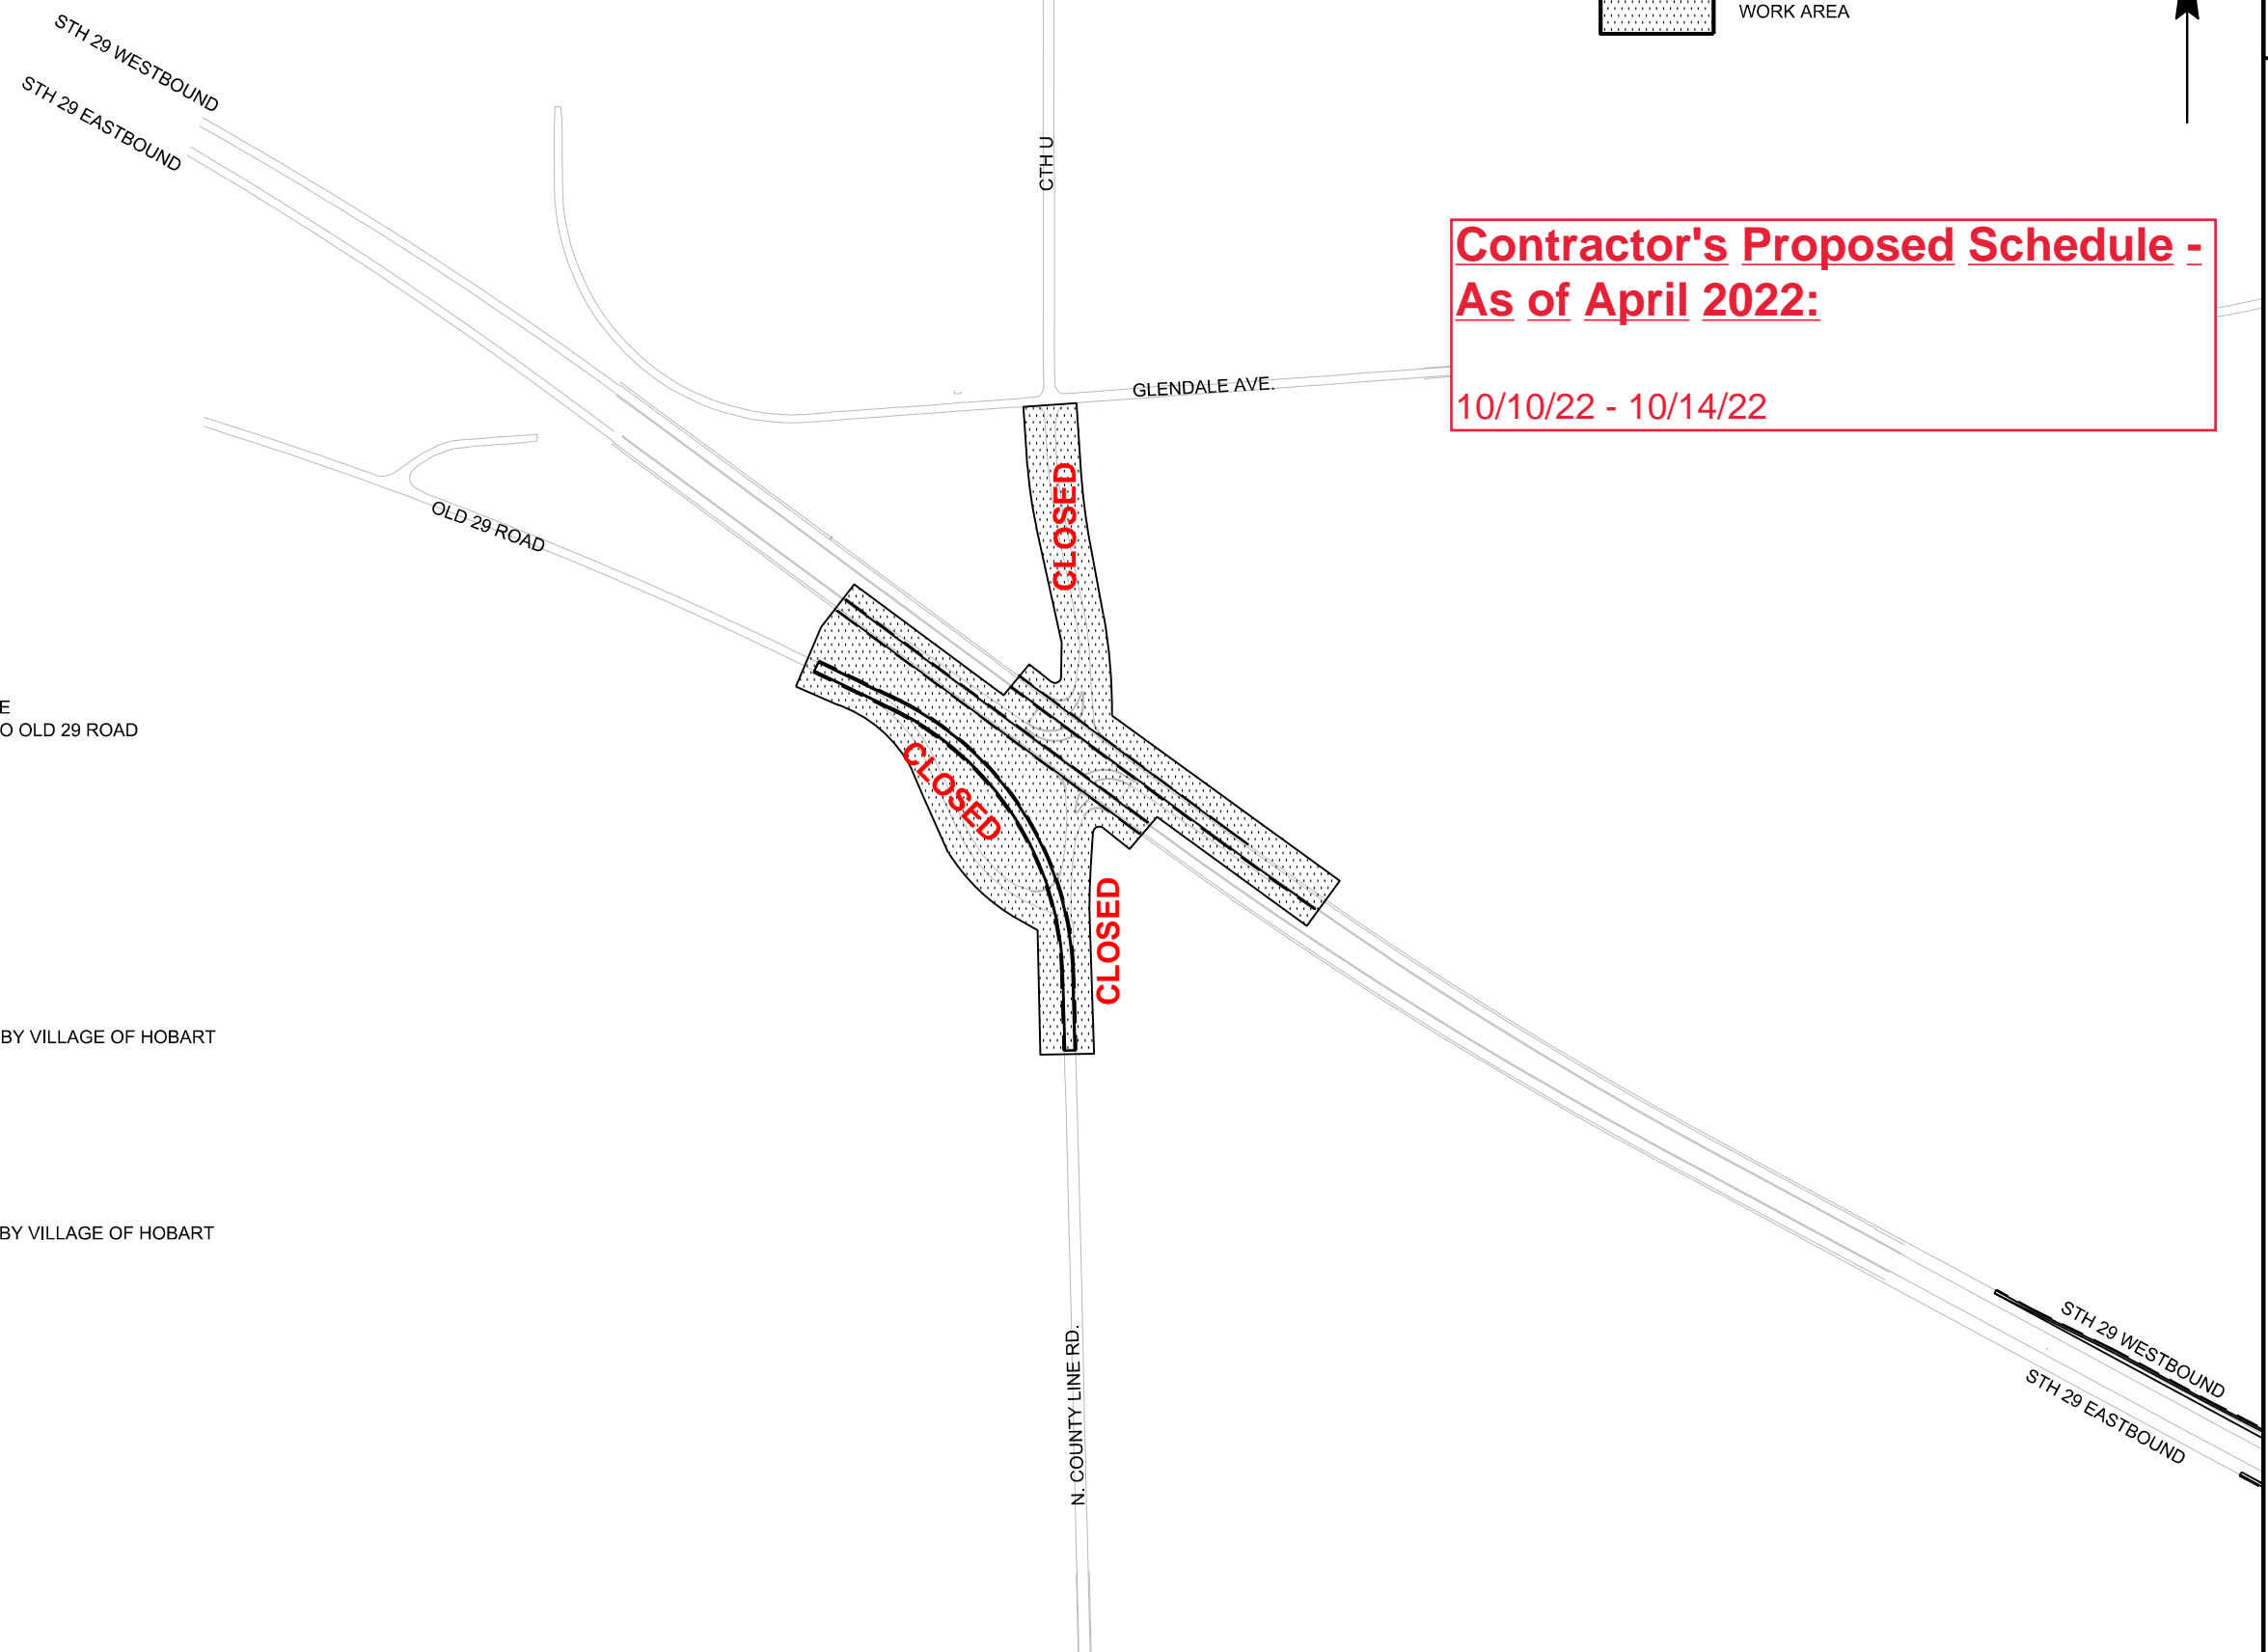

CONSTRUCTION STAGE NOTES:

STAGE WORK

- REMOVE CTH U INTERSECTION
- REMOVE CTH U BETWEEN WIS 29 AND GLENDALE AVENUE
- CONSTRUCT NORTH COUNTY LINE ROAD CONNECTION TO OLD 29 ROAD

TRAFFIC IMPACTS

- WIS 29 LANE AND SHOULDER CLOSURES
- WEST RCUT CLOSED
- EAST RCUT CLOSED

ROADWAYS OPEN

- RAMPS 'A', 'B', 'C', AND 'D'
- EVERGREEN AVENUE
- CTH VV
- MARLEY STREET
- CTH U
- CTH TS
- MILLWOOD COURT
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART

WORK COMPLETED

- CTH VV INTERCHANGE WITH RAMPS 'A', 'B', 'C', AND 'D'
- CTH VV
- EVERGREEN AVENUE
- MARLEY STREET/EVERGREEN AVENUE ROUNDABOUT
- MARLEY STREET NORTH OF ROUNDABOUT
- CTH TS
- NORTH OVERLAND ROAD ROUNDABOUT CONSTRUCTED BY VILLAGE OF HOBART
- CONNECTION ROAD
- MILLWOOD COURT INTERSECTION
- TRIANGLE ROAD CUL DU SAC
