

# US 18/151 (Town Hall Road to Fitchrona Road)

Weekly Construction Update: 6/30 – 7/7

## Town Hall Road to West Verona Avenue Interchange

#### **WORK PROGRESS:**

- Upper layer asphalt paving for the inside lanes has been completed
- Upper layer asphalt paving for the outside lanes is ongoing

#### **TRAFFIC & ACCESS IMPACTS:**

- Long-term single lane closures will continue. See page 3 for the 10-day outlook of anticipated lane closures
- Access to all driveways and side roads will be maintained at all times
- Ramp Closures:
  - Short-term ramp closures will occur at CTH G and CTH PD when asphalt paving operations work through the ramp areas
  - The CTH G EB on-ramp and EB off-ramp are scheduled to be closed from July 10 July 16
  - o The CTH PD WB on-ramp is scheduled to be closed July 12 July 18

# **West Verona Avenue Interchange to CTH PB**

#### **WORK PROGRESS:**

No work anticipated for this section of the project until mid-July

# **TRAFFIC & ACCESS IMPACTS:**

 Lane closures will not occur in this section of the project until the long-term lane closures from Town Hall Road to the West Verona Avenue Interchange are removed

## **CTH PB to Fitchrona Road**

#### **WORK PROGRESS:**

- Concrete pavement patching for the WB inside lane has been completed
- WB traffic is scheduled to be switched to the inside lane on Thursday, July 6
- Concrete pavement replacement for the EB inside lane is ongoing

#### TRAFFIC & ACCESS IMPACTS:

- Long term single lane closures will continue. See page 4 for the 10-day outlook of anticipated lane closures
- Ramp Closures:
  - The on-ramp from Williamsburg Way to WB US 18/151 will remain closed until mid-November
  - No additional ramp closures are anticipated for the week



# US 18/151 (Town Hall Road to Fitchrona Road)

Weekly Construction Update: 6/30 – 7/7

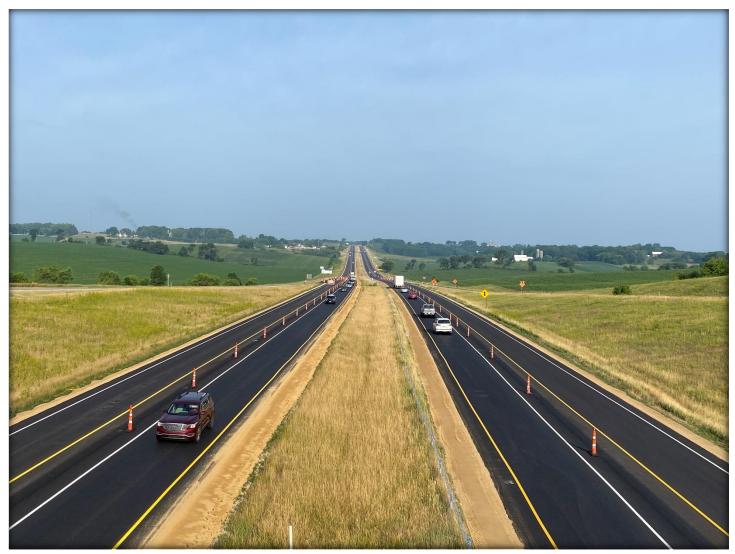


Photo above: Traffic driving on the recently completed final surface pavement for the inside lanes just west of CTH G

## For more information, contact:

Dustin Hunt US 18/151 Project Engineer (608) 286-9226 | <a href="mailto:dhunt@HNTB.com">dhunt@HNTB.com</a> Cody Kammerzelt
US 18/151 WisDOT Project Manager
(608) 219-1331 | Cody.Kammerzelt@dot.wi.gov



# Town Hall Road to West Verona Avenue Interchange

Anticipated Lane Closures - 10-Day Outlook

	WB/SB US 18/151	EB/NB US 18/151
FRI, 6/30		
SAT, 7/1		
SUN, 7/2		
MON, 7/3		
TUE, 7/4		
WED, 7/5		
THU, 7/6		
FRI, 7/7		
SAT, 7/8		
SUN, 7/9		



# **CTH PB to Fitchrona Road**

Anticipated Lane Closures - 10-Day Outlook

	WB/SB US 18/151	EB/NB US 18/151
FRI, 6/30		
SAT, 7/1		
SUN, 7/2		
MON, 7/3		
TUE, 7/4		
WED, 7/5		
THU, 7/6		
FRI, 7/7		
SAT, 7/8		
SUN, 7/9		

## **Project Location** 14 Project I.D. 1204-08-35/65 Mount Horeb - Madison (Town Hall Road to CTH PD) USH 18 **Dane County** $\widetilde{14}$ 12 **Project Location Dane County** 78 60 **CITY OF** 89 19 113 60 **MADISON** [12] 18 [51] 151 14 PD [151] Ρ VILLAGE OF MOUNT [12] **HOREB** PD 18 J [51] 18 78 [151] 14 [39] 92 59 CITY OF VERONA Windy \ Oak Ln Spring **CITY OF FITCHBURG** G 151 18 92 **Project Location** РΒ **Dane County** М MOUNT VERNON 69 Legend Long term lane closures anticipated to remain until mid-July Long term lane closures anticipated to remain until mid-November **69** Long term lane closures anticipated from mid-July to mid-November
