

State Project ID: 1206-06-79
US 12, Dane County
Whitney Way to I-39/90
Madison

Update Date: **April 29, 2022**

Project Weekly Update **(Madison Beltline Construction)**

General Project Information –

WisDOT is making the following improvements on the eastbound Madison Beltline (US 12) between Seminole Highway and Fish Hatchery Road.

- Extension of the auxiliary lane between the Todd Drive off-ramp and Todd Drive on-ramp.
- Widening of the eastbound bridge over Todd Drive for the auxiliary lane extension.
- Upgrades to traffic signal equipment for a portion of the South Frontage Road and Todd Drive intersection.

Traffic Impacts:

- Nighttime single and double lane closures will be occurring from approximately I-39 to Todd Drive for the EB and WB Beltline from 6:30 PM to 6:00 AM. Daytime shoulder closures will also be taking place for the EB and WB Beltline between Agricultural Drive to Fish Hatchery Road.
- **Todd Drive under the Beltline bridge is anticipated to be closed nightly starting May 2, 2022 through May 3, 2022 from 8pm to 6am for the setting of the bridge girders.**
- Traffic under the Todd Drive bridge is anticipated to be placed back in their original travel lanes the night of May 3, 2022.

Please refer to the following website link for anticipated specific closure locations (<https://projects.511wi.gov/flexlane/closures/>). Please note that work is weather dependent and may be subject to change.

Testing of the newly installed Lane Control Signs (LCS) will be ongoing. LED lights will likely be visible on the LCSs when testing of the LCS's occur. At this time, the Flex Lane is not operational and WisDOT will provide additional information at a later date as to when the Flex Lane will become operational.

Work this week (week of 5/2/2022)

- Crews will continue retaining wall forming, rebar placement, and concrete placement operations.
- Crews will begin bridge girder placement the night of May 2, 2022. At this time, Todd Drive under the Beltline bridge is anticipated to be closed nightly starting May 2, 2022 through May 3, 2022 from 8pm to 6am.
- Crews will continue storm sewer installations along the Todd Drive auxiliary lane extension.
- Crews will continue existing drainage cleanouts on the outside shoulders throughout the corridor.
- Crews will continue overhead sign structure inspections.


- Crews will continue 2021 punch list work throughout the corridor.
- Crews will place HMA pavement under the Todd Drive bridge.
- Crews will placement pavement marking under the Todd Drive bridge and anticipate to switch traffic under the bridge back to its original travel lanes the night of May 3, 2022.
- Crews will resume pavement removal and excavation to subgrade operations along with aggregate placement at the Todd Drive auxiliary lane extension.

Work next week (week of 5/9/2022)

- Crews will begin decking operations for the Todd Drive bridge structure widening.
- Crews will continue existing drainage cleanouts on the outside shoulders throughout the corridor.
- Crews will continue pavement removal and excavation to subgrade operations along with aggregate placement at the Todd Drive auxiliary lane extension.
- Crews are anticipated to complete the 2021 punch list work throughout the corridor.



Completed partial structure demolition operations.

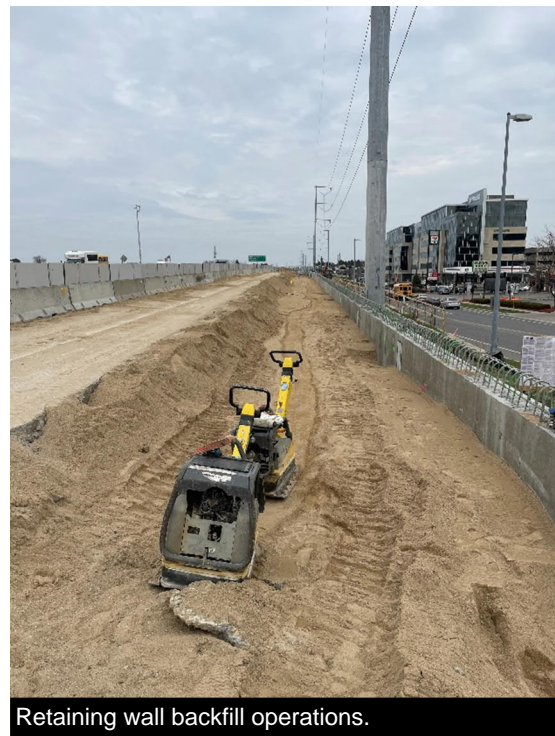

Retaining wall backfill operations.

Contact information

Trenton Diehl, Strand Associates, Inc.- Project Leader

Email: trenton.diehl@strand.com

If you would like to be added to the weekly update distribution list, please email your name and email address to trenton.diehl@strand.com. Thank you for your patience and understanding throughout this construction season.

Project Website

<https://projects.511wi.gov/flexlane/>
