

State Project ID: 1206-06-79
US 12, Dane County
Whitney Way to I-39/90
Madison

Update Date: **August 6, 2021**

Project Weekly Update **(Madison Beltline Construction)**

General Project Information –

WisDOT is making the following improvements on the Madison Beltline (US 12) between the Whitney Way exit and I-39/90 interchange.

- Resurface to address deteriorating pavement,
- Improve existing drainage deficiencies,
- Replace the existing median barrier wall, and
- Upgrade the Beltline median shoulders to be used part-time as travel lanes.

Project Schedule:

- Overall Completion Date: December 2021

Traffic Impacts:

- Nighttime single and double lane closures will be occurring from approximately Agriculture Drive to Verona Road for the EB and WB Beltline from 6:30 PM to 6:00 AM. Daytime shoulder closures will also be taking place for the EB and WB Beltline between Agricultural Drive to Fish Hatchery Road.
- Various ramp closures from Seminole Highway to Stoughton Road will also be taking place throughout any given night.
- EB and WB Beltline long term HMA paving operations will continue for the remainder of the construction season.


Please refer to the following website link for anticipated specific closure locations (<https://projects.511wi.gov/flexlane/closures/>). Please note that work is weather dependent and may be subject to change.

Work this week (week of 8/09/21)

- Crews will continue survey and layout operations throughout the project.
- Crews will continue median finish grading operations for concrete base from the Park Street to Seminole Highway.
- Crews will continue placing concrete base in the median from John Nolan Dr to Park Street.
- Crews will continue barrier wall footing from Fish Hatchery Road to Seminole Highway.
- Crews will continue barrier wall placement from John Nolan Drive to Park Street.
- Crews will continue placement of barrier wall transitions at sign structures from John Nolan Drive to Park Street.
- Crews will begin forming sign bases from Fish Hatchery Road to Seminole Highway.
- Crews anticipate placing HMA pavement on EB roadway from Fish Hatchery Road to the Yahara River bridge.
- Crews will begin replacing overhead Type I signs throughout the project.
- Crews will continue electrical installations throughout the project.



Concrete base patching operations with mobile concrete batch plant.

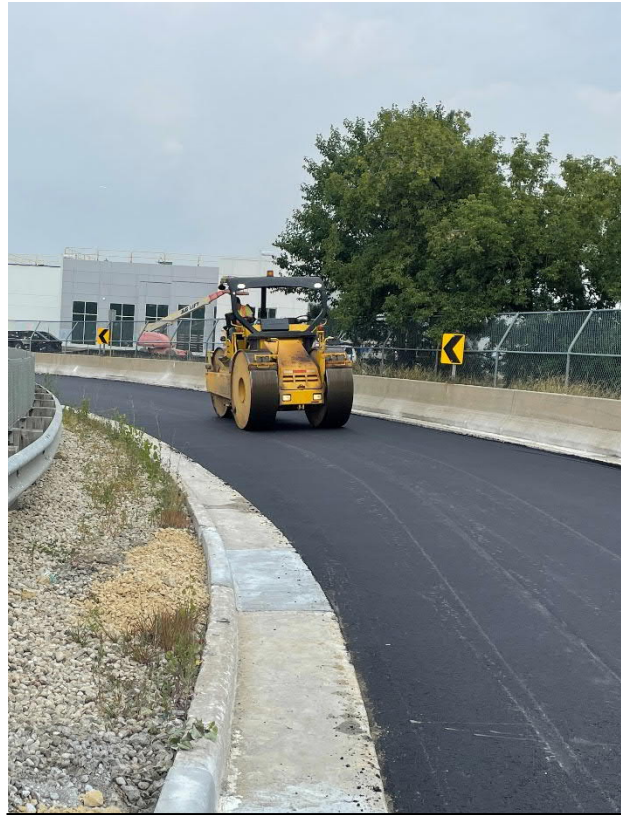

Fish Hatchery Road on ramp to the EB Beltline asphalt paving operation.

Work scheduled for the next week (week of 8/16/2021)

- Crews will continue survey and layout operations.
- Crews will continue electrical installations throughout the project.
- Crews will continue finish grading operations for concrete base from Fish Hatchery Road to Seminole Highway.
- Crews will continue placing concrete base from Rimrock Road to Fish Hatchery Road.
- Crews will continue barrier wall footing from Fish Hatchery Road to Seminole Highway.
- Crews will continue barrier wall placement from John Nolan Drive to Fish Hatchery Road.
- Crews will continue placement of barrier wall transitions at sign structures from John Nolan Drive to Park Street.
- Crews will continue HMA paving EB between Fish Hatchery Road to the Yahara River Bridge. Crews will also begin placing HMA pavement WB between the Yahara River bridge and Fish Hatchery Road.
- Crews will begin forming and pouring sign structures between Park Street and Seminole Highway.
- Crew may begin permanent pavement marking placement from the Yahara River bridge to I-39.

Contact information

Trenton Diehl, Strand Associates, Inc. - Project Leader

Email: trenton.diehl@strand.com

If you would like to be added to the weekly update distribution list, please email your name and email address to trenton.diehl@strand.com. Thank you for your patience and understanding throughout this construction season.

Project Website

<https://projects.511wi.gov/flexlane/>



HMA paving complete EB and WB from I-39 to the Yahara River bridge. Permanent pavement markings are being scheduled to be installed in the next few weeks.
