

## US 18/151 PROJECT (COUNTY G TO WIS 69)

# Weekly Construction Update


The Wisconsin Department of Transportation (WisDOT) is continuing construction along US 18/151 between County G and WIS 69 to address emerging traffic growth and operational deficiencies. Auxiliary lanes will be added, along with interchange and safety improvements. Construction began in March and is scheduled to be complete in late 2025.

### WORK PROGRESS

- **Military Ridge State Trail box culvert extensions:** Crews continuing structure backfill at the north extension, followed by removing the access road. Partial demolition work and sheeting installation is continuing on the south extension next week
- **County G/Dairy Ridge Road bridge:** Girder installation completed this week. Next week, crews will continue partial removals of the existing deck and parapet, and decking operations for the new bridge
- **W. Verona Avenue/Epic Lane entrance ramp to eastbound US 18/151:** Work continues at night with partial removals of existing abutments, deck and parapet. Slope widening at bridge abutments next week
- **Sugar River bridge widenings:** Partial removal of existing structures and cofferdam installation ongoing

### TRAFFIC ACCESS IMPACTS

- **The speed limit on US 18/151, between Spring Rose Road and WIS 69, is reduced to 55 mph when work is taking place**
- US 18/151, between County G and W. Verona Ave./Epic Lane, reduced to one lane in each direction through fall 2025
- County G/ Dairy Ridge Road over US 18/151 and the eastbound and westbound US 18/151 ramps at County G are closed through fall 2025
- Military Ridge Trail closed through **late summer**
- Overnight full closure of US 18/151 at County G **Monday-Wednesday nights, June 2-4; 10 p.m. - 5.a.m. (see detour below)**
- Overnight full closure of W. Verona Avenue/ Epic Lane entrance ramp to eastbound US 18/151 **Monday-Friday nights, June 2-6; 10 p.m. - 5.a.m.**

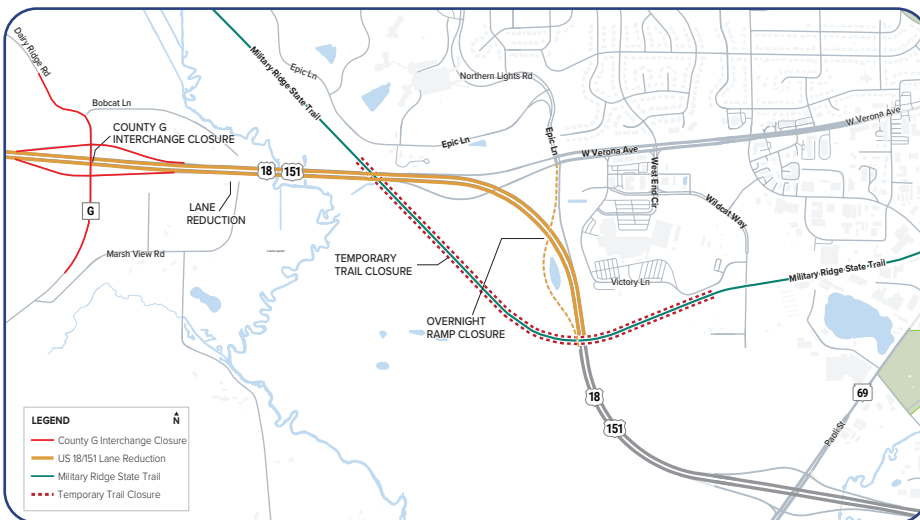

FOR PROJECT UPDATES,  
SCAN THE QR CODE OR VISIT  
<https://projects.511wi.gov/us18151-danecounty/>


#### CONTACT:

Barry Larson  
[BLarson@hntb.com](mailto:BLarson@hntb.com)  
(608) 209-1626



US 18/151 PROJECT (COUNTY G TO WIS 69)

# Weekly Construction Update

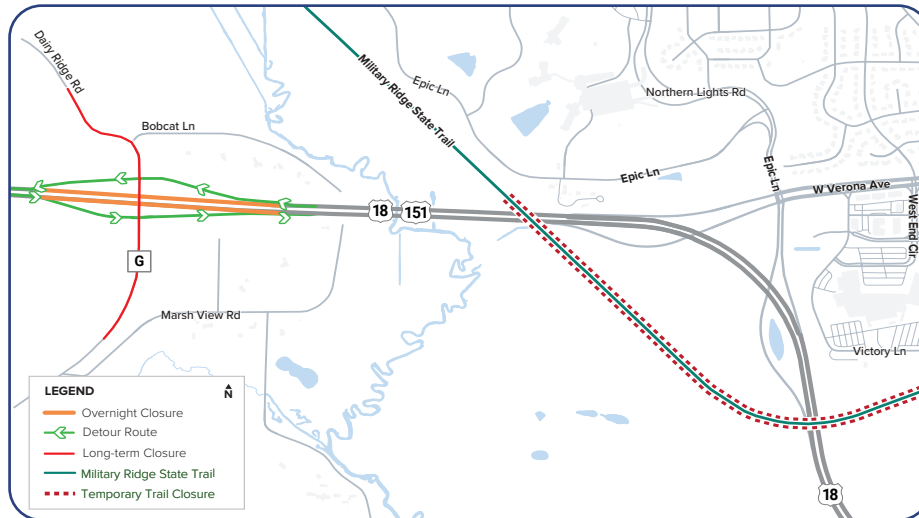

Above: Overnight full closure of US 18/151 at County G

*The project team thanks you for your patience and cooperation throughout this project!*



US 18/151 PROJECT (COUNTY G TO WIS 69)

# Weekly Construction Update



Above: Bridge deck removals at W. Verona Ave entrance ramp to eastbound US 18-151



Above: Prestressed concrete girders set in place at County G bridge

*The project team thanks you for your patience and cooperation throughout this project!*

