



State Project ID: 5845-16-77
US 51
Larson Beach Rd to Voges Rd
Dane County

Update Date: November 10, 2025

Project Weekly Update (US 51 Construction)

General Project Information – The US 51 project includes replacing the existing concrete pavement on US 51 northbound and southbound between Larson Beach Road and Voges Road. Reconstructing the US 51 southbound bridge over Taylor Road, Lower Yahara River Trail and the Wisconsin and Southern Railroad. Constructing single lane roundabouts at the Siggelkow Road ramp terminals and the addition of auxiliary lanes to US 51 north of Siggelkow Road. The project includes removals, excavations, base aggregate, concrete pavement, HMA pavement, concrete curb and gutter, concrete sidewalk, bridge and retaining wall structures, storm sewer, MGS guardrail, temporary shoring, erosion control, traffic control, restoration, pavement marking, permanent signing and street lighting.

Project Schedule - Overall Completion Date: November 26, 2025

Upcoming Stage / Traffic Impacts: Stage 4 - Stage 4 is scheduled to begin November 14, 2025 (weather dependent). Stage 4 entails work activities in the median that will include removal of temporary crossovers, curb and gutter, guardrail installation, and final restoration. Work also includes completing the remaining signing and restoration work on Siggelkow Rd.

- During Stage 4 all US 51 traffic will be shifted to their respective northbound and southbound lanes with daily single lane closures required in both directions to complete work in the US 51 median (See Attachment A).
- The US 51 exit and entrance ramps at the Siggelkow Rd. interchange will reopen with the exception of the northbound entrance ramp from Siggelkow Rd.
- The US 51 southbound exit ramp at the Siggelkow Rd. interchange remains open for southbound US 51 traffic that would like to travel east or west on Siggelkow Rd.
- Eastbound Siggelkow Rd. remains open to through traffic. Westbound Siggelkow Rd. will remain closed to through traffic between Paulson Rd./Triangle St. and Terminal Dr. until approximately November 26, 2025 (See Attachment B).
- Pedestrian routes on Siggelkow Rd. (between Terminal Dr. and Triangle St./Paulson Rd.) will utilize the sidewalks on the south side of Siggelkow Rd.

Upcoming Stage / Traffic Impacts: Substantial Completion - Substantial completion of the project is anticipated to occur by November 26, 2025. All lanes of US 51 northbound and southbound along with the Siggelkow Rd. interchange ramps will be opened and traffic control devices will be removed from the project. Siggelkow Road will be open to eastbound and westbound traffic and access to all ramps at the US 51 interchange will be available.

- Work on the project will end for the season; however, there will be a few minor items that will need to be completed such as installation of railings and staining of the Siggelkow Rd. retaining walls.
- Please note that with the late season completion of the project, there may be a need to complete some minor restoration and punchlist work in the spring of 2026. These final work operations will result in minimal impacts on traffic.



Work this week (week of 11/10/2025)

- Traffic using the SB US 51 exit ramp to Siggelkow Rd. will be shifted slightly to the east to complete the western portion of the ramp.
- Please note that northbound and southbound US 51 single lane closures will need to occur daily in order to facilitate installation of pavement markings, permanent signage and joints sealing.
- Crews will continue placement of curb and gutter and sidewalk on the north side of Siggelkow Rd. As part of this work pedestrian ramp and sidewalk/crosswalk improvements are being made at the intersection of Siggelkow Rd. and Paulson Rd./Triangle St. and the existing crosswalks at the intersection have been temporarily closed. Pedestrian detour signs are installed to delineate pedestrian routes while the work in this intersection is being completed (See Attachment C).
- Crews will be sealing joints for the new concrete pavement at the Siggelkow Rd. roundabouts. Please note that the contractor intends to perform this work utilizing traffic flagging and short-term stoppages of traffic on Siggelkow Road will be required.

Work scheduled for the next week (week of 11/17/2025)

- Crews will remove temporary crossovers in the US 51 median and perform final grading and restoration of the median.
- Joint sealing, rumble strips, and installation of permanent pavement markings will occur on northbound and southbound US 51. Please note that northbound and southbound US 51 single lane closures will need to occur daily in order to facilitate this work.
- Installation of permanent signage, pavement markings and final restoration will occur on Siggelkow Rd. and the associated US 51 ramps.

Please be alert when traveling the US 51 corridor. Please also note that work is weather dependent and may be subject to change. Thank you in advance for your patience throughout the construction season.

Contact information


Kevin Drunasky, WisDOT - Project Manager
Email: kevin.drunasky@dot.wi.gov

Dave Eisentraut, Strand Associates, Inc.- Project Leader
Email: david.eisentraut@strand.com

If you would like to be added or removed from the weekly update distribution list, please email your name and email address to david.eisentraut@strand.com.

Project Website


<https://projects.511wi.gov/us51-larsonvoges/>

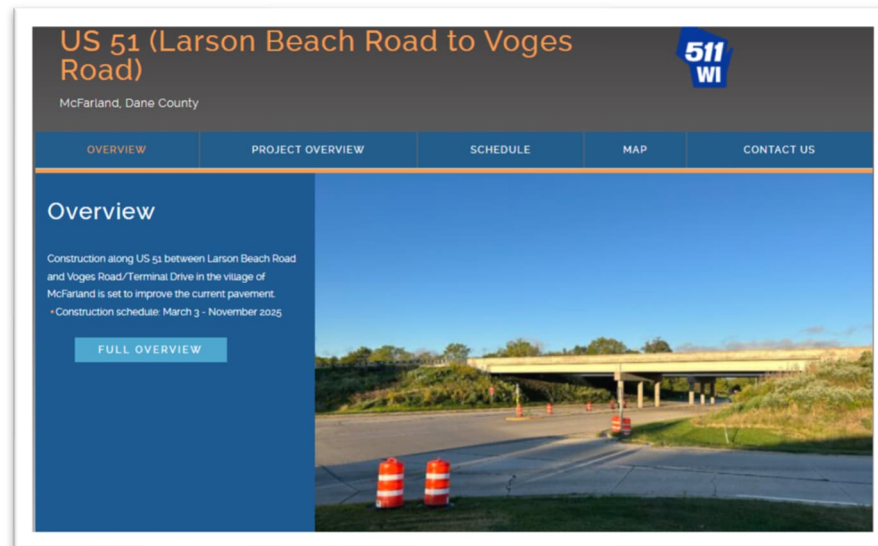

Siggelkow Road (East Roundabout)




STAGE 4 ANTICIPATED TO BEGIN 11/14/25

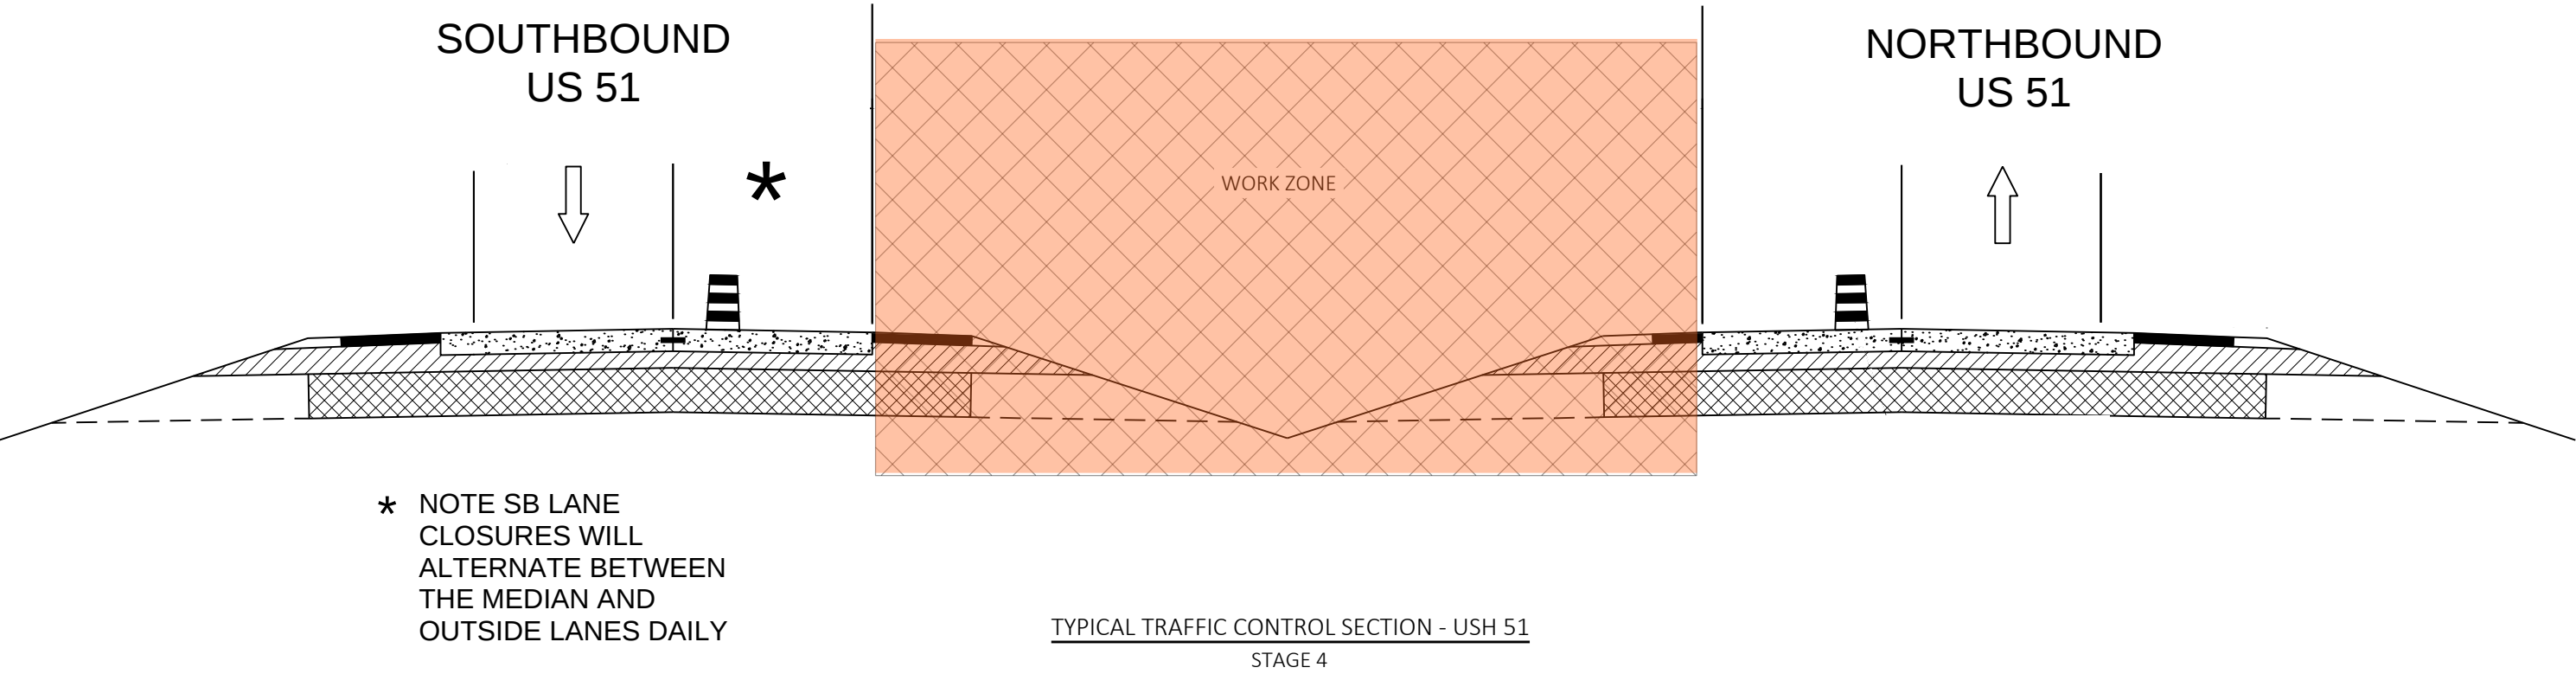

Stage 2C Construction Siggelkow Road

(REMAINING WORK ANTICIPATED TO BE COMPLETE BY 11/26/25)

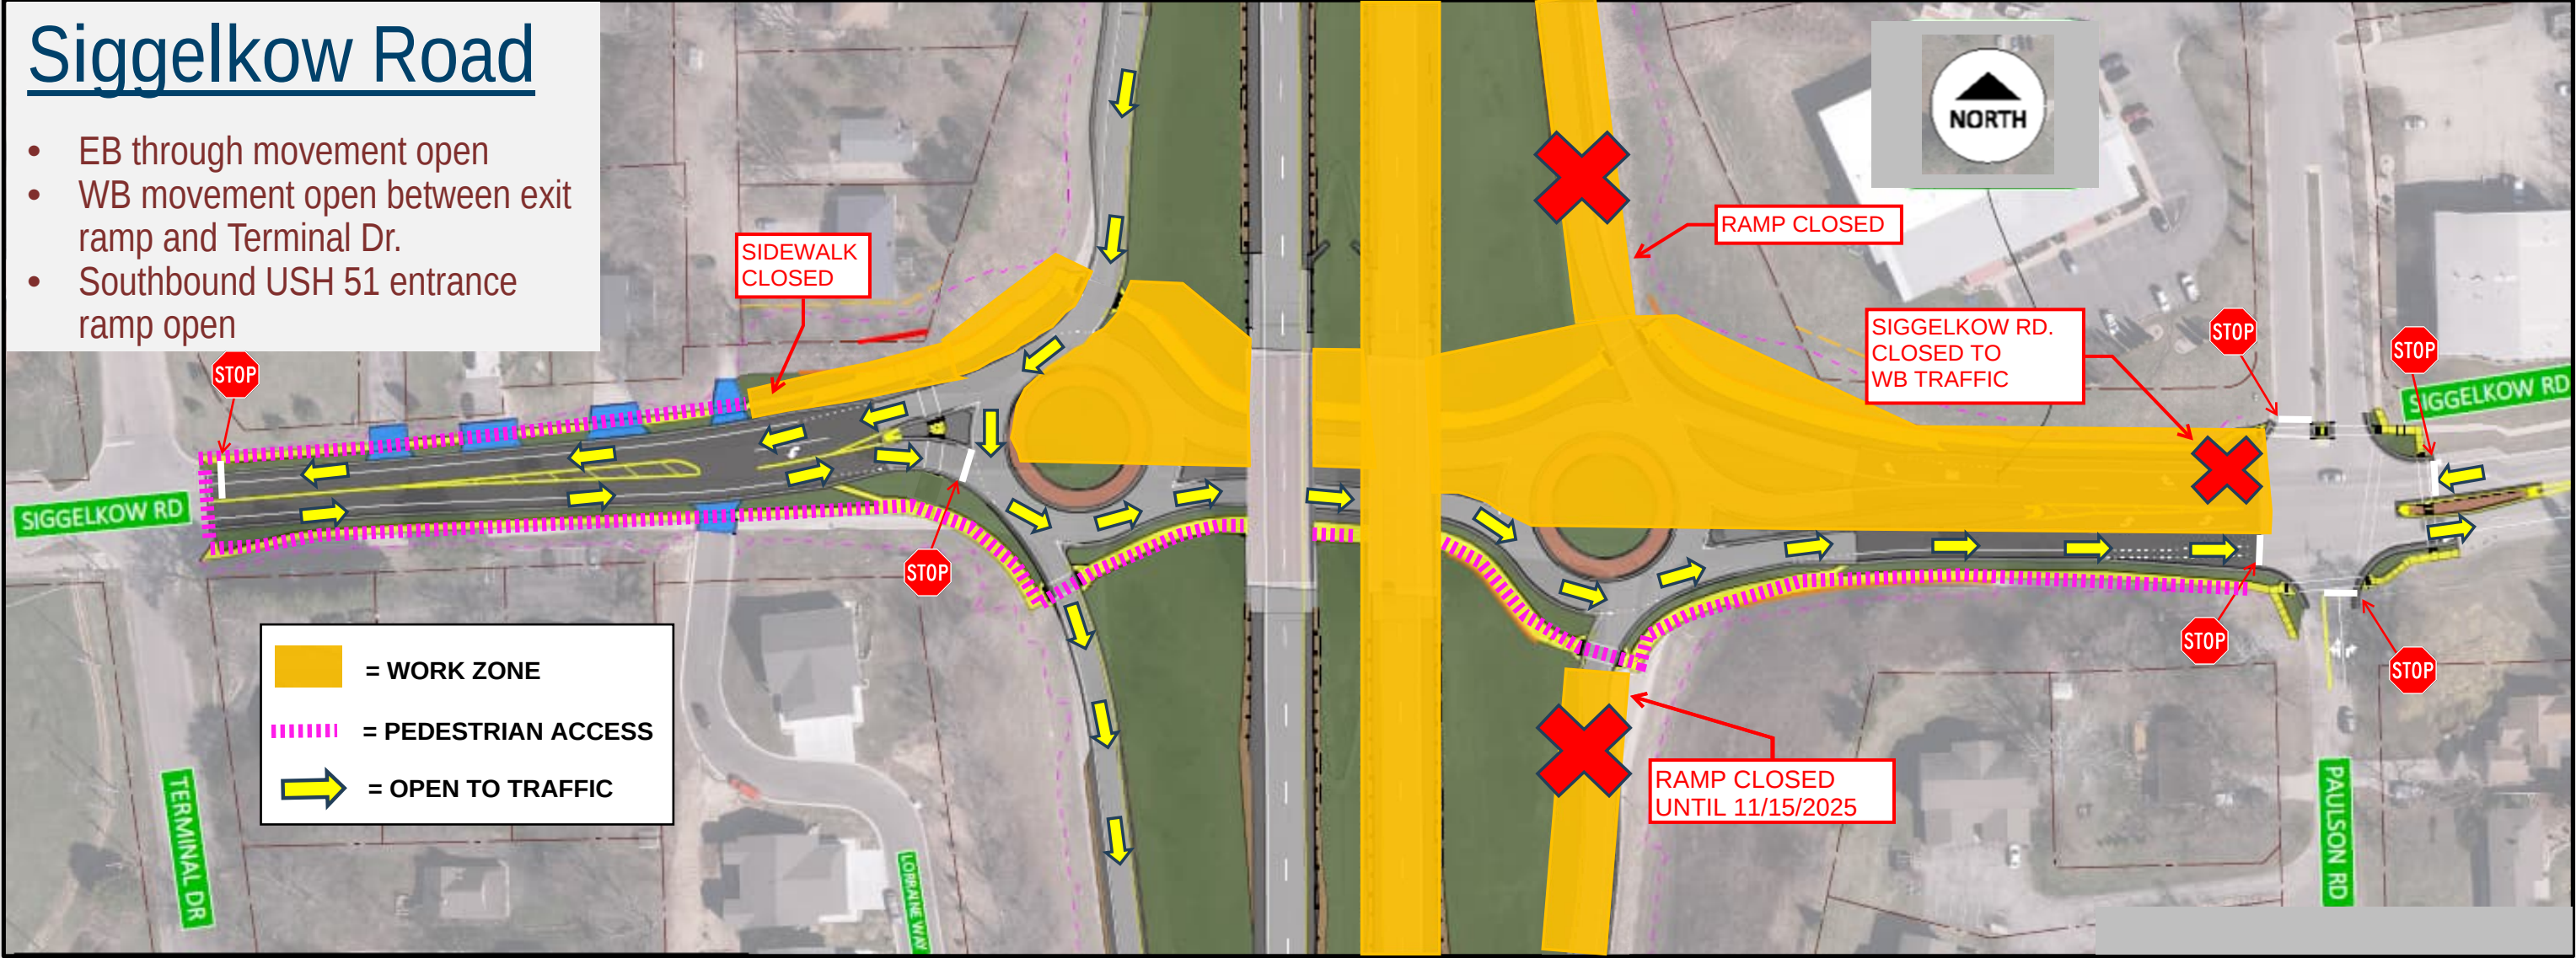

SIGGELKOW RD. PEDESTRIAN DETOUR
PAULSON RD. / TRIANGLE ST. INTERSECTION
(ANTICIPATED TO BE COMPLETE BY 11/26/25)

LEGEND:

- WORK AREA
- DIRECTION OF VEHICULAR TRAFFIC
- PEDESTRIAN TRAFFIC
- PEDESTRIAN DETOUR
- TRAFFIC CONTROL SIGN ON TEMPORARY/PERMANENT SUPPORT
- TRAFFIC CONTROL BARRICADES TYPE II WITH / WITHOUT ATTACHED SIGN AND WITH TWO TYPE "A" LIGHTS
- CONCRETE BARRIER TEMPORARY PRECAST
- TEMPORARY PEDESTRIAN BARRICADE
- TRAFFIC CONTROL DRUM WITH / WITHOUT TYPE "C" LIGHT

