



State Project ID: 5845-16-77
US 51
Larson Beach Rd to Voges Rd
Dane County

Update Date: August 15, 2025

Project Weekly Update (US 51 Construction)

General Project Information – The US 51 project includes replacing the existing concrete pavement on US 51 northbound and southbound between Larson Beach Road and Voges Road. Reconstructing the US 51 southbound bridge over Taylor Road, Lower Yahara River Trail and the Wisconsin and Southern Railroad. Constructing single lane roundabouts at the Siggelkow Road ramp terminals and the addition of auxiliary lanes to US 51 north of Siggelkow Road. The project includes removals, excavations, base aggregate, concrete pavement, HMA pavement, concrete curb and gutter, concrete sidewalk, bridge and retaining wall structures, storm sewer, MGS guardrail, temporary shoring, erosion control, traffic control, restoration, pavement marking, permanent signing and street lighting.

Project Schedule - Overall Completion Date: November 21, 2025

Current Stage / Traffic Impacts: Stage 2B - Work entails the construction of the US 51 southbound lanes and associated US 51 ramps at the Siggelkow Rd. interchange and the southern portion of Siggelkow Rd. (between Terminal Dr. and Paulson Rd./Triangle St.).

- US 51 traffic will remain shifted to the existing northbound lanes in a bi-directional traffic configuration until approximately August 26, 2025.
- The US 51 northbound exit and entrance ramp as well as the southbound entrance ramp at the Siggelkow Rd. interchange are currently closed to traffic.
- The US 51 southbound exit ramp at the Siggelkow Rd. interchange is open for southbound US 51 traffic that would like to travel east on Siggelkow Rd.; however, Siggelkow Rd. will remain closed to through traffic (between Terminal Dr. and Paulson Rd./Triangle St.) until early September (See Attachment A).
- Taylor Rd. is open to local through traffic. Please be aware that the north and south sides of Taylor Rd. will remain an active work zone until the end of August 2025.
- The Lower Yahara River Trail remains detoured until the end of August. Please follow the signs that indicate the current detour route for the trail (See Attachment B).
- Pedestrian routes on Siggelkow Rd. (between Terminal Dr. and Triangle St./Paulson Rd.) are delineated with detour signs and temporary pedestrian barricades. Please note that the contractor intends to adjust pedestrian routes to the south side of Siggelkow Rd. on approximately August 20, 2025 (See Attachment C).

Upcoming Stage / Traffic Impacts: Stage 3 - Stage 3 is anticipated to begin approximately August 26, 2025 (weather dependent).

- During Stage 3 all US 51 traffic will be shifted onto the new southbound lanes in a bi-directional traffic configuration that will be similar to the current Stage 2 configuration (See Attachment D).



- The US 51 northbound exit and entrance ramp and southbound entrance ramp at the Siggelkow Rd. interchange will remain closed.
- The US 51 southbound exit ramp at the Siggelkow Rd. interchange will be open for southbound US 51 traffic that would like to travel east on Siggelkow Rd.
- Siggelkow Rd. will remain closed to through traffic (between Terminal Dr. and Paulson Rd./Triangle St.) until early September.

Work this week (week of 8/18/2025)

- Concrete pavement will be placed for the remainder of southbound US 51 and for the southern portions of the Siggelkow Rd. roundabouts.
- Electrical installations for streetlights will be completed on Siggelkow Rd.
- Topsoil and restoration items will continue throughout the project.
- Installation of asphalt shoulders on southbound US 51 will be completed.
- Restoration work, slope paving and roadway paving underneath the Taylor Rd. overpass will continue. Please note that short-term traffic stoppages on Taylor Rd. will be required.
- Crews will begin placing temporary pavement markings on southbound US 51 to prepare for the upcoming traffic switch.

Work scheduled for the next week (week of 8/25/2025)

- The Stage 3 traffic switch is anticipated to occur on Tuesday 8/26/25 (weather dependent). The traffic switch will move all US 51 traffic into a bi-directional configuration on the newly constructed southbound lanes of US 51.
- Topsoil placement and restoration work will continue throughout the project.
- Crews will begin placing temporary pavement markings on southbound US 51 to prepare for the upcoming traffic switch.
- Final grading and asphalt paving for Stage 2B will be completed on Siggelkow Rd.

Please be alert when traveling the US 51 corridor. Please also note that work is weather dependent and may be subject to change. Thank you in advance for your patience throughout the construction season.

Contact information


Kevin Drunasky, WisDOT - Project Manager
Email: kevin.drunasky@dot.wi.gov

Dave Eisentraut, Strand Associates, Inc.- Project Leader
Email: david.eisentraut@strand.com

If you would like to be added or removed from the weekly update distribution list, please email your name and email address to david.eisentraut@strand.com.

Project Website

<https://projects.511wi.gov/us51-larsonvoges/>

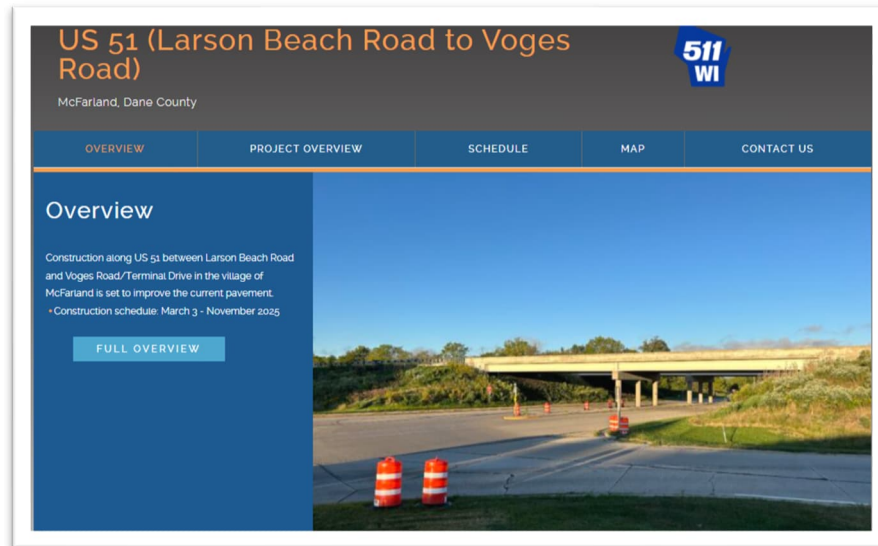

Siggelkow Road West Roundabout





Stage 2B Construction


(Current to Approximately Early September 2025)

Siggelkow Road

- Closed between Terminal Dr. and Paulson Rd./Triangle St.
- SB off ramp open to east
- Taylor Rd. is open to through traffic (Note: short term stoppages may be required)

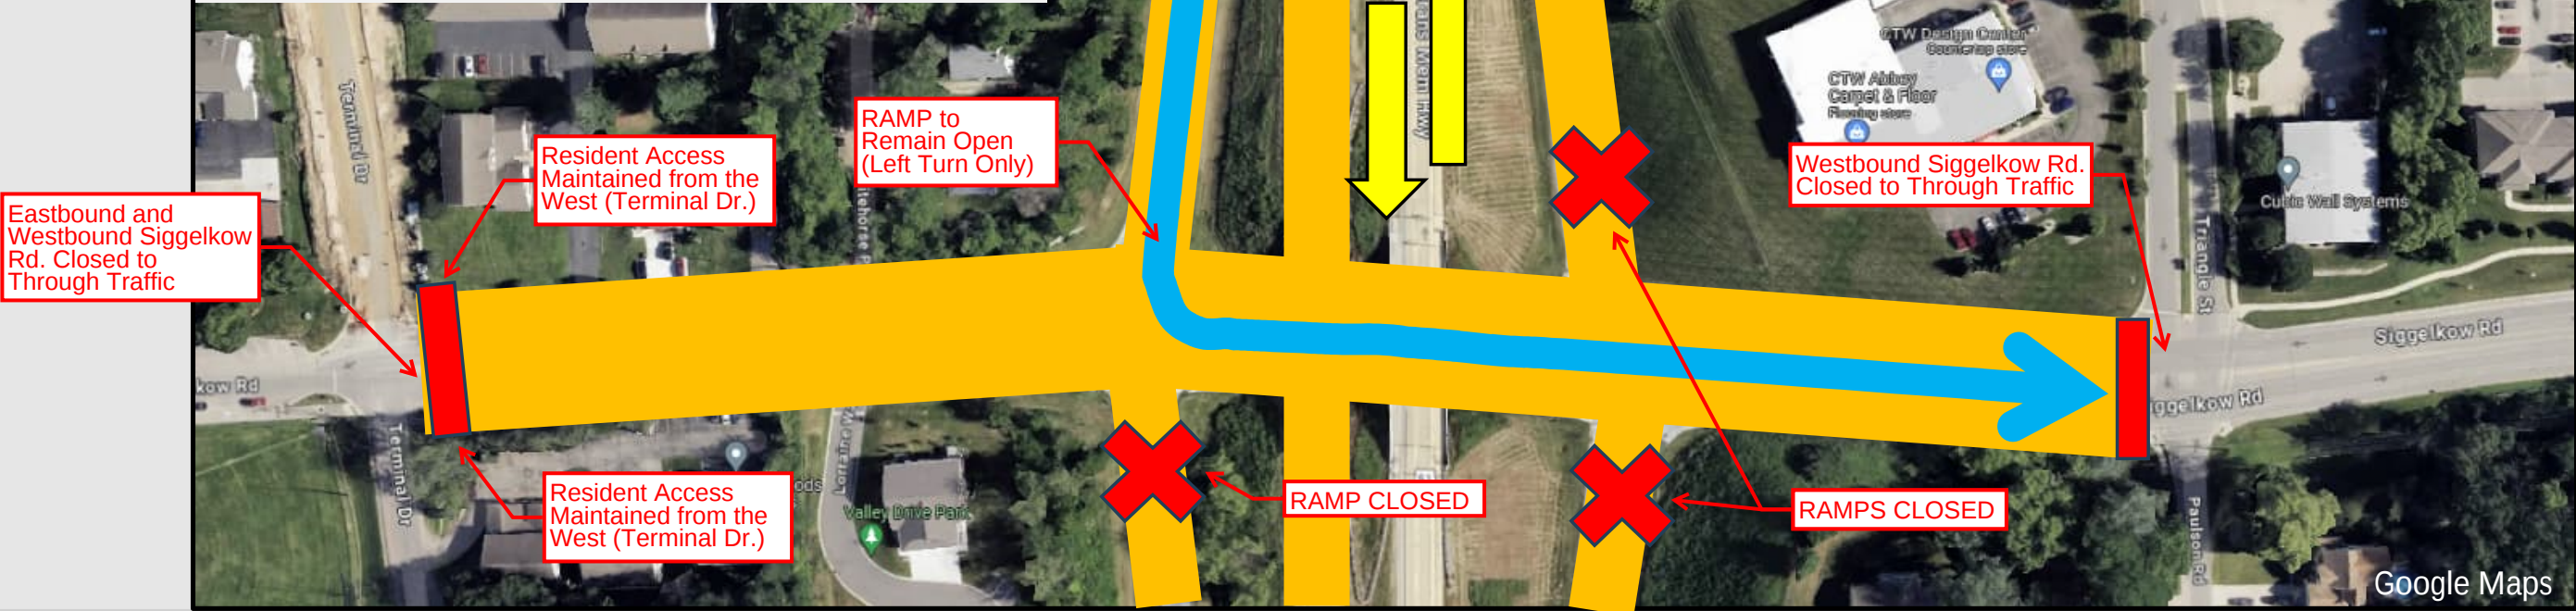

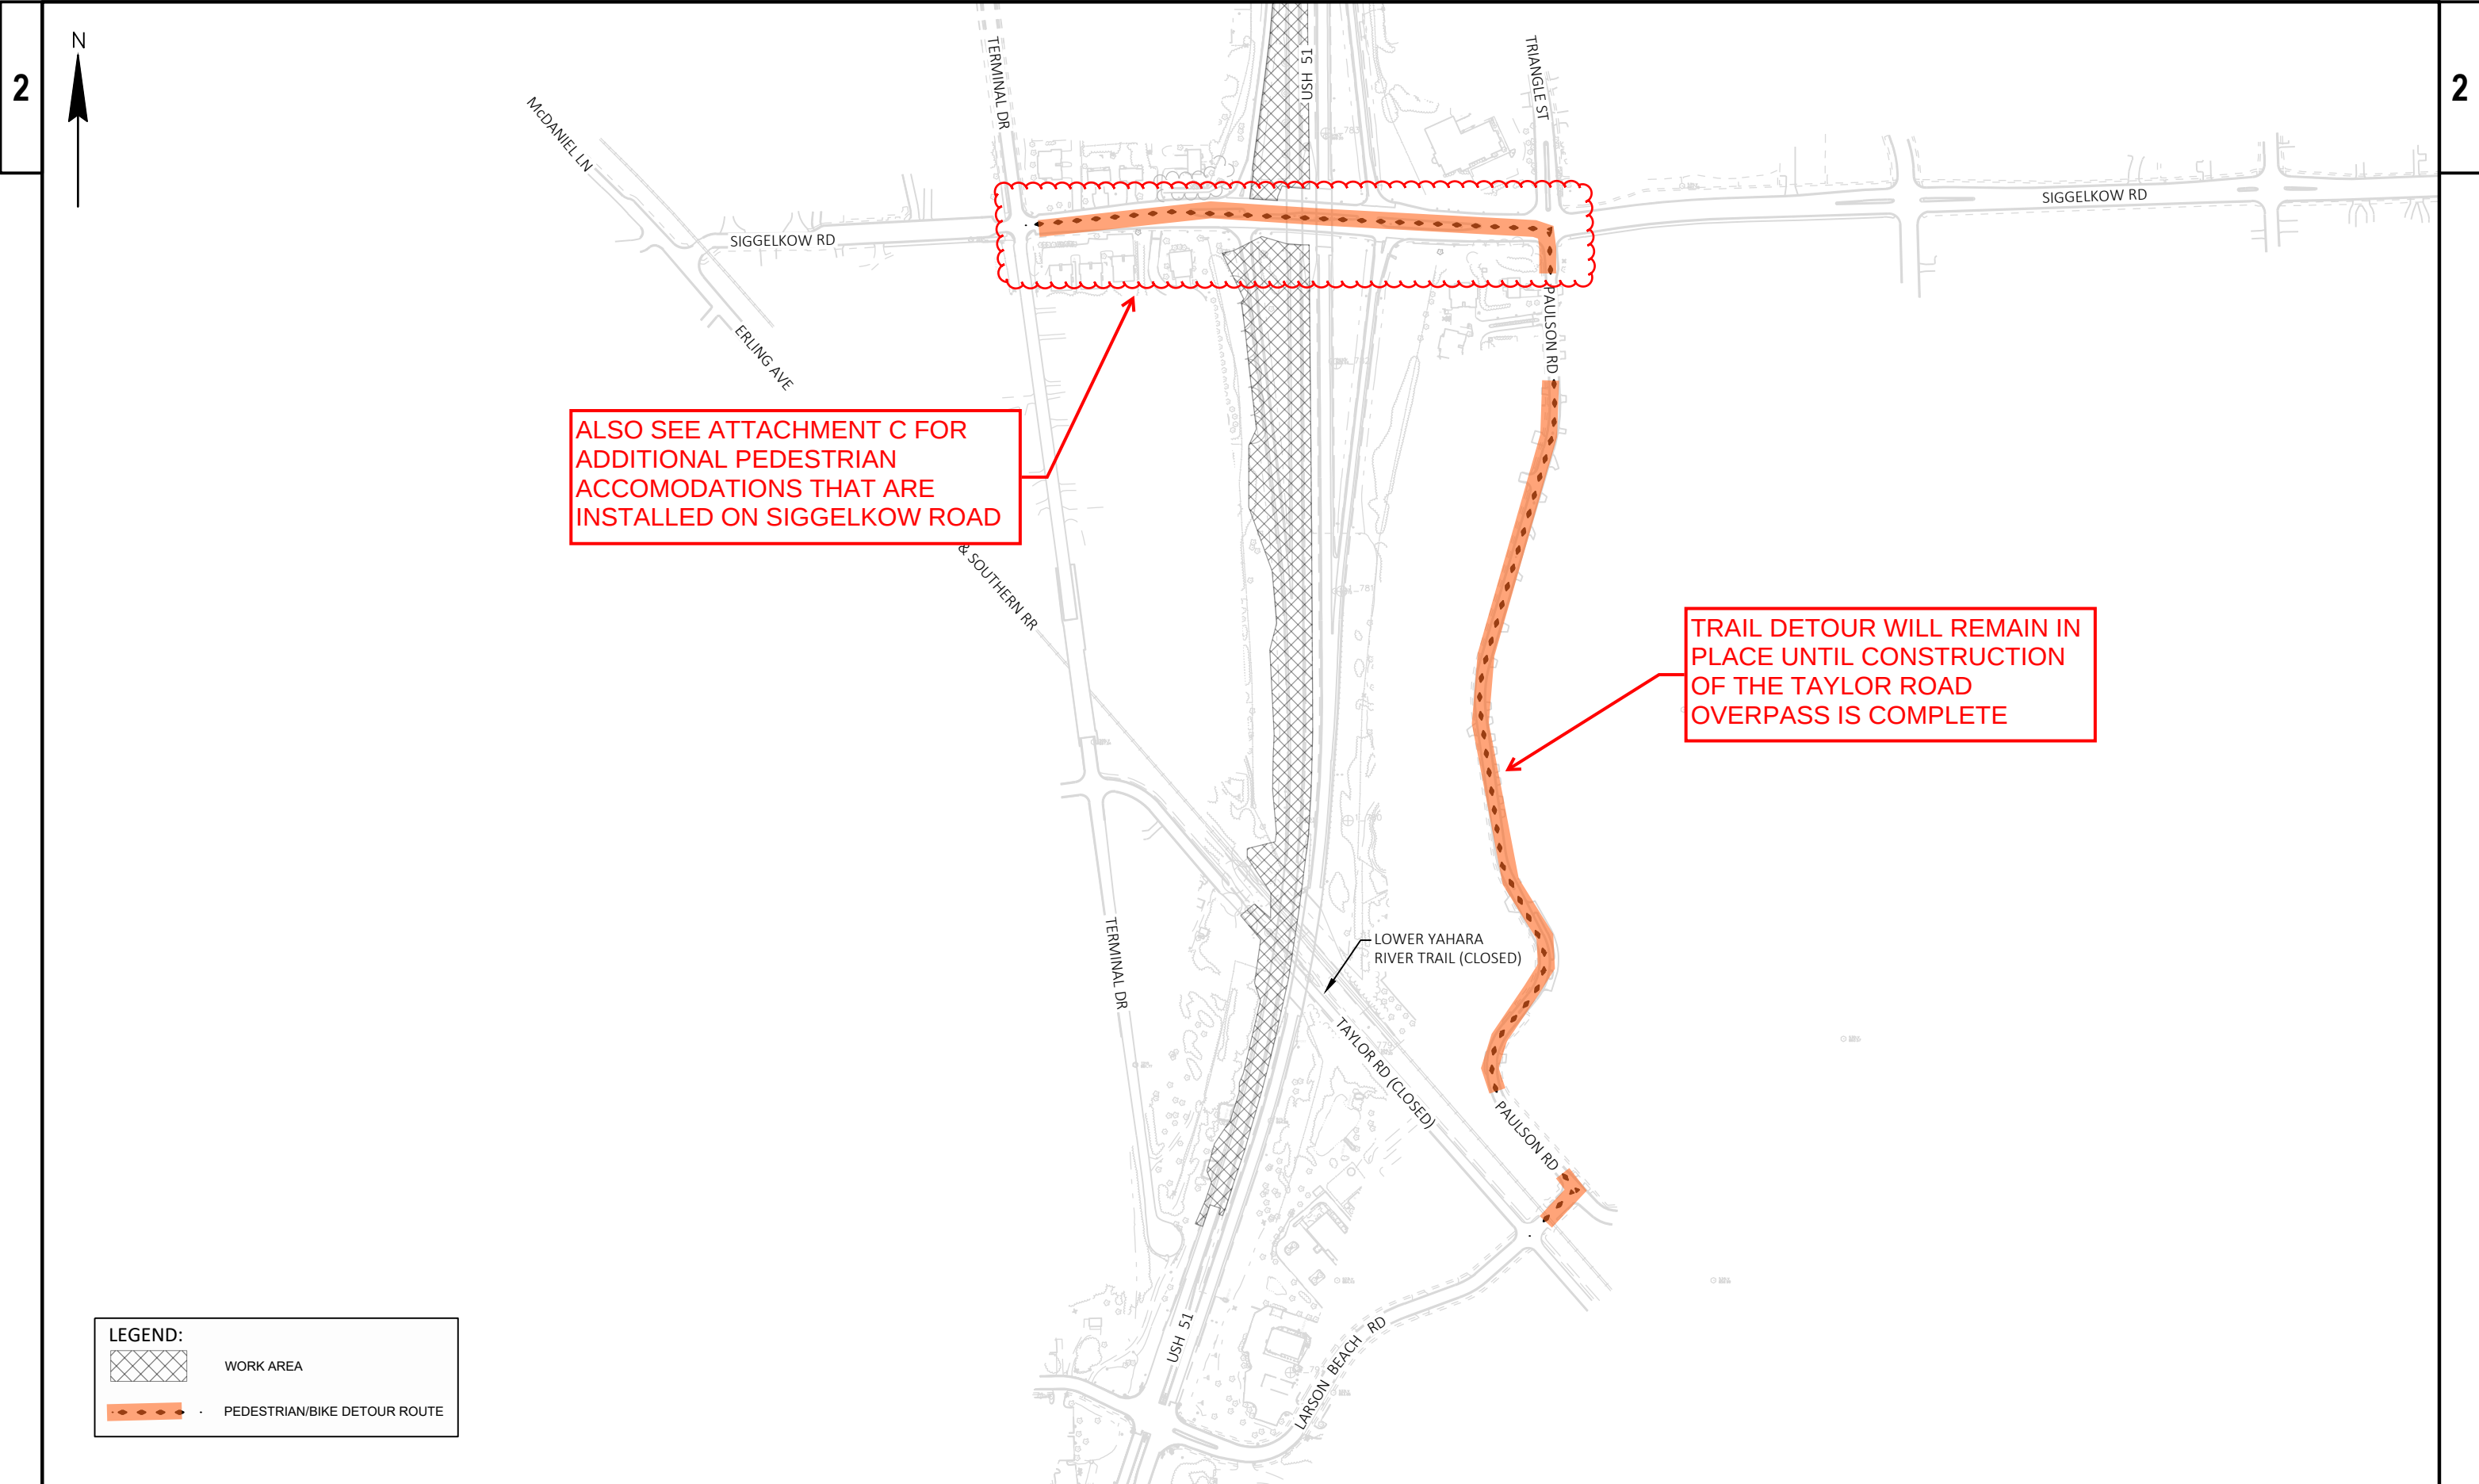

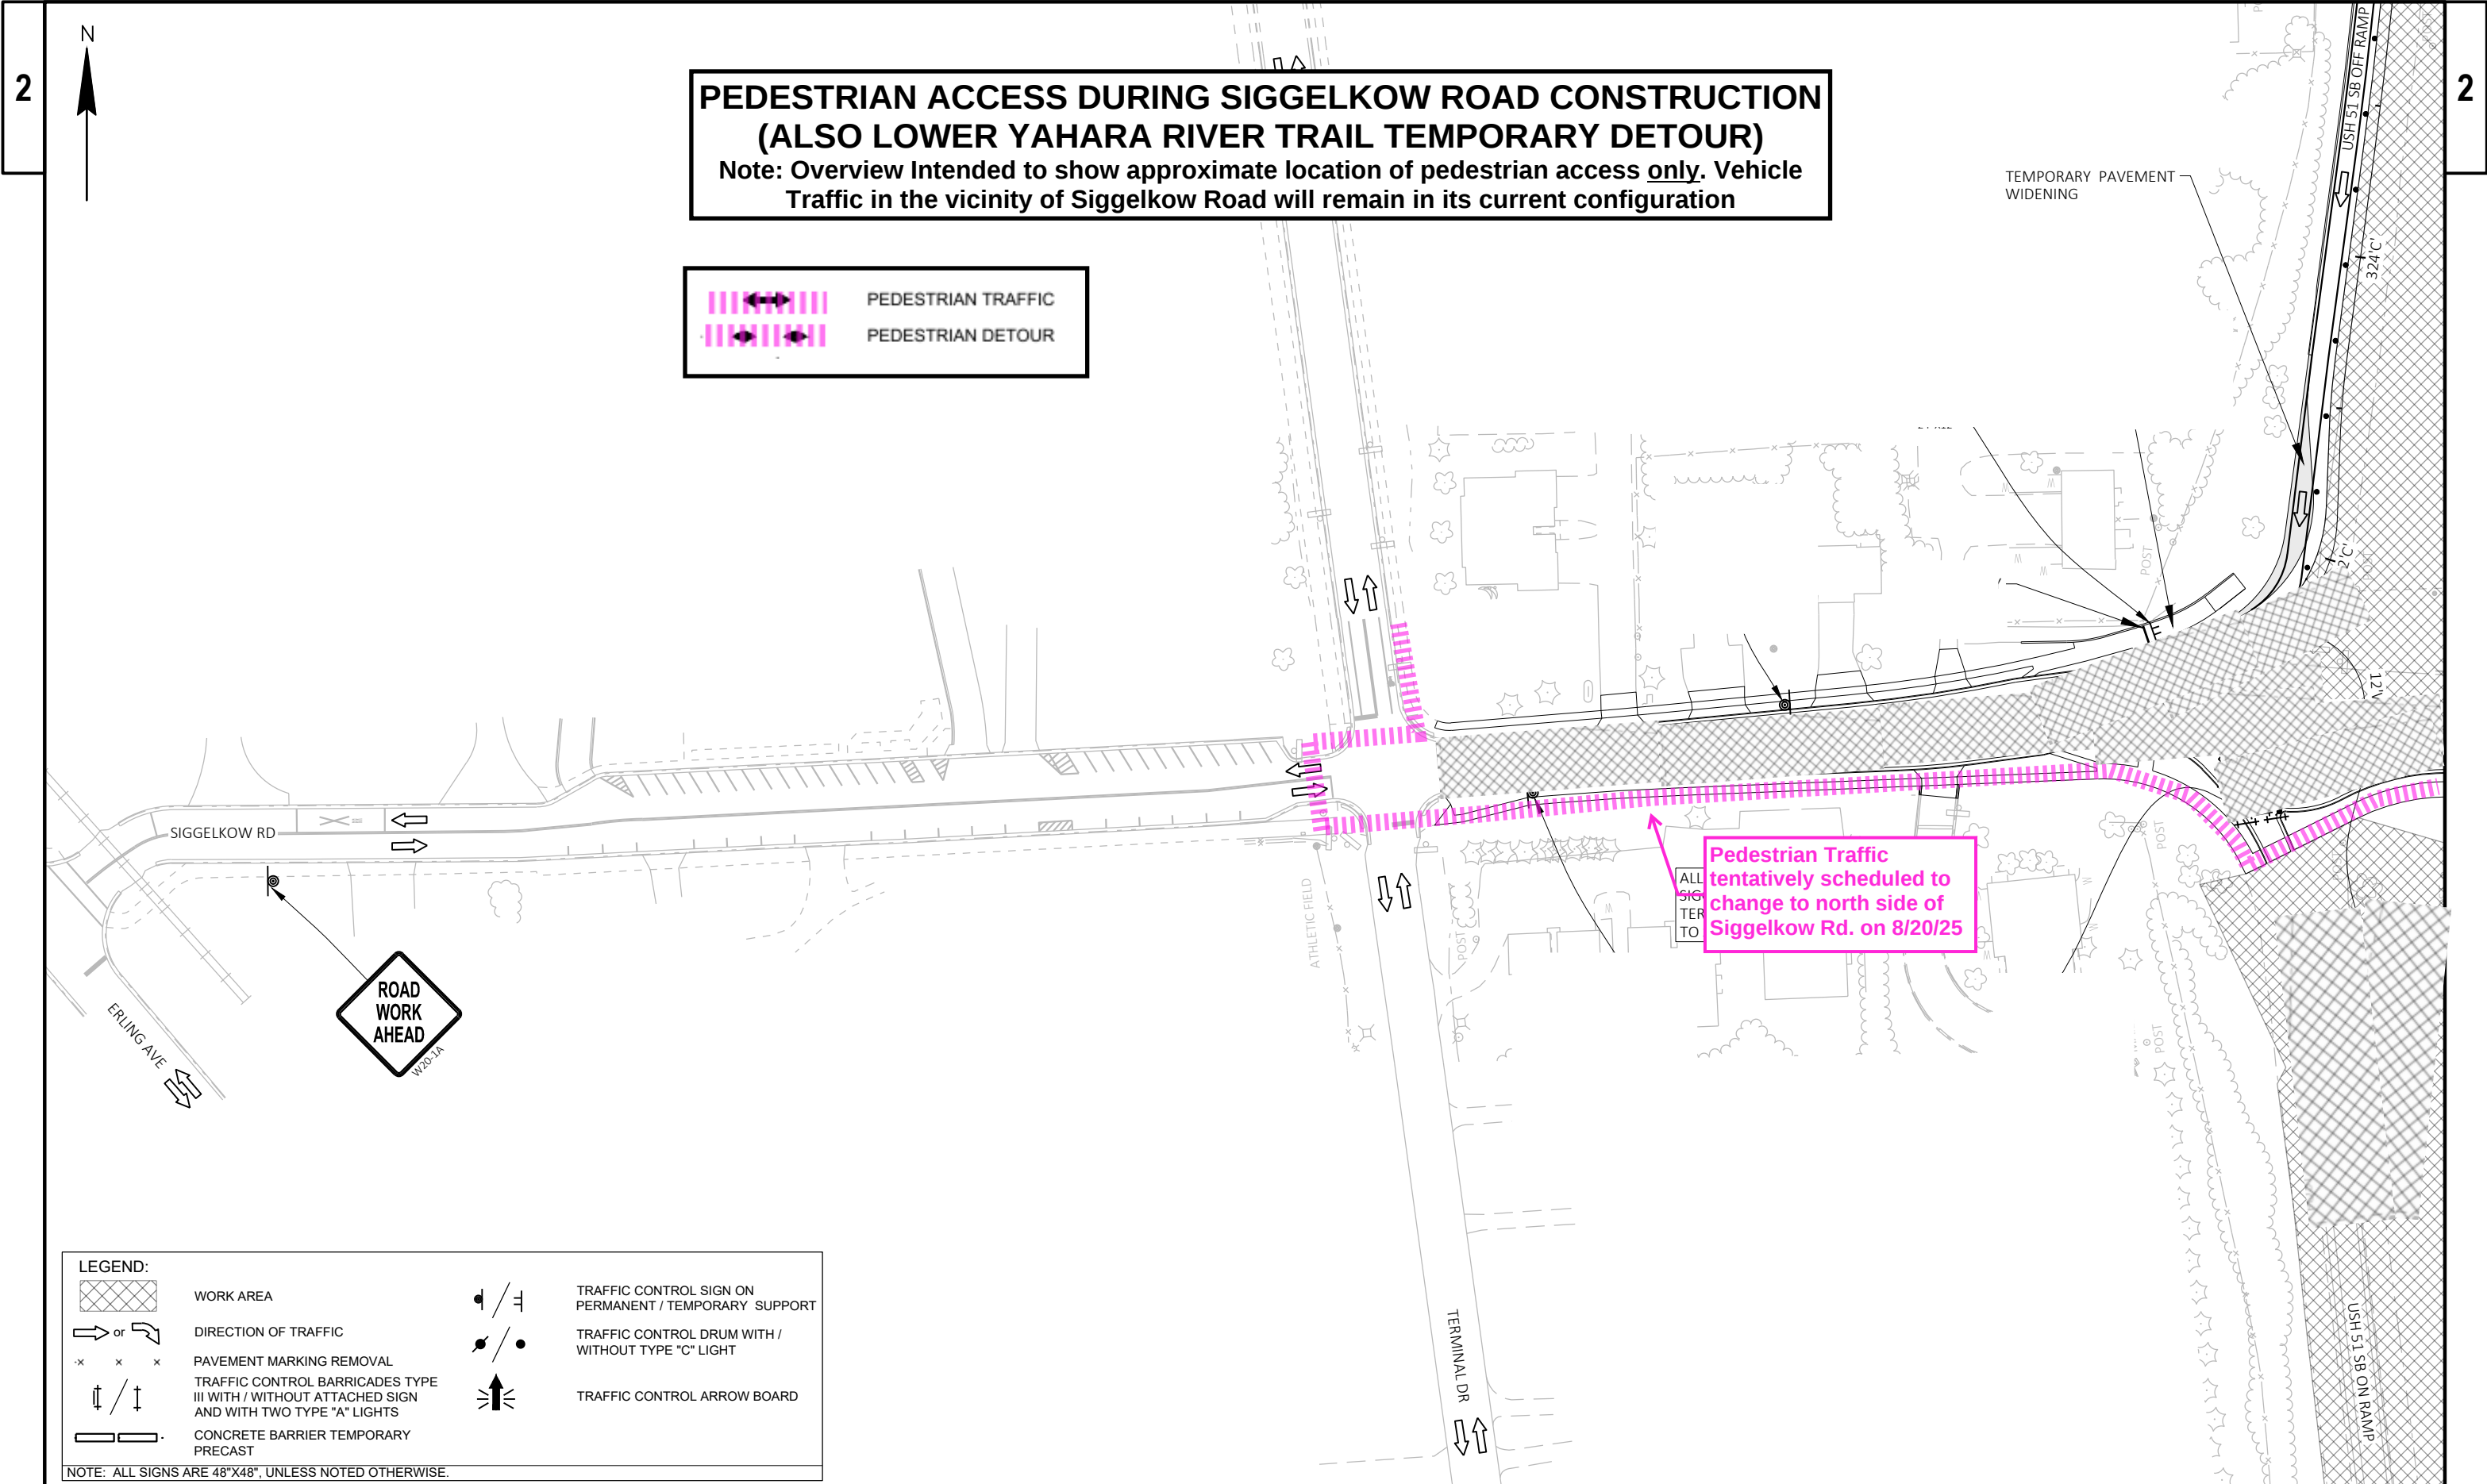


**PEDESTRIAN ACCESS DURING SIGGELKOW ROAD CONSTRUCTION
(ALSO LOWER YAHARA RIVER TRAIL TEMPORARY DETOUR)**
Note: Overview Intended to show approximate location of pedestrian access only. Vehicle Traffic in the vicinity of Siggelkow Road will remain in its current configuration

PEDESTRIAN TRAFFIC
PEDESTRIAN DETOUR

LEGEND:

	WORK AREA		TRAFFIC CONTROL SIGN ON PERMANENT / TEMPORARY SUPPORT
	DIRECTION OF TRAFFIC		TRAFFIC CONTROL DRUM WITH / WITHOUT TYPE "C" LIGHT
	PAVEMENT MARKING REMOVAL		TRAFFIC CONTROL ARROW BOARD
	TRAFFIC CONTROL BARRICADES TYPE III WITH / WITHOUT ATTACHED SIGN AND WITH TWO TYPE "A" LIGHTS		
	CONCRETE BARRIER TEMPORARY PRECAST		

NOTE: ALL SIGNS ARE 48"x48", UNLESS NOTED OTHERWISE.

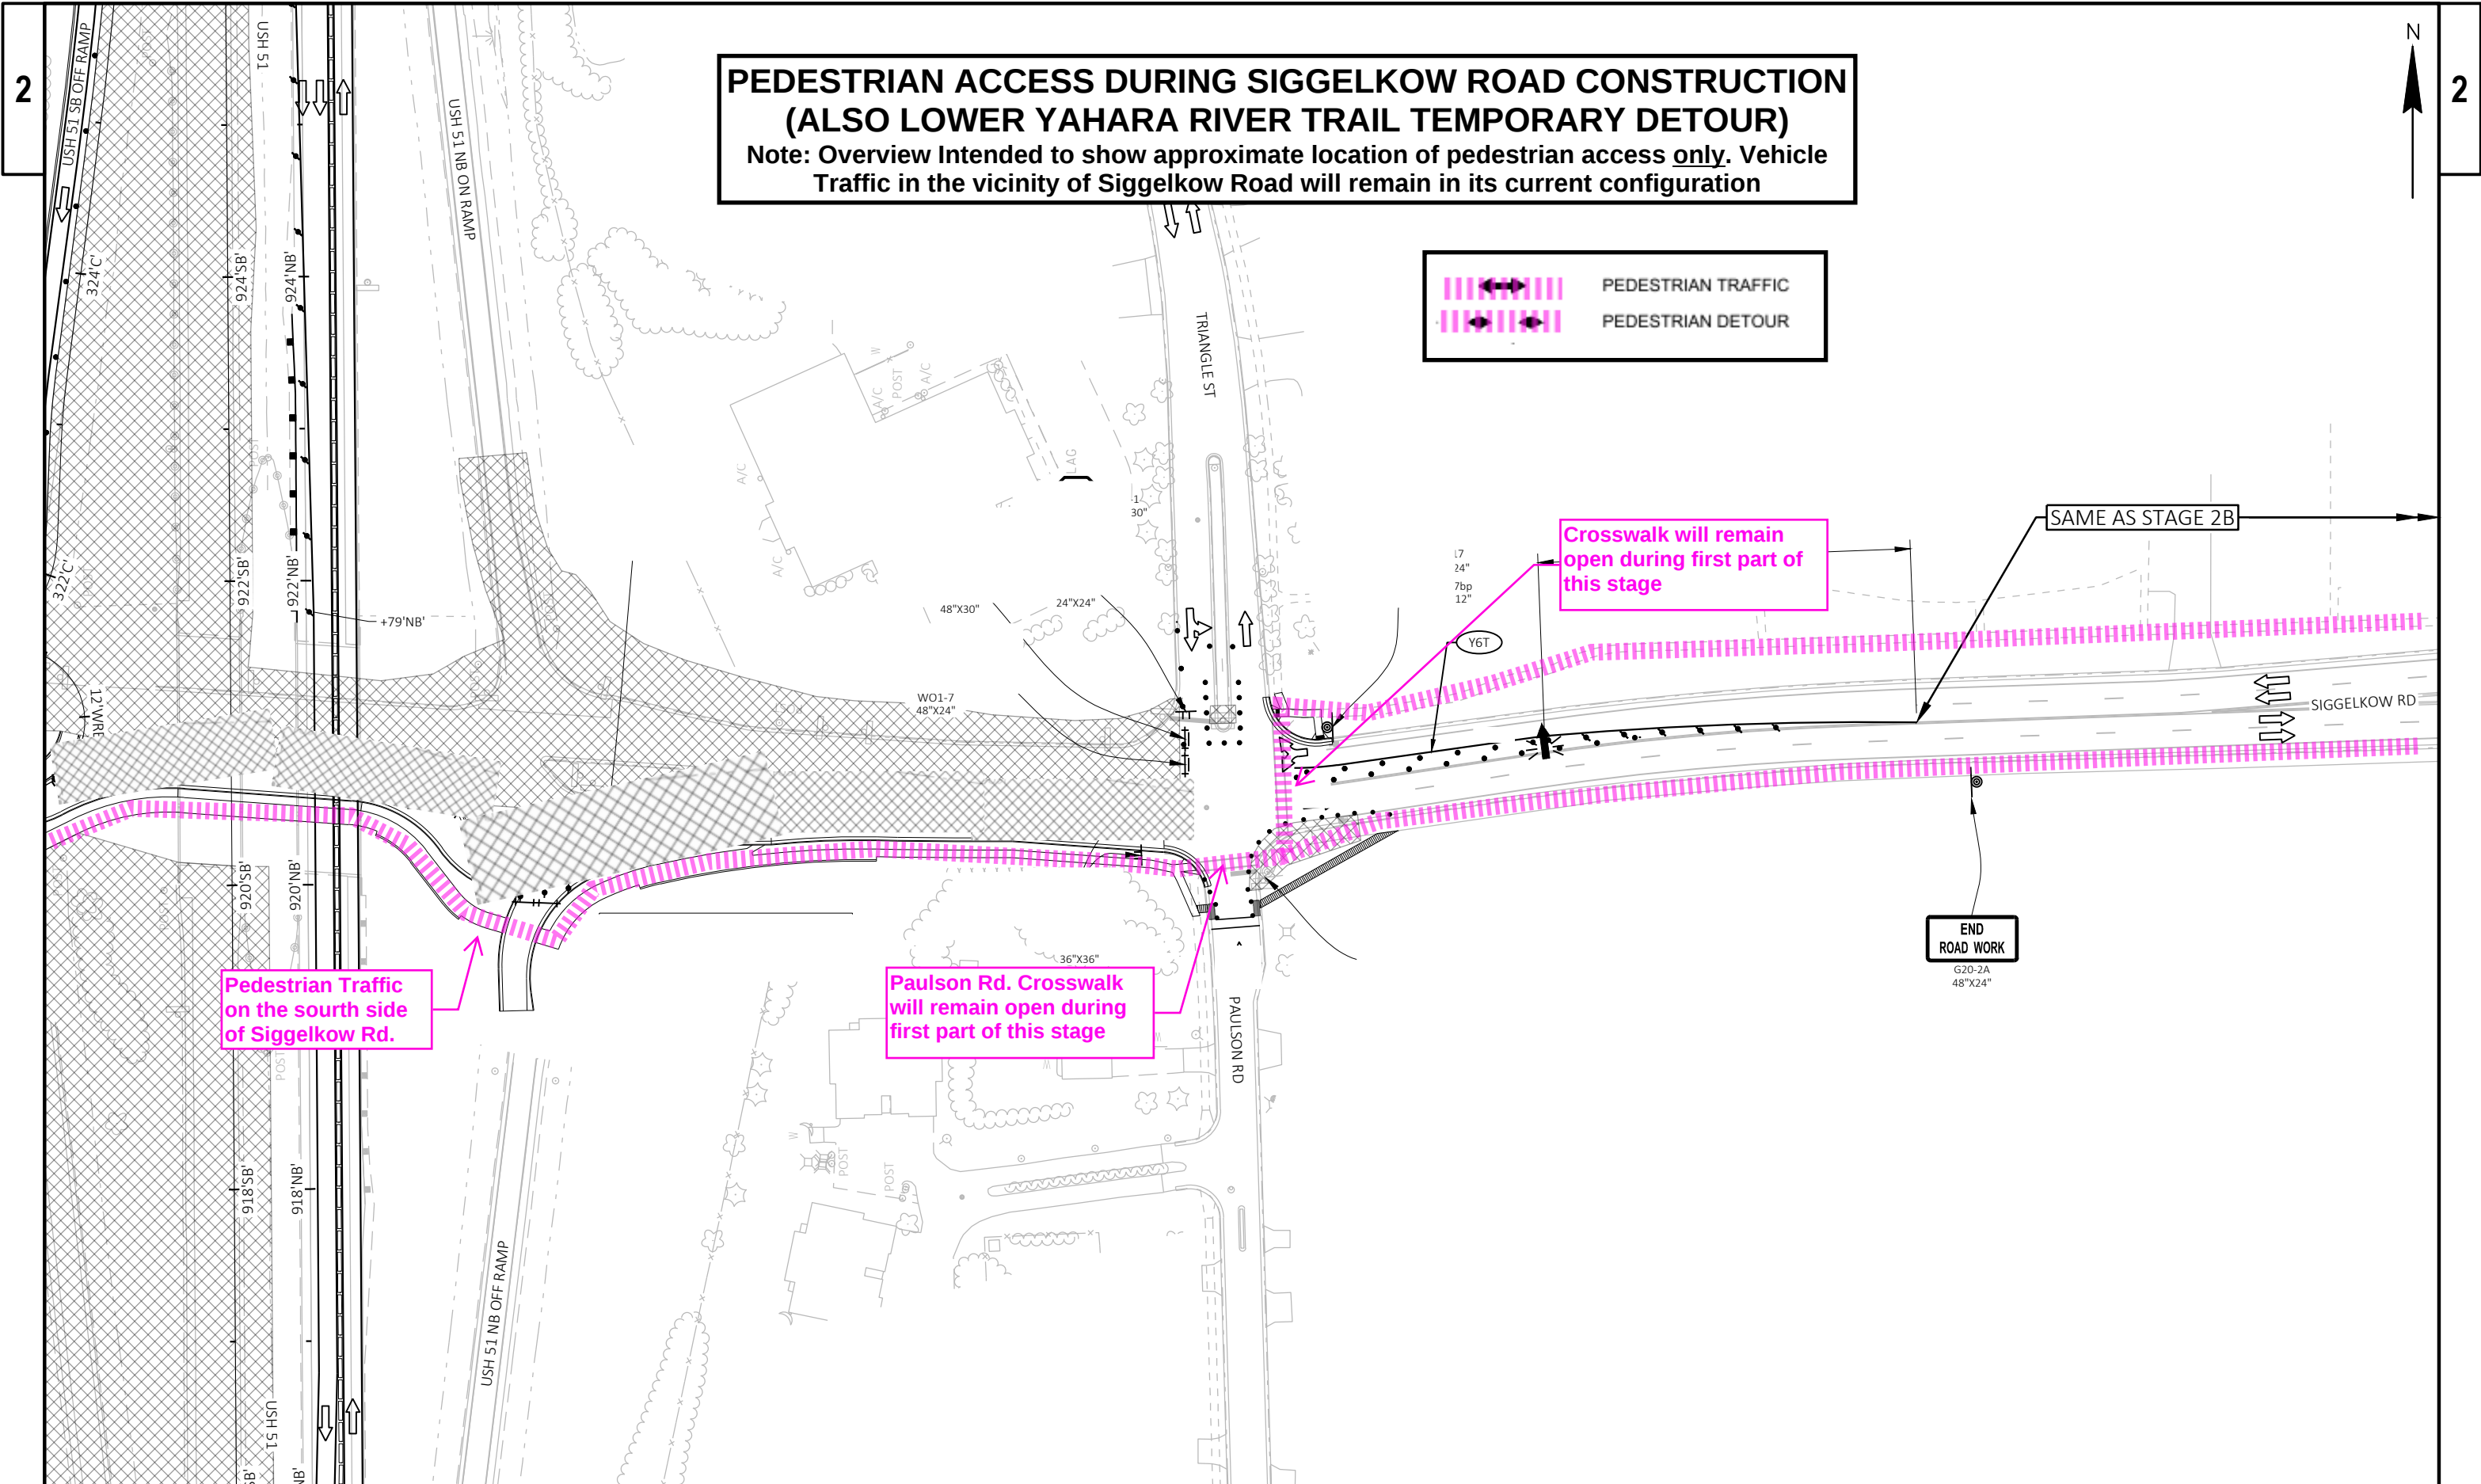

**PEDESTRIAN ACCESS DURING SIGGELKOW ROAD CONSTRUCTION
(ALSO LOWER YAHARA RIVER TRAIL TEMPORARY DETOUR)**
Note: Overview Intended to show approximate location of pedestrian access only. Vehicle Traffic in the vicinity of Siggelkow Road will remain in its current configuration

PEDESTRIAN TRAFFIC
PEDESTRIAN DETOUR

Pedestrian Traffic on the south side of Siggelkow Rd.


Paulson Rd. Crosswalk will remain open during first part of this stage

Crosswalk will remain open during first part of this stage


SAME AS STAGE 2B

END ROAD WORK
G20-2A
48"X24"

CURRENT

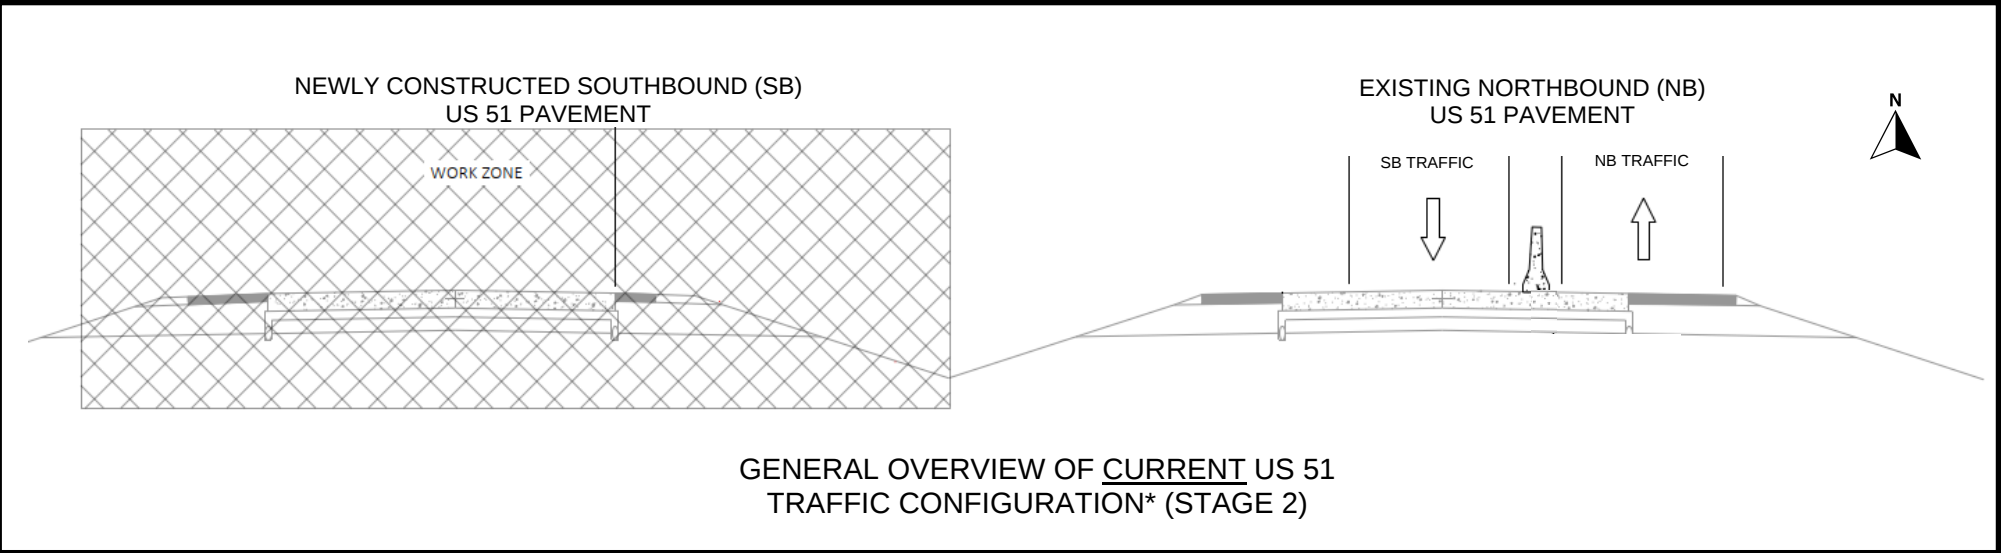

UPCOMING (ANTICIPATED 8/26/25)

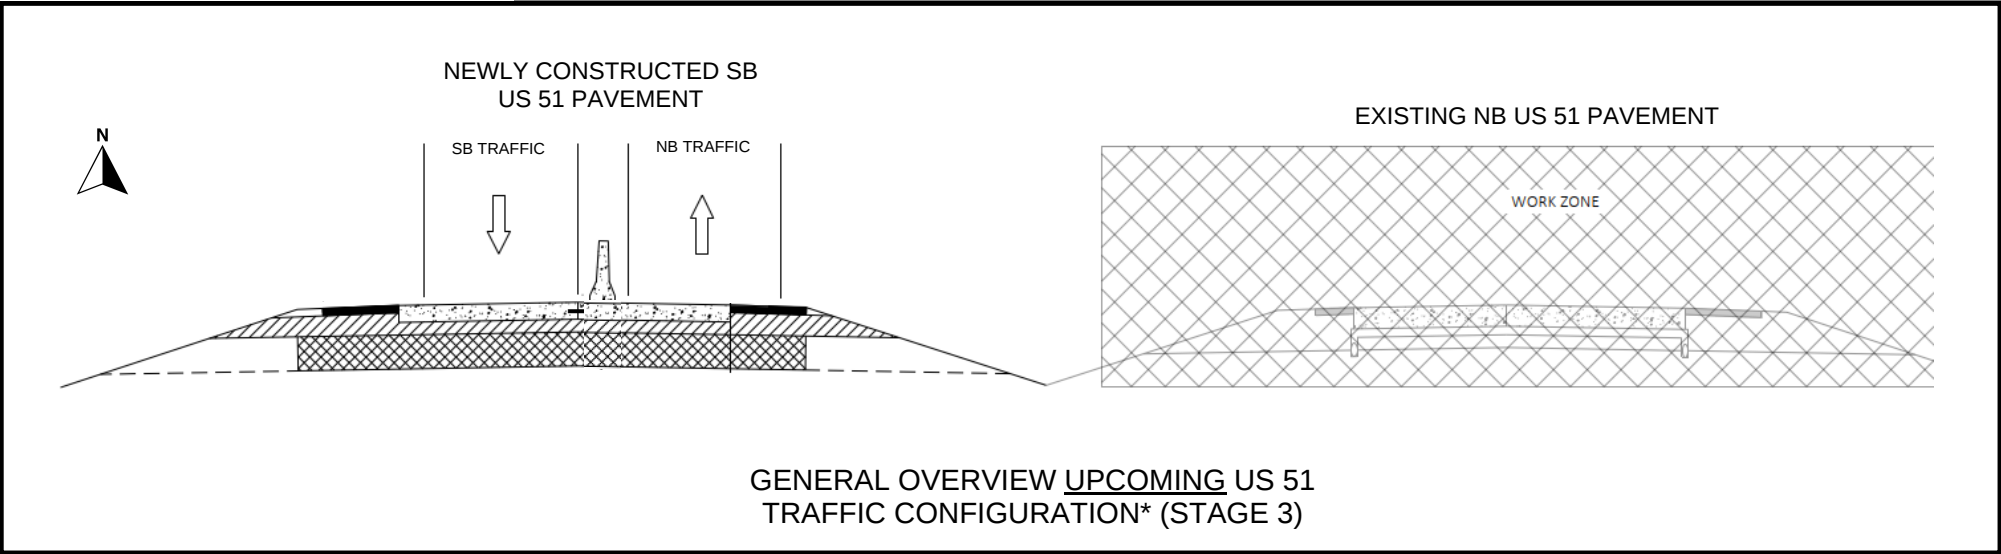

* TRAFFIC CONFIGURATIONS SHOWN ARE FOR GENERAL INFORMATION ONLY. FIELD CONDITIONS MAY VARY
