

CONSTRUCTION STAGING

STAGE 1 - 2019:

WORK TO OCCUR BETWEEN MADISON ST AND VETERANS LN WITH MADISON ST. REMAINING OPEN, BUT NARROWED. ALL WORK TO BE COMPLETED AT END OF STAGE.

STAGE 2 - 2019:

WORK TO OCCUR BETWEEN VETERANS LN AND LAKE PARK PL WITH LAKE PARK PLACE REMAINING OPEN BUT NARROWED. WORK IS RESTRICTED TO NOT BEGIN UNTIL AFTER STAGE 1 WATER AND SEWER WORK IS COMPLETE. ALL WORK TO BE COMPLETED AT END OF STAGE.

STAGE 3 - 2019:

WORK TO OCCUR BETWEEN LAKE PARK PL AND WOODLAND BEACH RD WITH LAKE PARK PLACE BEING CLOSED INTERMITTENTLY. WORK IS RESTRICTED TO NOT BEGIN UNTIL AFTER ALL OF STAGE 1 IS COMPLETE. ALL WORK TO BE COMPLETED AT END OF STAGE.

STAGE 4 - WINTER SUSPENSION PREP - 2019:

WORK TO OCCUR BETWEEN WOODLAND BEACH RD AND PINNACLE DR. SANITARY SEWER AND WATER WILL BE CONNECTED TO EXISTING SYSTEMS & STORM SEWER WILL BE EXTENDED TO THE NEAREST OUTFALL. TEMPORARY ASPHALT PAVEMENT WILL BE IN PLACE OVER WINTER AND ROADWAY WILL BE FULLY OPENED TO TRAFFIC AT END OF STAGE.

STAGE 4 - 2020:


WORK TO OCCUR BETWEEN WOODLAND BEACH RD AND SOUTHERN LIMITS. STH 89 CLOSED AGAIN AND DETOUR IN PLACE. ALL WORK TO BE COMPLETED AT END OF STAGE.

STAGE 1 - Madison St. to Veterans Ln.


STAGE 2 - Veterans Ln. to Lake Park Pl.

STAGE 3 - Lake Park Pl. to Woodland Beach Rd.

STAGE 4 - Woodland Beach Rd. to Southern Limits



DETOUR ROUTE

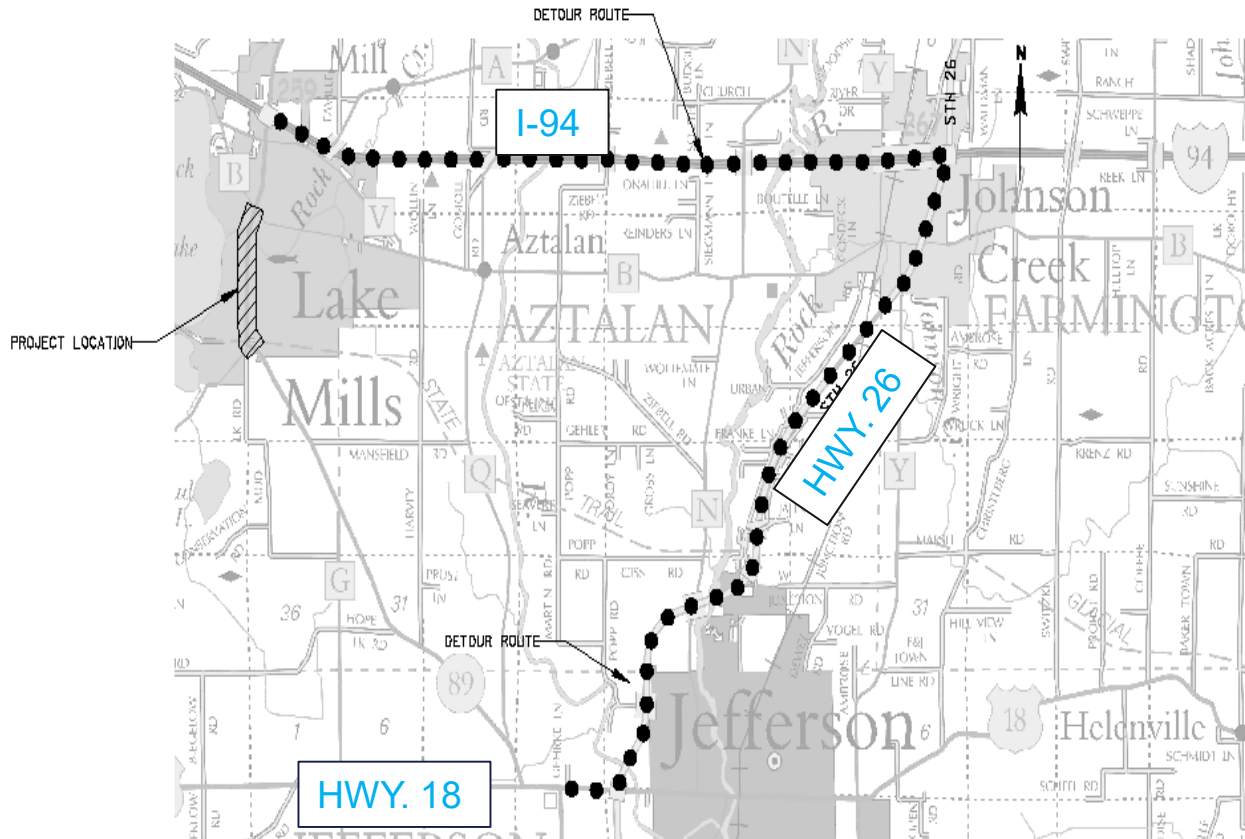

- ▶ State Signed Detour for Through Traffic & Trucks:
I 94 to WIS 26
to US 18
